

M.G.N.R.E.G.S

1. Date of inspection : 19-1-2017
2. Name of the village:- Darakhuna Garo
3. Name of the Block:- Resubelpara C&RD Block
4. Name of the scheme: Construction of B.N.R.G.S.K. building.
5. Amount sanctioned: - Rs. 14,43,650/-
6. Year of sanctioned: 2016-17
7. Date of commencement of the work: NA.
8. Date of completion:- Expected to be completed by March ,2017
9. Expenditure incurred:
  - (i) Wages: = Rs. 5,02,775/-
  - (ii) Cost of Materials : = Rs. 9,40,875/-
  - Total =Rs. 14,43,650/-
10. No. of Mandays:- 2975
11. Implementing Agency:- Resubelpara Development Block
9. Total length of the building: 57 Ft.
10. Width of the building:- 6.00 Meters
11. No of laboureres: 86 households
12. Status of the work: Construction works is in progress and only 40% Completed.
13. Quality of the work:- Good
14. Observations/Findings: The inspection team found that construction works of BNRGSK building is in progress.



BNRGSK building under construction




A Toilet under construction

## MGNREGS

1. Date of inspection :- 19-01-2017
2. Name of the village:- Rongpetchi
3. Name of the Block:- Resubelpara C&RD Block
4. Name of the scheme:- Construction of RCC Bridge
5. Amount sanctioned:- Rs. 20,10,334/-
6. Year of sanctioned:- 2015
7. Date of commencement of the work:- 8-04-2015
8. Date of completion: - October, 2015
9. Expenditure incurred:-
  - i) Wages: = Rs. 12,06,200/-
  - ii) Cost of Materials = Rs. 8,04,133/-
  - iii) Total =Rs. 20,10,333/-
10. No of labourers : 74 Households
10. No. of Mandays:- 7400
11. Implementing Agency:- Resubelpara Dev. Block
12. Total Length of RCC bridge:- 5.00 meters
13. Width of RCC bridge:- 4.20 meters
14. Status of the work:- Completed
15. Quality of the work:- Good
16. Observations/Findings:- The inspection team found that construction of RCC bridge is completed and the quality of the work is good.



RCC Bridge

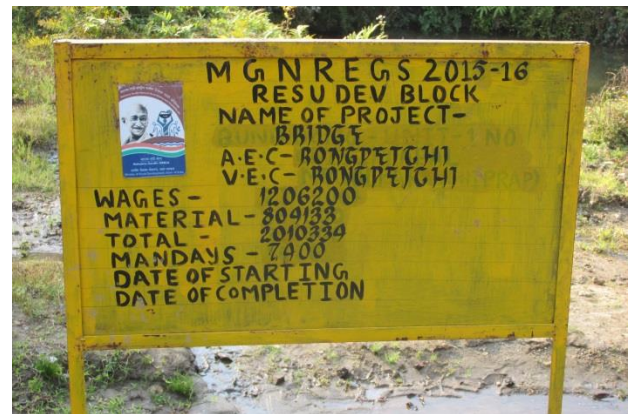

A Sign Board

M.G.N.R.E.G.S

1. Date of inspection : 19-1-2017
2. Team of inspecting officers :-  
Shri D.S Kharpan, Asstt. Director, Shri N. R Kharchandy, Research Officer, Shri M.C Khonglah, Research Asstt accompanied by Shri Rahul Medhi (APO), Shri Motjim Momin (Senior Gram Sevak), Shri Arsandro Sangma (Gram Sevak)
3. Village:- Rongpetchi
4. Name of the Block:- Resubelpara C&RD Block
5. Scheme:- Construction of CC Road at Rongpetchi
6. Amount sanctioned: Rs. 20,74,770/-
6. Year of sanctioned: 2016-17
7. Date of commencement of the work: August, 2016
8. Date of completion: Dec, 2016
9. Expenditure incurred:
  - i) Wages: = Rs. 11,88,070/-
  - ii) Cost of Materials :- =Rs. 8,86,700/-Total = =Rs. 20,74,770/-
10. No. of Mandays:- 7030
11. Implementing Agency:- Resubelpara Development Block
12. Total Length of the CC Road :- 600 meters
13. Width of the CC Road:- 10 Ft.
14. No. of laboureres :- 74 households
15. Status of the work: - Completed
16. Quality of the work:- Good
17. Observations/Findings: -The inspection team found the condition of the C.C.Road is good whereas no signboard has been fixed, hence the APO of the said Development Block was advised to fix a sign board at the starting point of the road



A C.C. Road



M.G.N.R.E.G.A

1. Date of inspection : 19-1-2017
2. Name of the village: Narongkol
3. Name of the Block: Resubelpara C&RD Block
4. Name of the scheme: Construction of motorable bridge at Narongkol
5. Scheme:- Ongoing
6. Amount sanctioned: Rs. 17,11,500/-
7. Year of sanctioned: 2015-16
8. Date of commencement of the work: August, 2016
9. Date of completion: Dec, 2016

10. Expenditure incurred:

- i) Wages: = Rs.10,26,900/-
- ii) Cost of Materials : Rs. 6,84,600/-
- iii) Total =Rs. 17,11,500/-

11. No. of Mandays: 7030
12. Implementing Agency: Resubelpara Development Block.
13. Total Length of motorable bridge: 6 meters
14. Width of the CC Road: 4 meters
15. No. of laboures: 66 households
16. Status of the work: Completed
17. Quality of the work: Good
18. Observations/Findings: The inspection team observed that Construction of motorable bridge at Narongkol is completed



A motorable bridge



A Sign Board
