


## MGNREGS

1. Scheme :- Construction of CC footpath
2. Date of inspection :- 29-11-2017
3. Name of Inspecting Officers: Shri M. C Khonglah, Asstt Research Officer, Shri B.R Marak, Asstt Research Officer, accompanied by Shri Tengsang A Sangma, APO, H.N Sangma,JE, Kalseng R Marak, GS
4. Village:- Samanda Megapgre
5. Block:- Samanda C&RD Block
6. Scheme :- Construction of CC footpath
7. Amount sanctioned :- Rs.12.12 lakhs
8. Year of sanctioned :- 2015-16
9. Date of commencement of the work:- 29-9-2016
10. Date of completion :- Completed
11. Expenditure incurred :-
  - i. Wages :- = Rs. 7.0416 lakhs
  - ii. Cost of materials: = Rs. 5.0787 lakhsTotal = Rs. 12.12 lakhs
12. No. of labourers :- 96 (Ninety six)
13. No. of Mandays:- 4320
14. Implementing agency: Samanda C&RD Block
15. Total Length of the Footpath:- 465 meters
16. Width of the Footpath:- 1.53 meters
17. Status of the work :- Completed
18. Quality of the work :- Good
19. Observation/findings:- It was observed that construction of CC footpath is completed and the quality of work is good.



CC Footpath

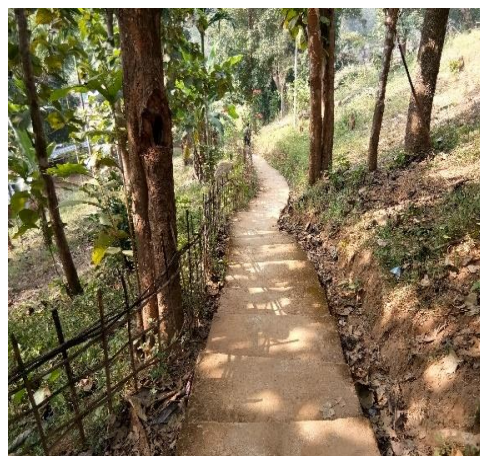

CC Footpath

## MGNREGS

1. Scheme :- Construction of CC footpath
2. Date of inspection :- 29-11-2017
3. Village:- Samanda Megapgre
4. Block:- Samanda C&RD Block
5. Amount sanctioned :- Rs.21.36 lakhs
6. Year of sanctioned :- 2016-17
7. Date of commencement of the work:- 22-9-2015
8. Date of completion :- Completed
9. Expenditure incurred :-
  - i. Wages :- = Rs. 13.4355 lakhs
  - ii. Cost of materials: =Rs. 7.9285 lakhsTotal = Rs. 21.36 lakhs
10. No. of labourers :- 96 (Ninety six)
11. No. of Mandays:- 7950
12. Implementing agency: Samanda C&RD Block
13. Total Length of the Footpath:- 950 meters
14. Width of the Footpath:- 1.5 meters
15. Status of the work :- Completed
16. Quality of the work :- Good
17. Observation/findings:- It was observed that construction of CC footpath is completed with good workmanship.



CC footpath



## MGNREGS

1. Scheme :- Construction of a Suspension Foot Bridge
2. Date of inspection :- 29-11-2017
3. Village:- Nokgilawe
4. Block:- Samanda C&RD Block
5. Amount sanctioned :- Rs.21.36 lakhs
6. Year of sanctioned :- 2012,2013 & 2015
7. Date of commencement of the work:-12-03-2012
8. Date of completion :- Completed
9. Expenditure incurred :-
  - i. Wages :- = Rs. 71,88,825 lakhs
  - ii. Cost of materials: = Rs. 51,79,460 lakhsTotal = Rs. 1,23,68,285 lakhs
10. No. of labourers :- NA
11. No. of Mandays:- 52,233
12. Implementing agency: Samanda C&RD Block
13. Total length of a Suspension Foot Bridge :-140 mts.
14. Width of the foot bridge:-1.5 meters
15. Status of the work :- Completed
16. Quality of the work :- Good
17. Observation/findings:- It was observed that construction of a suspension foot bridge is completed and the quality of work is good.



A suspension Foot Bridge



A sign board
