

## FENCING OF PLAYGROUND AT TLUH



<b>Date of Inspection:</b>	01 <sup>st</sup> July 2016
<b>Team of inspection officers:</b>	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior
<b>Accompanied by:</b>	Shri M.D. Laloo, Assistant Engineer and Shri C. Sutnga, Gram Sevak.
<b>Name of the Scheme:</b>	Fencing of playground at Tluh.
<b>Name of the MP:</b>	Shri V.H. Pala MP(LS)
<b>Year recommended/sanctioned:</b>	2013-2014
<b>Amount &amp; Date of sanctioned by the DC:</b>	Rs.5,00,000/- sanctioned on 14 <sup>th</sup> January 2014
<b>Reason for delay of sanction, if any:</b>	Nil
<b>Date of release of fund:</b> <b>1<sup>st</sup> instalment :-</b> <b>2<sup>nd</sup> instalment :-</b>	Released from Block Office on 09 <sup>th</sup> July 2014. Released from Block Office on 15 <sup>th</sup> April 2015.
<b>Reason for delay in release of fund, if any:</b>	Nil
<b>Amount utilized:</b>	Rs. 5,00,000/-
<b>Date of commencement/starting of the work:</b>	10 <sup>th</sup> July 2014
<b>Date of completion/Expected date of completion:</b>	05 <sup>th</sup> May 2015
<b>Status of the work:</b>	Completed
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.
<b>Name of executing agency:</b>	Local Village Committee
<b>Whether signboard erected or not:</b>	No
<b>Date of submission of UC:</b> <b>1<sup>st</sup> Instalment:</b> <b>2<sup>nd</sup> Instalment:</b>	Submitted to BDO, Saipung C & RD Block on 02 <sup>nd</sup> February 2015 Not yet submitted.
<b>In case of completed Scheme whether the completion Report/ Certificate submitted to BDO/DC:</b>	Yes
<b>Impact of the scheme:</b>	To prevent the encroachment of animals inside the playground and also to demarcate the boundary of the school compound.
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>1. The construction of fencing is well done with usage of good quality materials and good workmanship.</li> <li>2. On inspection the team found that the fencing is completed. It was constructed with brick wall and grills painted with colour distemper. Its length (200m approx) and height (1.5m) and Steel gate with length (2.8) and height (1.8).</li> <li>3. The local village committee was advised to erect a plaque with complete details.</li> <li>4. It was informed that the fencing was for the school, but due to the construction of the church on this playground, so the playground for school students was shifted to a new area.</li> <li>5. It was informed that ₹20.00 lakhs was contributed by the Local Village Committee for the completion of the work.</li> </ol>
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

**CONSTRUCTION OF MULTIPURPOSE INDOOR SPORTS AND CULTURAL COMPLEX AT LATYRKE**



<b>Date of Inspection:</b>	01 <sup>st</sup> July 2016
<b>Team of inspection officers:</b>	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
<b>Accompanied by:</b>	Shri M.D. Laloo, Assistant Engineer and Shri C. Sutnga, Gram Sevak.
<b>Name of the Scheme:</b>	Construction of multipurpose indoor sports and cultural complex at Latyrke.
<b>Name of the MP:</b>	Smt. W. Syiem MP(RS)
<b>Year recommended/sanctioned:</b>	2013-14
<b>Amount &amp; Date of sanctioned by the DC:</b>	Rs. 25,00,000/- sanctioned on 10 <sup>th</sup> February 2014.
<b>Reason for delay in sanction, if any:</b>	Nil
<b>Date of release of fund:</b>	
<b>1<sup>st</sup> instalment :-</b>	Released from Block Office on 23 <sup>rd</sup> July 2014.
<b>2<sup>nd</sup> instalment :-</b>	Released from Block Office on 14 <sup>th</sup> October 2014.
<b>Reason for delay in release of fund, if any:</b>	Nil
<b>Amount utilized:</b>	Rs. 25,00,000/-
<b>Date of commencement/starting of the work:</b>	04 <sup>th</sup> April 2014.
<b>Date of completion/Expected date of completion:</b>	25 <sup>th</sup> September 2015
<b>Status of the work:</b>	Completed.
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.
<b>Name of executing agency:</b>	Local Village Committee
<b>Whether signboard erected or not:</b>	Yes
<b>Date of submission of UC:</b>	
<b>1<sup>st</sup> Instalment:</b>	Submitted to BDO, Saipung C & RD Block on 11 <sup>th</sup> September 2014.
<b>2<sup>nd</sup> Instalment:</b>	
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	Yes
<b>Impact of the scheme:</b>	For Cultural Festivals, Indoor Sports, Village Dorbar Meetings, etc.
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>On inspection the team found that the construction of a building was completed. It is a 4 storey building (G+3). The scheme from MPLADS was constructed on the top floor and it will be utilised as a Conference Hall. This building was built in convergence with ICDP (Integrated Cooperative Development Project) of ₹3,00,000 (2008-09) and Chief Minister's Rural Development fund (CMSRDF) of ₹40,00,000 (2013-14).</li> <li>The Hall was constructed with truss and covered with Dyna roof. It was attached with bathroom, toilet, wash basin and with a false ceiling. The electrical work has also been completed. Both exterior and interior was painted with high gloss paint and there are 10 nos of windows (steel casement) and 2 nos of flush door. The dimension of Hall is (L=17.75m and B=11.2m), windows (L=2.2m and B=1.7m), door 1 (B=0.95m and H=2.05m) and door 2 (B=1.6m and H=2.05m). Door 1 chowkat: L=5.2m, B=100mm and Thickness =70mm. Door 2 chowkat: L=5.85m, B=100mm and Thickness=70mm. Terrace Railing (L=47.5m), Brick wall (H=0.5m), grill (L=47.5m and H=0.5m), RCC Rain gutter: L=47.5m, B=0.25m and H=0.2m.</li> <li>It was informed that the Local Village Committee contributed ₹15.00 lakhs for the completion of the scheme. The members of the Local Village Committee were advised to erect a plaque with complete details.</li> </ol>
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-


**CONSTRUCTION OF COMMUNITY HALL AT MOOLAMYLLIANG VILLAGE.**



<b>Date of Inspection</b>	01 <sup>st</sup> July 2016
<b>Team of inspection officers</b>	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
<b>Accompanied by</b>	Shri M.D. Laloo, Assistant Engineer and Shri C. Sutnga, Gram Sevak
<b>Name of the Scheme:</b>	Construction of Community Hall at Moolamyliang Village.
<b>Name of the MP:</b>	Shri V.H. Pala MP(LS)
<b>Year recommended/sanctioned:</b>	2013-2014
<b>Amount &amp; Date of sanctioned by the DC:</b>	Rs. 2,00,000/- sanctioned on 6 <sup>th</sup> June 2014
<b>Reason for delay in sanction, if any:</b>	Nil
<b>Date of release of fund:</b> <b>1<sup>st</sup> instalment :-</b> <b>2<sup>nd</sup> instalment :-</b>	Released from Block Office on 14 <sup>th</sup> October 2014. Released from Block Office on 15 <sup>th</sup> April 2015.
<b>Reason for delay in release of fund, if any:</b>	Nil
<b>Amount utilized:</b>	Rs. 2,00,000/-
<b>Date of commencement/starting of the work:</b>	14 <sup>th</sup> October 2014.
<b>Date of completion/Expected date of completion:</b>	Work in progress
<b>Status of the work:</b>	Work in progress
<b>Cause/Reason for delay in sanction/completion of works:</b>	Due to insufficient funds.
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.
<b>Name of executing agency:</b>	The work is executed by the Village Committee.
<b>Whether signboard erected or not:</b>	No
<b>Date of submission of UC:</b> <b>1<sup>st</sup> Instalment:</b> <b>2<sup>nd</sup> Instalment:</b>	Submitted to BDO, Saipung C&RD Block on 21 <sup>st</sup> January 2015
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	Yes
<b>Impact of the scheme:</b>	Used for the purpose of Village Dorbar Meeting, Office, etc.
<b>Findings/Observations:</b>	1. On inspection it was found that the construction of the Community Hall was completed only upto plinth level and It was informed that due to insufficient funds the building cannot be completed. 2. The members of the Local Village Committee were advised to come up with funds of their own for completion of the scheme since it has taken almost 2 years.
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-



**LEVELLING OF PLAYGROUND AT LAMYRSIANG SOCIAL CULTURAL BLOCK**

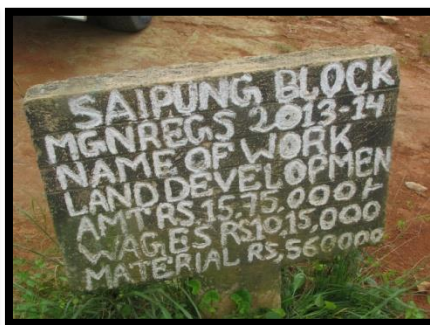


<b>Date of Inspection</b>	01 <sup>st</sup> July 2016
<b>Team of inspection officers</b>	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
<b>Accompanied by</b>	Shri M.D. Laloo, Assistant Engineer and Shri C. Sutnga, Gram Sevak.
<b>Name of the Scheme:</b>	Levelling of Playground at Lamyrsiang Social Cultural Block.
<b>Name of the MP:</b>	Smt. W. Syiem MP(RS)
<b>Year recommended/sanctioned:</b>	2014-2015
<b>Amount &amp; Date of sanctioned by the DC:</b>	Rs. 20,00,000/- sanctioned on 10 <sup>th</sup> March 2015.
<b>Reason for delay in sanction, if any:</b>	Nil
<b>Date of release of fund:</b>	
<b>1<sup>st</sup> instalment :-</b>	Released from Block Office on 9 <sup>th</sup> June 2015.
<b>2<sup>nd</sup> instalment :-</b>	Not yet released
<b>Reason for delay in release of fund, if any:</b>	Nil
<b>Amount utilized:</b>	Rs. 20,00,000/-
<b>Date of commencement/starting of the work:</b>	02 <sup>nd</sup> June 2015.
<b>Date of completion/Expected date of completion:</b>	Work in progress
<b>Status of the work:</b>	Work under progress.
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.
<b>Name of executing agency:</b>	Sports Managing Committee.
<b>Whether signboard erected or not:</b>	No
<b>Date of submission of UC:</b>	
<b>1<sup>st</sup> Instalment:</b>	Not yet submitted.
<b>2<sup>nd</sup> Instalment:</b>	-----
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	Yes
<b>Impact of the Scheme:</b>	To be used for Football, Sports, etc.by the local people
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>1. On inspection the team found that the levelling of the playground is in progress.</li> <li>2. It was informed that the work was converged with MGNREGA(2013-14) ₹15.75/- lakhs.</li> <li>3. It was found that though there was convergence of schemes and the amount was almost Rs 35.75 lakhs, the physical work done was very less since there is no side drain, gallery cum retaining wall which is required in a playground. The AE was advised to inform the Sports Managing Committee to submit the UC and Photographs to the office of the BDO and also take follow-up-action to complete the playground with the above mentioned requirements.</li> </ol>
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

**CONSTRUCTION OF SCHOOL BUILDING AT SEIN RAIJ SCHOOL, JALAPHET**



<b>Date of Inspection</b>	01 <sup>st</sup> July 2016
<b>Team of inspection officers</b>	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
<b>Accompanied by</b>	Shri M.D. Laloo, Assistant Engineer and Shri C. Sutnga, Gram Sevak.
<b>Name of the Scheme:</b>	Construction of School building at Sein Raij School, Jalaphet.
<b>Name of the MP:</b>	Smt. W. Syiem MP(RS)
<b>Year recommended/sanctioned:</b>	2014-2015
<b>Amount &amp; Date of sanctioned by the DC:</b>	Rs. 10,00,000/- sanctioned on 28 <sup>th</sup> December 2015.
<b>Reason for delay in sanction, if any:</b>	Nil
<b>Date of release of fund:</b> 1 <sup>st</sup> instalment :- 2 <sup>nd</sup> instalment :-	Released from Block Office on 18 <sup>th</sup> February 2016
<b>Reason for delay in release of fund, if any:</b>	Nil
<b>Amount utilized:</b>	Rs. 10,00,000/-
<b>Date of commencement/starting of the work:</b>	23 <sup>rd</sup> February 2016
<b>Date of completion/Expected date of completion:</b>	Work in progress
<b>Status of the work:</b>	Work under progress.
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.
<b>Name of executing agency:</b>	School Managing Committee
<b>Whether signboard erected or not:</b>	No
<b>Date of submission of UC:</b> 1 <sup>st</sup> Instalment: 2 <sup>nd</sup> Instalment:	Submitted to BDO, Saipung C&RD Block on 15 <sup>th</sup> June 2016. -----
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	Yes
<b>Impact of the Scheme:</b>	To be used as classrooms & School office.
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>1. On inspection the team found that the structural work is completed, whereas the flooring, walling, plastering is yet to be started.</li> <li>2. It was informed that ₹10.00 Lakh was contributed by School Managing Committee towards construction of the scheme</li> <li>3. The School Managing Committee was advised to erect the plaque with complete details after completion of the scheme.</li> </ol>
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

**CONSTRUCTION OF COMMUNITY HALL AT MOOKNOR VILLAGE**

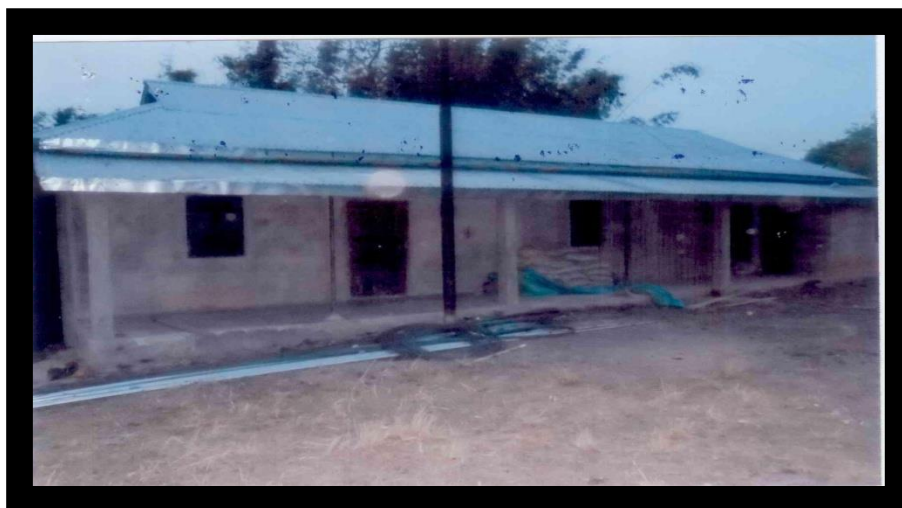

<b>Date of Inspection</b>	01 <sup>st</sup> July 2016
<b>Team of inspection officers</b>	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
<b>Accompanied by</b>	Shri M.D. Laloo, Assistant Engineer and Shri C. Sutnga, Gram Sevak.
<b>Name of the Scheme:</b>	Construction of Community Hall at Mooknor Village.
<b>Name of the MP:</b>	Shri V.H.Pala MP(LS)
<b>Year recommended/sanctioned:</b>	2013-2014
<b>Amount &amp; Date of sanctioned by the DC:</b>	Rs. 2,00,000/- sanctioned on 14 <sup>th</sup> January 2014.
<b>Reason for delay in sanction, if any:</b>	Nil
<b>Date of release of fund:</b> <b>1<sup>st</sup> instalment :-</b> <b>2<sup>nd</sup> instalment :-</b>	Released from Block Office on 4 <sup>th</sup> June 2014 Released from Block Office on 16 <sup>th</sup> March 2016.
<b>Reason for delay in release of fund, if any:</b>	Improper function of the Village Committee.
<b>Amount utilized:</b>	Rs. 2,00,000/-
<b>Date of commencement/starting of the work:</b>	01 <sup>st</sup> July 2014.
<b>Date of completion/Expected date of completion:</b>	11 <sup>th</sup> February 2016.
<b>Status of the work:</b>	Completed
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.
<b>Name of executing agency:</b>	Village Committee
<b>Whether signboard erected or not:</b>	No
<b>Date of submission of UC:</b> <b>1<sup>st</sup> Instalment:</b> <b>2<sup>nd</sup> Instalment:</b>	Submitted to BDO, Saipung C&RD Block on 05 <sup>th</sup> March 2015 Not yet submitted
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	Yes
<b>Impact of the Scheme:</b>	Used for the purpose of Committee Meeting, Village Dorbar Meeting, Office, etc.
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>1. On inspection it was found that the construction is complete. It was constructed with usage of good materials and good workmanship.</li> <li>2. The building is constructed with wooden roof truss covered with CGI sheet.</li> <li>3. The Assistant Engineer, Saipung Block was advised to inform the members of the Village Committee to erect a plaque with all details.</li> </ol>
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

**CONSTRUCTION OF FOOTBALL GROUND AT KHAHNAR VILLAGE**



<b>Date of Inspection</b>	01 <sup>st</sup> July 2016
<b>Team of inspection officers</b>	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
<b>Accompanied by</b>	Shri M.D. Laloo, Assistant Engineer and Shri C. Sutnga, Gram Sevak.
<b>Name of the Scheme:</b>	Construction of Football Ground at Khahnar Village.
<b>Name of the MP:</b>	Shri V.H.Pala MP(LS)
<b>Year recommended/sanctioned:</b>	2013-2014
<b>Amount &amp; Date of sanctioned by the DC:</b>	Rs. 3,00,000/- sanctioned on 14 <sup>th</sup> January 2014
<b>Reason for delay in sanction, if any:</b>	Nil
<b>Date of release of fund:</b> <b>1<sup>st</sup> instalment :-</b> <b>2<sup>nd</sup> instalment :-</b>	Released from Block Office on 27 <sup>th</sup> May 2014. Released from Block Office on 30 <sup>th</sup> March 2015
<b>Reason for delay in release of fund, if any:</b>	Nil
<b>Amount utilized:</b>	Rs. 3,00,000/-
<b>Date of commencement/starting of the work:</b>	30 <sup>th</sup> May 2014
<b>Date of completion/Expected date of completion:</b>	15 <sup>th</sup> April 2015
<b>Status of the work:</b>	Completed
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.
<b>Name of executing agency:</b>	The work is executed by the Village Committee
<b>Whether signboard erected or not:</b>	Yes
<b>Date of submission of UC:</b> <b>1<sup>st</sup> Instalment:</b> <b>2<sup>nd</sup> Instalment:</b>	Submitted to BDO, Saipung C&RD Block on 28 <sup>th</sup> January 2015. Not yet submitted
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	Yes
<b>Impact of the Scheme:</b>	Used for the purpose of sports,football competition, etc.
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>1. The inspection team found that the construction of the football ground is completed.</li> <li>2. Its dimension: Length= 100m Breadth=95m</li> <li>3. The Assistant Engineer, Saipung Block was advised to inform the Village Committee to erect a plaque with complete details.</li> </ol>
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
