



CONSTRUCTION OF COMMUNITY HALL AT KHLIEHRIAT WEST VILLAGE



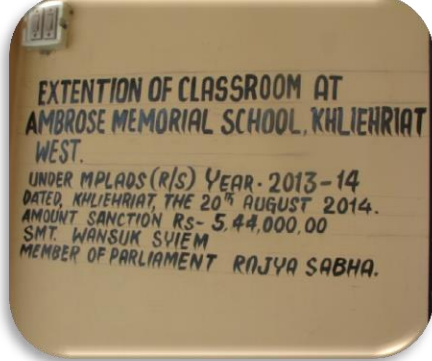


Date of Inspection:	16.06.2016
Team of inspection officers:	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Construction of Community Hall at Khliehriat West Village
Name of the MP:	Shri V.H. Pala MP(LS)
Year recommended/sanctioned:	2014
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/- Sanctioned on 14 th January 2014
Reason for delay of sanction, if any:	Nil
Date of release of fund:	
1st instalment :-	Rs. 2,50,000/- released from Block Office on 30 th June 2014.
2nd instalment :-	Rs. 2,50,000/- released from Block Office on 10 th August 2015.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	20 th May 2014.
Date of completion/Expected date of completion:	31 st May 2015
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Local Committee, Khliehriat West Village.
Whether signboard erected or not:	No
Date of submission of UC:	
1st Instalment:	Utilisation Certificate of 1 st instalment has been submitted to BDO,Khliehriat C &RD Block on 18 th Nov 2014 and
2nd Instalment:	Utilisation Certificate of 2 nd instalment has been submitted to BDO,Khliehriat C &RD Block on 20 th August 2015
In case of completed Scheme whether the completion Report/ Certificate submitted to BDO/DC:	Yes
Impact of the scheme:	Availability of Community Hall will benefit the local people for their various needs like public awareness programmes ,Dorbar, awards ceremonies, dramatics plays, concerts performance, dance competition. etc.
Findings/Observations:	<ol style="list-style-type: none"> 1. On observation it was found that the building constructed is sound and strong as good quality materials were used along with good workmanship. There are no visible defects such as cracks, water seepage, etc. It is also well maintained. 2 The Local Committee contributed Rs 15,00,000/- towards construction of the Community Hall . 3.The members of the Local Committee were advised to erect a plaque with complete details as specified in the Guidelines.
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

EXTENSION OF CLASS ROOM AT AMBROSE MEMORIAL SCHOOL, KHLIEHRIAT WEST	
  	
Date of Inspection:	16.06.2016
Team of inspection officers:	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Extension of Class Rooms at Ambrose Memorial School, Khliehriat West
Name of the MP:	Smt. W. Syiem MP(RS)
Year recommended/sanctioned:	2014
Amount & Date of sanctioned by the DC:	Rs 5,44,000/- sanctioned on 10 th July 2014
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 4,08,000/- released from Block Office on 3 rd September 2014. Not yet released.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 4,08,000/-
Date of commencement/starting of the work:	3 rd September 2014
Date of completion/Expected date of completion:	30 th October 2015
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the School Managing Committee, Ambrose Memorial Secondary School, Khliehriat.
Whether signboard erected or not:	Yes
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	Utilisation Certificate of 1 st instalment has been submitted to BDO,Khliehriat C &RD Block on 29 th April 2015 Not yet submitted to BDO, Khliehriat C&RD Block.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	No
Impact of the scheme:	Addition of extra classrooms to accommodate the students.
Findings/Observations:	<ol style="list-style-type: none"> On observation it was found that the building constructed is sound and strong as good quality materials were used along with good workmanship. There are no visible defects such as cracks, etc. It was painted with good quality paints. The building consists of two Class rooms and the Secretary, School Managing Committee informed that the Committee had also spent from their own funds for completing the class rooms. The Secretary was advised to submit the UC of the 1st installment so as to avail the 2nd installment since the construction is complete. The Secretary of the School Managing Committee was advised to fix a plaque on the wall of the building indicating the details viz, Name of MP, Year, Name of scheme, Amount sanctioned, date of completion, etc.
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

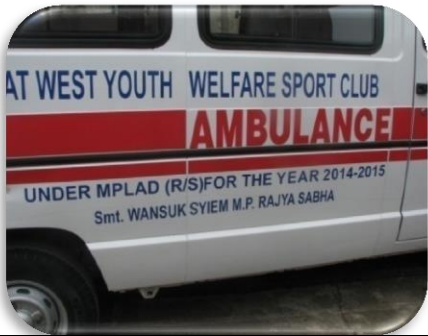


PURCHASE OF TATA WINGER AMBULANCE A/C/ KHLIEHRIAT

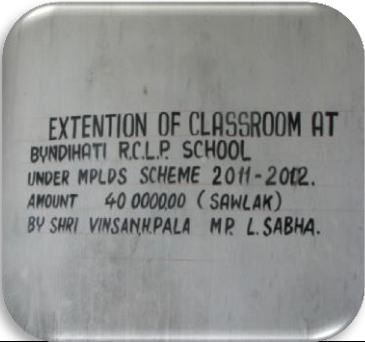





Date of Inspection	16.06.2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Purchase of TATA Winger Ambulance A/C/ Khliehriat
Name of the MP:	Smt. W. Syiem MP(RS)
Year recommended/sanctioned:	2014
Amount & Date of sanctioned by the DC:	Rs. 8,63,000/- sanctioned on 16 th December 2014
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :-	Rs. 8,63,000/- released from Block Office on 25 th February 2015.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 8,63,000/-
Date of commencement/starting of the work:	24 th February 2015
Date of completion/Expected date of completion:	8 th May 2015
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	East Jaintia Hills Welfare & Development Society, Khliehriat
Whether signboard erected or not:	-
Date of submission of UC: 1 st Instalment:	Utilisation Certificate has been submitted to the BDO, Khliehriat C&RD Block on 15 th May 2015
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	No
Impact of the scheme:	Benefit for the general public for use during emergencies,accidents,etc.
Findings/Observations:	1.It was found that the ambulance was well equipped with modern amenities for the patients. 2.It is serving the whole area by carrying patients from East .Jaintia Hills to Silchar, Shillong, Guwahati for treatment who need to pay only for the fuel during their journey. 3.The particulars of the scheme were written on the body of the ambulance.
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

IMPROVEMENT OF BYNDIHATI RCLP SCHOOL	
  	
Date of Inspection	16.06.2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Improvement of Byndihati RCLP School
Name of the MP:	Shri V.H Pala MP(LS)
Year recommended/sanctioned:	2013
Amount & Date of sanctioned by the DC:	Rs. 4,00,000/- sanctioned on 16 th September 2013
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 2,00,000/- released from Block Office on 11 th February 2014. Rs. 2,00,000/- released from Block Office on 01 st August 2014.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 4,00,000/-
Date of commencement/starting of the work:	09 th April 2012
Date of completion/Expected date of completion:	09 th June 2014
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the School Managing Committee, Byndihati RCLP School.
Whether signboard erected or not:	Yes
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	Utilisation Certificate of 1 st instalment has been submitted to the BDO, Khliehriat C&RD Block on 22 nd May 2014 and Utilisation Certificate of 2 nd instalment has been submitted to the BDO, Khliehriat C&RD Block on 05 th August 2014
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Improvement of the school building will have a positive impact on the students and community, so that high academic standards can be achieved with teachers motivated so that the students can achieve their goals.
Findings/Observations:	1.The building construction is of good quality with usage of good quality materials and good workmanship It is also well maintained. 2.There is no evidence of leakage, no visible defects such as cracks, etc. 3.The Classroom dimensions are Length = 6m, Breadth = 4m. It consists of 3 rooms with wooden door, windows (4*2), Columns(4), beams(4) and grill fencing. 4.The School Managing Committee informed that they had contributed Rs 5,00,000/- for the completion of the school building.
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

CONSTRUCTION OF ECO-FRIENDLY CREMATORIUM FOR THE PEOPLE OF SEIN NIAMTRE, BYNDIHATI	
Date of Inspection	16.06.2016 .
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Construction of Eco-Friendly Crematorium for the people of Sein Niamtre, Byndihati.
Name of the MP:	Smt. W. Syiem MP(RS)
Year recommended/sanctioned:	2014
Amount & Date of sanctioned by the DC:	Rs. 25,00,000/- sanctioned on 14 th January 2014
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 18,37,500/- released from block office on 11 th February 2014 Rs. 6,62,500/- released from block office on 06 th October 2015
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 25,00,000/-
Date of commencement/starting of the work:	29 th January 2014
Date of completion/Expected date of completion:	04 th September 2015
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Seng Niamtre, Byndihati
Whether signboard erected or not:	Yes
Date of submission of UC: 1 st Instalment:	Submitted to the BDO Khliehriat C&RD Block on 06 th February 2015
2 nd Instalment:	Submitted to the BDO Khliehriat C&RD Block on 15 th October 2015
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Benefit to the people of indigenous (Niamtre) faith. Moreover the Crematorium is environmentally friendly with less usage of wood and is non-polluting.
Findings/Observations:	It was found that the construction of the Crematorium was fully completed and it is open for public use for the people of Byndihati village. The floor was paved with granite tiles and the signboard was also erected.
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

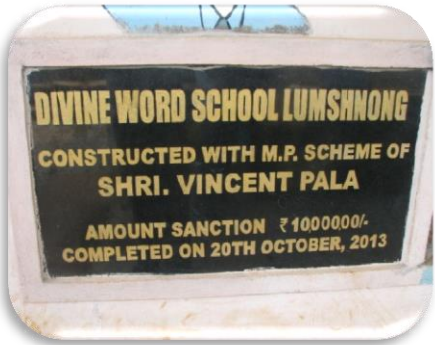
CONSTRUCTION OF DON BOSCO COLLEGE	
  	
Date of Inspection	16.06.2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Construction of Don Bosco College
Name of the MP:	Smt. W.Syiem MP(RS)
Year recommended/sanctioned:	2015
Amount & Date of sanctioned by the DC:	Rs.20,00,000/- sanctioned on 15 th July 2015
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 10,00,000/- released from block office on 15 th October 2016 Rs. 10,00,000/- released from block office on 28 th March 2016
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 20,00,000/-
Date of commencement/starting of the work:	14 th September 2015
Date of completion/Expected date of completion:	28 th March 2016
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Governing Body, St. Anthony's College, Shillong.
Whether signboard erected or not:	Yes
Date of submission of UC: 1 st instalment :- 2 nd instalment :-	Submitted to the BDO, Khliehriat C&RD Block on 08 th February 2016 Submitted to the BDO, Khliehriat C&RD Block on 30 th March 2016
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Construction of the college building will have a positive impact both on the students and community, setting of high academic standards, paving the way for accommodation of more students from the areas in and around Khliehriat.
Findings/Observations:	1. The building is two storied. The structural work, exterior and interior plastering, interior white washing, primer is completed . 2. The building consist of 3 class rooms and its dimension Length=110m and Breadth= 60m. 3. There is no evidence of leakage, no visible defects such as cracks,etc. 4. Painting, electrical works , miscellaneous works are in progress.
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-


CONSTRUCTION OF BUILDING OF DIVINE WORDS SCHOOL, LUMSHNONG	
  	
Date of Inspection	16.06.2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Construction of Building of Divine Words School, Lumshnong
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2014
Amount & Date of sanctioned by the DC:	Rs. 10,00,000/- sanctioned on 14 th January 2014
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 4,90,000/- released from block office on 02 nd July 2014 Rs. 5,10,000/- released from block office on 07 th September 2015
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 10,00,000/-
Date of commencement/starting of the work:	29 th January 2014
Date of completion/Expected date of completion:	14 th August 2015
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the School Managing Committee, Divine Word School, Lumshnong.
Whether signboard erected or not:	Yes
Date of submission of UC: 1 st instalment :- 2 nd instalment :-	Submitted to the BDO, Khliehriat C&RD Block on 18 th November 2014 Submitted to the BDO, Khliehriat C&RD Block on 10 th September 2015
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Construction of the School building will benefit the people living in and around Lumshnong especially the children of the workers of the Cement factories.
Findings/Observations	<ol style="list-style-type: none"> The construction of the building is of good quality with usage of good quality of materials and good workmanship. It is also well maintained. It was found that the building is two storied. There are 5 classrooms in each floor which included 1 (one) Teacher's room , 2(two) office rooms and 1 (one) indoor game room and two 2 (two) classrooms are in progress as the School Managing Committee contributed Rs 35,00,000/- from own funds for completion of the building construction. The Plinth area of the building is Length= 24M and Breadth= 22M
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-


CONSTRUCTION OF NARPUH BORDER PRESBYTERIAN BUILDING AT LUMSHNONG	
	
Date of Inspection	16.06.2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Construction of Narpuh Border Presbyterian Building at Lumshnong
Name of the MP:	Shri V.H. Pala MP(LS)
Year recommended/sanctioned:	2014
Amount & Date of sanctioned by the DC:	Rs. 3,00,000/- sanctioned on 14 th January 2014
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 1,47,000/- released from block office on 18 th November 2014 Rs. 1,53,000/- released from block office on 22 nd March 2016
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 3,00,000/-
Date of commencement/starting of the work:	29 th January 2014
Date of completion/Expected date of completion:	18 th February 2013
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work executed by the Construction Committee, Narpuh Border Presbytery
Whether signboard erected or not:	No
Date of submission of UC: 1 st instalment :- 2 nd instalment :-	Submitted to the BDO, Khliehriat C&RD Block on 10 th August 2015 Submitted to the BDO, Khliehriat C&RD Block on 30 th March 2016
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	The building will be used as an office of the Narpuh Presbytery
Findings/Observations:	1. The inspection team found that the construction work of the building is quite big. The execution of the work was as per specifications & drawings. 2.The Secretary, Narpuh Border Presbytery Committee informed that more than Rs 1 crore will be spent for completion of the building. 3. Rs. 3,00,000/- from MPLAD Schemes has already been received from Block office and utilised for construction of the foundation work only. 4.The Committee was advised to erect a signboard indicating the name of the scheme, name of MP, amount sanctioned, date of commencement of the scheme, date of completion, etc. after completion of the building.


Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-




CONSTRUCTION OF STADIUM AT SUTNGA VILLAGE




	
Date of Inspection	16.06.2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Construction of Stadium at Sutnga Village
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2014
Amount & Date of sanctioned by the DC:	Rs. 10,00,000/- sanctioned on 14 th January 2014
Reason for delay in sanction, if any:	
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 5,00,000/- released from block office on 07 th April 2015
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	6 th April 2015
Date of completion/Expected date of completion:	Work in Progress
Status of the work:	Work in Progress
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Local Committee, Dorbar Shnong, Sutnga.
Whether signboard erected or not:	No
Date of submission of UC: 1 st instalment :- 2 nd instalment :-	Submitted to the BDO, Khliehriat C&RD Block on 30 th September 2015 Not yet Submitted.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	The availability of a Stadium will benefit the local village people and the school students of nearby schools who can use it for their required needs.
Findings/Observations:	1.The inspection team was found that earth work cutting, earth filling is in progress 2.The Local committee has been advised to erect a signboard indicating the name of the scheme, name of MP, amount sanctioned, date of commencement of the scheme, date of completion etc. after the work is completed.
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

CONSTRUCTION FOR FENCING AND BASKETBALL FOR HOLY TRINITY SECONDARY SCHOOL MOOPAKHAR, SUTNGA	
	
Date of Inspection	16.06.2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Construction for fencing and basketball for Holy Trinity Secondary School Moopakhar, Sutnga.
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2016
Amount & Date of sanctioned by the DC:	Rs. 8,00,000/- sanctioned on 14 th January 2016
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 4,00,000/- released from block office on 23 rd March 2016 Not yet released.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 4,00,000/-
Date of commencement/starting of the work:	01 st February 2016
Date of completion/Expected date of completion:	Work in Progress
Status of the work:	Work in Progress
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the School Managing Committee, Holy Trinity Secondary School, Moopakhar, Sutnga.
Whether signboard erected or not:	No
Date of submission of UC: 1 st instalment :- 2 nd instalment :-	Submitted to the BDO, Khliehriat C&RD Block on 21 st April 2016 Not yet submitted.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Benefit to the students of the School.
Findings/Observations:	1.It was observed that the Basketball court is completed whereas the Basket Board is yet to be fixed and the fencing is still in progress. 2.Dimension of basket ball court is Length =28m Breadth =15m. 3. Fencing L=100m. 4. The School Managing Committee has been advised to erect a plaque with complete details after completion of the work..
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

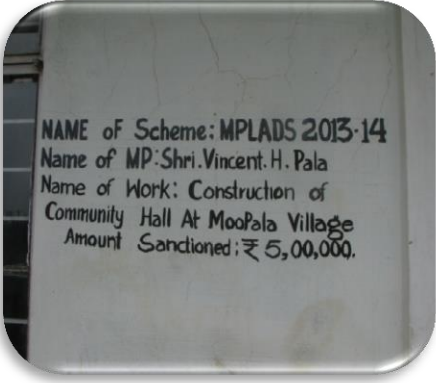CONSTRUCTION OF AUDITORIUM AT SUTNGA DONGPOHSHNONG, PLAYGROUND, SUTNGA	
	
Date of Inspection	16.06.2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Construction of Auditorium at Sutnga Dongpohshnong, Sutnga.
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2016
Amount & Date of sanctioned by the DC:	Rs. 9,00,000/- sanctioned on 14 th January 2016
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 4,50,000/- released from block office on 22 nd March 2016 Not yet released.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 4,50,000/-
Date of commencement/starting of the work:	01 st February 2016
Date of completion/Expected date of completion:	Work in Progress
Status of the work:	Work in Progress
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Youth Club, Pohshnong Sutnga.
Whether signboard erected or not:	-
Date of submission of UC: 1 st instalment :-	Not yet submitted to the Block Office.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	The Auditorium on the 1 st floor will be used for VIP guests and prominent persons. The players and referees/officials will use the ground floor as a changing/dressing room during tournaments.
Findings/Observations:	<ol style="list-style-type: none"> 1. The inspection team found that the Structural work, Roof structure with truss covered with Dyna roof is completed whereas walling, plastering, windows, doors is yet to be started. 2.It is a 2 storied structure with 3 rooms in Ground floor and 1 room on the first floor. 3. It was informed that Rs 5,00,000/- has been contributed by the youth club towards construction of the Auditorium. 4. The members of the Youth club have been advised to erect a Plague with complete details after completion of the work.
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-




CONSTRUCTION OF PLAYGROUND AT MOOKYMPAD VILLAGE	
	
Date of Inspection	16.06.2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Construction of Playground at Mookympad Village.
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2016
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/- sanctioned on 14 th January 2016
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 2,50,000/- released from block office on 19 th April 2016 Not yet released.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 2,50,000/-
Date of commencement/starting of the work:	19 th April 2016
Date of completion/Expected date of completion:	Work in Progress
Status of the work:	Work in Progress
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Mookympad Sports & Social Cultural Club.
Whether signboard erected or not:	-
Date of submission of UC: 1 st instalment :-	Not yet submitted to the Block Office.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	The availability of a playground will benefit the local village people and the school students of nearby schools who can use it for their needs like holding football tournaments, fetes, competitions,etc .
Findings/Observations:	1. It was found that earthwork excavation is in progress. The Secretary, Mookympad Sports & Social Cultural Club informed that they have proposed to construct a retaining wall with an open gallery on the existing playground. 2. The dimension of the playground is Length=96m and Breadth=70m 3. The members of Mookympad Sports & Social Cultural Club have been advised to erect a Plague with complete details after completion of the work.
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

CONSTRUCTION OF COMMUNITY HALL AT MOOPALA VILLAGE	
  	
Date of Inspection	16.06.2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Construction of Community Hall at Moopala Village
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2014
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/- sanctioned on 14 th January 2014
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 2,45,000/- released from block office on 02 nd July 2014 Not yet released.
Reason for delay in release of fund, if any:	Non receipt of Utilisation Certificate from the beneficiary
Amount utilized:	Rs. 2,45,000/-
Date of commencement/starting of the work:	30 th January 2014
Date of completion/Expected date of completion:	30 th January 2016
Status of the work:	Work Completed
Cause/Reason for delay in sanction/completion of works:	Due to Village Members has been changed.
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Local Committee, Moopala Village.
Whether signboard erected or not:	Yes
Date of submission of UC: 1 st instalment :- 2 nd instalment :-	10 th August 2015 Not yet submitted
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	No
Impact of the Scheme:	Benefit for the local people who use the Community Hall for all types of public awareness meetings, Dorbars, award ceremonies, dramatic plays, concert performance, dance competition. etc.
Findings/Observations:	1. The inspection team found that construction of the community hall was completed . 2. There is no evidence of detectable defects such as cracks, etc. 3. The Secretary, Local Committee, Moopala Village informed that Rs 10,00,000/- has been spent from the village funds for completion of the building construction. 4. The Secretary, Local Committee, Moopala Village was advised to submit the UC of the 1 st installment so as to avail the 2 nd installment. 5. Plinth area Length=18.3M and Breadth= 5.2M Wooden door= 8nos, Windows= 6nos, Ventilators= 6nos.
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-


CONSTRUCTION OF WATER TANK FOR KHLIEHRIAT HIGHER SECONDARY SCHOOL		
<div></div> <div></div> <div></div>		
Date of Inspection	17.06.2016	
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer	
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.	
Name of the Scheme:	Construction of Water Tank for Khliehriat Higher Secondary School	
Name of the MP:	Shri V.H.Pala, MP(LS)	
Year recommended/sanctioned:	2014	
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/- sanctioned on 06 th June 2014	
Reason for delay in sanction, if any:		
Date of release of fund: 1 st instalment :-	Rs. 2,50,000/- released from block office on 01 st August 2014	
2 nd instalment :-	Rs. 2,50,000/- released from block office on 26 th June 2015	
Reason for delay in release of fund, if any:	Nil	
Amount utilized:	Rs. 5,00,000/-	
Date of commencement/starting of the work:	13 th June 2014	
Date of completion/Expected date of completion:	15 th June 2015	
Status of the work:	Completed	
Cause/Reason for delay in sanction/completion of works:	Nil	
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.	
Name of executing agency:	The work is executed by the School Managing Committee, Khliehriat Higher Secondary School.	
Whether signboard erected or not:	Yes	
Date of submission of UC: 1 st instalment :- 2 nd instalment :-	Submitted to the BDO, Khliehriat C&RD Block on 13 th January 2015 Submitted to the BDO, Khliehriat C&RD Block on 30 th June 2015	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes	
Impact of the Scheme:	Benefit for the school and students.	
Findings/Observations:	1. The construction of Water Tank is sound and strong with usage of good quality materials and good workmanship. 2. There are no visible cracks and water leakage. 3. It was found that the capacity of water tank is 1.00 Lakh litres. It was constructed with RCC wall, RCC slab with two man hole with steel cover, railing, exterior & interior plastering, etc. 4. It was informed by the School Managing Committee that they had contributed Rs 2,00,000/- towards construction of the Water Tank and also for the Water Pump. 5.The dimension of tank is Length= 10.30M, Width=4.20M, Slab Thickness=100MM	
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-	
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-	
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-	
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-	

EXTENSION OF DKHIAH PRESBYTERIAN SECONDARY SCHOOL	
	
Date of Inspection	17.06.2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Extension of Dkhiah Presbyterian Secondary School.
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2014
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/- sanctioned on 14 th January 2014
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 2,50,000/- released from block office on 01 st August 2014 Rs. 2,50,000/- released from block office on 17 th November 2015
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	20 th May 2014
Date of completion/Expected date of completion:	15 th October 2015
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the School Managing Committee, Dkhiah Presbyterian Secondary School.
Whether signboard erected or not:	Yes
Date of submission of UC: 1 st instalment :- 2 nd instalment :-	Submitted to the BDO, Khliehriat C&RD Block on 06 th January 2015 Submitted to the BDO, Khliehriat C&RD Block on 01 st December 2015
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Extension of school building classrooms to accommodate the students.
Findings/Observations:	1. The construction/extension of School building is sound and strong with usage of good quality materials and good workmanship. 2. There are no visible defects like cracks. 3. It was found that the School building is fully completed & there are 2 Rooms i.e 1 for Classroom and 1 for Laboratory Room attached with 1 Toilet & Urinary. There are 4 windows, 2 doors, 2 ventilators in the building. 4. Plinth area Length= 19.00M, breadth=4.80M. 5. It was informed that the School managing committee contributed Rs 5,00,000/- towards completion of the building.
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

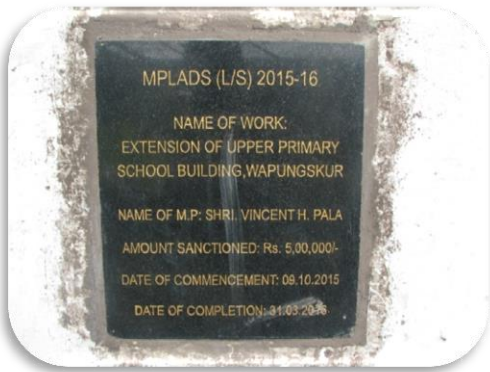


EXTENSION OF WAPUNGSKUR SECONDARY SCHOOL, WAPUNG	
  	
Date of Inspection	17.06.2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Extension of Wapungskur Secondary School, Wapung
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2015
Amount & Date of sanctioned by the DC:	Rs.5,00,000/- sanctioned on 16 th April 2015
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 3,75,000/- released from block office on 18 th May 2015 Rs. 1,25,000/- released from block office on 25 th November 2015
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	13 th May 2015
Date of completion/Expected date of completion:	24 th November 2015
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the School Managing Committee, Wapungskur Secondary School, Wapung
Whether signboard erected or not:	Yes
Date of submission of UC: 1 st instalment :- 2 nd instalment :-	Submitted to the BDO, Khliehriat C&RD Block on 28 th August 2015 Submitted to the BDO, Khliehriat C&RD Block on 01 st December 2015
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Extension of school building classrooms to accommodate the students.
Findings/Observations:	<ol style="list-style-type: none"> The inspection team found that the School building is completed with 2 Classroom s, having 2 doors, 2 windows & 2 ventilators. The Secretary, School Managing Committee, Wapungskur Secondary School, Wapung informed that Rs 1,00,000/- has been spent from the School funds for completion of the building .
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-


EXTENSION OF UPPER PRIMARY SCHOOL BUILDING, WAPUNGSKUR, WAPUNG	
<div><div><div><p>MPLADS (L/S) 2015-16</p><p>NAME OF WORK: EXTENSION OF UPPER PRIMARY SCHOOL BUILDING, WAPUNGSKUR</p><p>NAME OF M.P: SHRI. VINCENT H. PALA</p><p>AMOUNT SANCTIONED: Rs. 5,00,000/-</p><p>DATE OF COMMENCEMENT: 08.10.2015</p><p>DATE OF COMPLETION: 31.03.2016</p></div></div><div></div><div></div></div>	
Date of Inspection	17.06.2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Extension of Upper Primary School Building, Wapungskur, Wapung
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2015
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/- sanctioned on 22 nd September 2015
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 2,50,000/- released from block office on 02 nd November 2015 Rs. 2,50,000/- released from block office on 11 th April 2016
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	09 th October 2015
Date of completion/Expected date of completion:	31 st March 2016
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the School Managing Committee, Upper Primary School Wapungskur, Wapung.
Whether signboard erected or not:	Yes
Date of submission of UC: 1 st instalment :- 2 nd instalment :-	Submitted to the BDO, Khliehriat C&RD Block on 19 th February 2016 Submitted to the BDO, Khliehriat C&RD Block on 20 th April 2016
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Extension of school building classrooms to accommodate the students.
Findings/Observations:	<div>1. The Extension of School building is of good quality with I usage of good materials and good workmanship with no visible cracks.</div> <div>2. It was found that the School building is completed and there are 2 Classroom s with 2 doors,4 windows and 2 ventilators.</div> <div>3. The Secretary, School Managing Committee, Upper Primary School Wapungskur, Wapung. Informed that the School Managing Committee had contributed Rs 1,00,000/- from the School funds for completion of the building.</div>
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

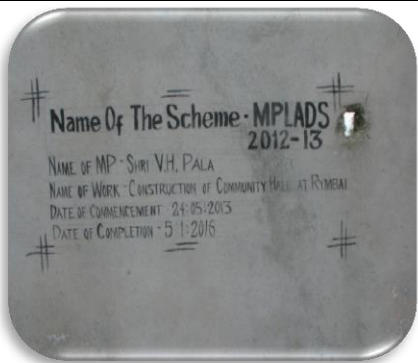

CONSTRUCTION OF COMMUNITY HALL AT RYMBAI

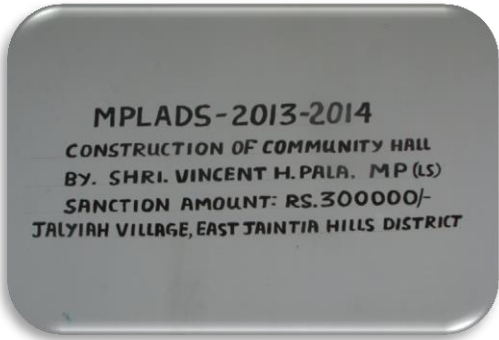

Date of Inspection	17.06.2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Construction of Community Hall at Rymbai
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2013
Amount & Date of sanctioned by the DC:	Rs.4,00,000/- sanctioned on 15 th May 2013
Reason for delay in sanction, if any:	
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 2,00,000/- released from block office on 30 th May 2013 Rs. 2,00,000/- released from block office on 16 th March 2016
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 4,00,000/-
Date of commencement/starting of the work:	24 th May 2013
Date of completion/Expected date of completion:	05 th January 2016
Status of the work:	Work in progress
Cause/Reason for delay in sanction/completion of works:	Due to dismantling of the old building and paucity of funds.
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Local Committee, Rymbai Village
Whether signboard erected or not:	Yes
Date of submission of UC: 1 st instalment :- 2 nd instalment :-	Submitted to the BDO, Khliehriat C&RD Block on 07 th April 2015 Submitted to the BDO, Khliehriat C&RD Block on 01 st April 2016
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Benefits for the local people for all types of public awareness, Dorbars, awards ceremonies, dramatics plays, concerts performance, dance competition. etc.
Findings/Observations:	1. It was observed that the project is in progress. The structural work, brick wall, column, tie beams, lintel, full steel casement window and doors, truss, including stage is completed whereas Roof structure, plastering (interior & exterior) and flooring is yet to be constructed due to shortage of funds since the amount for the project is quite high. 2. There are 13 windows and 10 ventilators. Hall dimension, L= 19M, B=10.90M and H= 7.5M Stage dimension, L= 15.6M, B=4.9M and H=4.5M. Verandah dimension, L=7M, B=2.3M. 3. It was informed by the Secretary, Local Committee that public had contributed Rs 10,00,000/-for construction of the Community Hall. 4. The Secretary, Local Committee has been advised to erect a Plaque with complete details after completion of the work.
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

CONSTRUCTION OF COMMUNITY HALL AT JALYIAH VILLAGE	
<div>    </div>	
Date of Inspection	17.06.2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Construction of Community Hall at Jalyiah Village
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2014
Amount & Date of sanctioned by the DC:	Rs. 3,00,000/- sanctioned on 14 th January 2014
Reason for delay in sanction, if any:	
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 1,47,000/- released from block office on 30 th June 2014
Reason for delay in release of fund, if any:	Non receipt of Utilisation Certificate from the beneficiary
Amount utilized:	Rs. 1,47,000/-
Date of commencement/starting of the work:	25 th June 2014
Date of completion/Expected date of completion:	10 th March 2016
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Local Committee, Jalyiah Village.
Whether signboard erected or not:	Yes
Date of submission of UC: 1 st instalment :- 2 nd instalment :-	Submitted to the BDO, Khliehriat C&RD Block on 02 nd June 2016 Not yet submitted.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	NA
Impact of the Scheme:	Benefit for the local people who use the Community Hall for all types of public awareness meetings, Dorbars, award ceremonies, dramatic plays, concert performance, dance competition. etc.
Findings/Observations:	1.It was found that the construction of the community hall was completed with no evidence of detectable defects such as cracks, seepage, etc. 2. There are 2 rooms, 2 windows & 3 ventilators. Plinth Area L= 7.55m and B= 7.2m 3.The Secretary, Local Committee, Jalyiah Village informed that Rs 2,00,000/- has been contributed from the village funds for completion of the building. 4. The Secretary, Local Committee, Jalyiah Village was advised to submit the UC of the 1 st installment so as to avail the 2 nd installment since the scheme is already completed.
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

CONSTRUCTION FOR FENCING OF LAD SUTNGA R.C. GRAVEYARD	
	
Date of Inspection	16.06.2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Construction for fencing of Lad Sutnga R.C. Graveyard
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2015
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/- sanctioned on 22 nd September 2015
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 2,50,000/- released from block office on 09 th November 2015 Not yet released
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 2,50,000/-
Date of commencement/starting of the work:	26 th October 2015
Date of completion/Expected date of completion:	Work in progress
Status of the work:	Work in progress
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Romance Catholic Committee, Lad Sutnga.
Whether signboard erected or not:	No
Date of submission of UC: 1 st instalment :-	Submitted to the BDO, Khliehriat C&RD Block on 26 th May 2016
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Benefit for the Catholic people and to control the trespassing of the people into the Graveyard.
Findings/Observations:	1. The Inspection team found that the construction of Fencing is in progress & it was constructed with brick masonry wall and Barbed wire. 2. The Local Committee has been advised to erect a Plague with complete details after completion of the work.
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

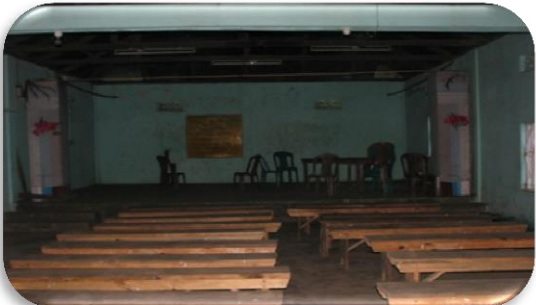CONSTRUCTION OF COMMUNITY HALL AT DKHIAH EAST VILLAGE	
 	
Date of Inspection	16.06.2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri Rimingson Daw, Assistant Engineer, Shri Rophel Bamon, Gram Sevak, Shri Mitchem Shullai, Gram Sevak, and Shri M. Lyngdoh, Gram Sevak.
Name of the Scheme:	Construction of Community hall at Dkhiah East Village
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2014
Amount & Date of sanctioned by the DC:	Rs.5,00,000/- sanctioned on 14 th January 2014
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 2,50,000/- released from block office on 10 th July 2014 Not yet released.
Reason for delay in release of fund, if any:	Non receipt of Utilisation Certificate from the beneficiary
Amount utilized:	Rs. 2,50,000/-
Date of commencement/starting of the work:	10 th June 2014
Date of completion/Expected date of completion:	Work in progress
Status of the work:	Work in progress
Cause/Reason for delay in sanction/completion of works:	Awaiting funds from the Fund Raising Committee of the village.
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Local Committee, Dkhiah East Village.
Whether signboard erected or not:	Yes
Date of submission of UC: 1 st instalment :- 2 nd instalment :-	Submitted to the BDO, Khliehriat C&RD Block on 18 th May 2015 Not yet submitted.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Benefit for the local people who will use the Community Hall for all types of public awareness meetings, Dorbars, award ceremonies, dramatic plays, concert performance, dance competition. etc.
Findings/Observations:	<ol style="list-style-type: none"> 1. The Secretary, Local Committee, Dkhiah East Village informed that it was proposed that a new building will be constructed in lieu of the existing Community Hall & the Plans & Estimate are readily available. 2. The reason for delay in completion of the Committee Hall is due to insufficient amount received from MPLAD Schemes & the 1st installment was utilised for repairing the roof with CGI sheets, construction of retaining wall, buying new benches and chairs in the existing building. 3. The Secretary, Local Committee, Dkhiah East Village informed that the construction of the new building will take time for completion since they are waiting for funds from other schemes where the 2nd installment will be utilised.
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
