


# CONSTRUCTION (EXTENSION) OF POMLUM SECONDARY SCHOOL, P.O. NONGLYER

<b>Date of Inspection:</b>		18 <sup>th</sup> August 2017	
<b>Team of inspection officers:</b>		Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdo, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer	
<b>Accompanied by:</b>		Shri B. Wanniang, Junior Engineer, Myllem Block	
<b>Name of the Scheme:</b>		Construction (Extension) of Pomlum Secondary School, P.O. Nonglyer	
<b>Name of the MP:</b>		Shri V.H. Pala, MP(LS)	
<b>Year recommended/sanctioned:</b>		2014-15	
<b>Amount &amp; Date of sanction by the DC:</b>		Rs. 10,00,000/- sanctioned on 2 <sup>nd</sup> June 2016	
<b>Reason for delay of sanction, if any:</b>		Nil	
<b>Date of release of fund:</b>			
<b>1<sup>st</sup> instalment :-</b>		-----	
<b>2<sup>nd</sup> instalment :-</b>			
<b>Reason for delay in release of fund, if</b>		Nil	
<b>Amount utilized:</b>		-----	
<b>Date of commencement/starting of the work:</b>		-----	
<b>Date of completion/Expected date of completion:</b>		-----	
<b>Status of the work:</b>		Not yet started	
<b>Cause/Reason for delay in sanction/completion of works:</b>		Waiting for the completion of Main Building	
<b>Whether inspection carried out from Block/DCs office:</b>		-----	
<b>Name of executing agency:</b>		-----	
<b>Whether signboard erected or not:</b>		-----	
<b>Date of submission of UC:</b>			
<b>1<sup>st</sup> Instalment:</b>		-----	
<b>2<sup>nd</sup> Instalment:</b>			
<b>In case of completed Scheme whether the completion Report/ Certificate submitted to BDO/DC:</b>		-----	
<b>Impact of the scheme:</b>			
<b>Findings/Observations:</b>		<ol style="list-style-type: none"> <li>1. On inspection the team found that the construction of school building has not yet been started. It was informed by the School Managing Committee that the project of MPLADs Scheme has been delayed due to the ongoing project of the Asian Development Bank.</li> <li>2. The School Managing Committee was advised to start the project of MPLADs Scheme as soon as possible, since it has exceeded the time line.</li> </ol>	

# CONSTRUCTION OF FENCING FOR SANMER SECONDARY SCHOOL, 5<sup>TH</sup> MILE, UPPER SHILLONG

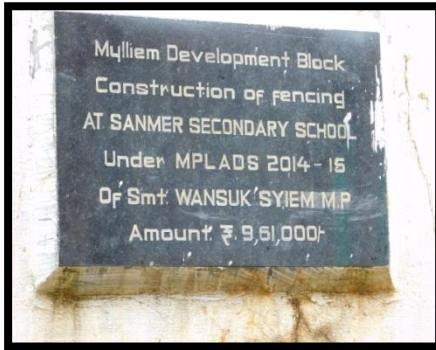


<b>Date of Inspection:</b>	18 <sup>th</sup> August 2017	
<b>Team of inspection officers:</b>	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdo, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer	
<b>Accompanied by:</b>	Shri B. Wanniang, Junior Engineer, Myllem Block	
<b>Name of the Scheme:</b>	Construction of Fencing for Sanmer Sec. School, 5 <sup>th</sup> Mile, Upper Shillong	
<b>Name of the MP:</b>	Smt. W. Syiem, MP(RS)	
<b>Year recommended/sanctioned:</b>	2014-15	
<b>Amount &amp; Date of sanction by the DC:</b>	Rs 9,61,000/- sanctioned on 11 <sup>th</sup> May 2015	
<b>Reason for delay in sanction, if any:</b>	Nil	
<b>Date of release of fund:</b>		
1 <sup>st</sup> instalment :-	16 <sup>th</sup> June 2015.	
2 <sup>nd</sup> instalment :-	22 <sup>nd</sup> March 2016.	
<b>Reason for delay in release of fund, if any:</b>	Nil	
<b>Amount utilized:</b>	Rs. 9,61,000/-	
<b>Date of commencement/starting of the work:</b>	16 <sup>th</sup> June 2015	
<b>Date of completion/Expected date of completion:</b>	23 <sup>rd</sup> March 2016	
<b>Status of the work:</b>	Work Completed	
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil	
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.	
<b>Name of executing agency:</b>	The work is executed by the Managing Committee of the School.	
<b>Whether signboard erected or not:</b>	Yes	
<b>Date of submission of UC:</b>		
1 <sup>st</sup> Instalment:	-----	
2 <sup>nd</sup> Instalment:		
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	Yes	
<b>Impact of the scheme:</b>	Boundary demarcation and prevent of encroachment of strangers.animals,etc.	
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>1. During inspection it has been found that construction of Fencing is completed.</li> <li>2. It was informed that ₹ 3 lakhs has been contributed by the School Managing Committee for completion of the scheme.</li> <li>3. The quality of the work is satisfactory.</li> <li>4. Its dimension:                      Brick Wall: Length =300m and Height =2.4m                      Retaining Wall: Length=300m and Height=2m                      Gate: :Length=1m and Height=1.6m                 </li> </ol>	

# CONSTRUCTION OF ST. PAULS SEMINARY SOCIETY, 3<sup>RD</sup> MILE, UPPER SHILLONG



<b>Date of Inspection:</b>	18 <sup>th</sup> August 2017	
<b>Team of inspection officers:</b>	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdo, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer	
<b>Accompanied by:</b>	Shri B. Wanniang, Junior Engineer, Myllem Block	
<b>Name of the Scheme:</b>	Construction of St. Pauls Seminary Society, 3 <sup>rd</sup> Mile, Upper Shillong	
<b>Name of the MP:</b>	Shri V.H. Pala, MP(LS)	
<b>Year recommended/sanctioned:</b>	2016-17	
<b>Amount &amp; Date of sanction by the DC:</b>	Rs. 5,00,000/- sanctioned on 21 <sup>st</sup> September 2016	
<b>Reason for delay in sanction, if any:</b>	Nil	
<b>Date of release of fund:</b> 1 <sup>st</sup> instalment :- 2 <sup>nd</sup> instalment :-	30 <sup>th</sup> May 2017. -----	
<b>Reason for delay in release of fund, if any:</b>	Nil	
<b>Amount utilized:</b>	Rs. 2,50,000/-	
<b>Date of commencement/starting of the work:</b>	15 <sup>th</sup> April 2017	
<b>Date of completion/Expected date of completion:</b>	-----	
<b>Status of the work:</b>	Work completed & final payment will be released soon .	
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil	
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.	
<b>Name of executing agency:</b>	The work is executed by the Managing Committee of Society.	
<b>Whether signboard erected or not:</b>	No	
<b>Date of submission of UC:</b> 1 <sup>st</sup> Instalment: 2 <sup>nd</sup> Instalment:	-----	
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	-----	
<b>Impact of the Scheme:</b>	Benefit for the students for arranging programmes, recreational activities.etc	
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>On inspection it has been observed that the construction of Seminary Hall is completed.</li> <li>The quality of workmanship is very good.</li> <li>It was informed that ₹10 lakhs has been contributed by the Society in completion of the scheme and also there was community participation from the parents of the student studying at St.Pauls Seminary towards completion of the scheme.</li> <li>The Society has been advised to submit UC, Photographs for releasing of the 2nd instalment from the Block Development Officer.</li> <li>Its dimension: Plinth area of Room Hall: L=15.2m and B=7.6m-----Windows ( 200*115)m (13nos) Ventilation: (30*100) cm (24 nos) -----Steel Door: 1 no. Column size: 34cm*35cm-----Beam size: 45cm * 32cm.</li> <li>The Seminary Society was advised to erect a plaque with complete details of the scheme mentioning the name of MP, amount sanctioned , date of starting and completion.etc</li> </ol>	

# EXTENSION OF SANSHNONG U.P. SCHOOL, 3<sup>RD</sup> MILE, UPPER SHILLONG

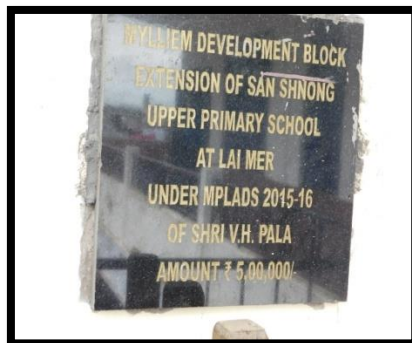


<b>Date of Inspection:</b>	18 <sup>th</sup> August 2017	
<b>Team of inspection officers:</b>	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer	
<b>Accompanied by:</b>	Shri B. Wanniang, Junior Engineer, Myllem Block	
<b>Name of the Scheme:</b>	Extension of Sanshnong U.P. School, 3 <sup>rd</sup> Mile, Upper Shillong	
<b>Name of the MP:</b>	Shri. V.H. Pala, MP(LS)	
<b>Year recommended/sanctioned:</b>	2015-16	
<b>Amount &amp; Date of sanction by the DC:</b>	Rs.5,00,000/- sanctioned on 16 <sup>th</sup> December 2015	
<b>Reason for delay in sanction, if any:</b>	Nil	
<b>Date of release of fund:</b>	23 <sup>rd</sup> February 2016. 16 <sup>th</sup> August 2016.	
<b>1<sup>st</sup> instalment :-</b>		
<b>2<sup>nd</sup> instalment :-</b>		
<b>Reason for delay in release of fund, if any:</b>	Nil	
<b>Amount utilized:</b>	Rs. 5,00,000/-	
<b>Date of commencement/starting of the work:</b>	14 <sup>th</sup> February 2016	
<b>Date of completion/Expected date of completion:</b>	14 <sup>th</sup> August 2016	
<b>Status of the work:</b>	Work Completed	
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil	
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.	
<b>Name of executing agency:</b>	The work is executed by the Managing Committee	
<b>Whether signboard erected or not:</b>	Yes	
<b>Date of submission of UC:</b>	-----	
<b>1<sup>st</sup> instalment :-</b>		
<b>2<sup>nd</sup> instalment :-</b>		
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	Yes	
<b>Impact of the Scheme:</b>	Additional rooms to accommodate more students for better education & to ease the problem of congestion.	
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>On inspection the team found that the extension of Sanshnong U.P School is completed. It consists of two rooms constructed with usage of good quality materials.</li> <li>It was informed that ₹ 35,000/- had been contributed by the School Managing Committee.</li> <li>Its dimension: Plinth area L=6.3m and B=4.2m. Window size: 1.2m * 1.5m (18 nos) -----Door: 75cm*180cm (2 nos). Chowkat: (10*6* 440) cm (2nos)-----Veranda: L=13.6m and Width=1.15m. Parapet Brick railing: L=13.6m and H=70cm----- Grill railing: L=13.6m H=35cm. Slab: L=13.6m and B=1.4m+4.2m Column size: 28cm*28cm (10 nos)-----Beam size: 25cm * 28cm.</li> </ol>	

# PROVIDING OF BOUNDARY WALL TO COG HALL, NONGUMLONG



<b>Date of Inspection:</b>	18 <sup>th</sup> August 2017
<b>Team of inspection officers:</b>	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
<b>Accompanied by:</b>	Shri B. Wanniang, Junior Engineer, Myllem Block
<b>Name of the Scheme:</b>	Providing of Boundary Wall to COG Hall, Nongumlong
<b>Name of the MP:</b>	Shri V.H. Pala, MP(LS)
<b>Year recommended/sanctioned:</b>	2015-16
<b>Amount &amp; Date of sanction by the DC:</b>	Rs. 5,00,000/- sanctioned on 9 <sup>th</sup> October 2015
<b>Reason for delay in sanction, if any:</b>	Nil
<b>Date of release of fund:</b>	
1 <sup>st</sup> instalment :-	16 <sup>th</sup> February 2016.
2 <sup>nd</sup> instalment :-	27 <sup>th</sup> September 2016.
<b>Reason for delay in release of fund, if any:</b>	Nil
<b>Amount utilized:</b>	Rs. 5,00,000/-
<b>Date of commencement/starting of the work:</b>	13 <sup>th</sup> February 2016
<b>Date of completion/Expected date of completion:</b>	20 <sup>th</sup> September 2016
<b>Status of the work:</b>	Completed
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.
<b>Name of executing agency:</b>	The work is executed by the Managing Committee of COG Hall.
<b>Whether signboard erected or not:</b>	Yes
<b>Date of submission of UC:</b>	
1 <sup>st</sup> instalment :-	-----
2 <sup>nd</sup> instalment :-	
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	Yes
<b>Impact of the Scheme:</b>	Demarcation of boundary and prevent trespassing of strangers.
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>On inspection the team found that the fencing at COG is completed.</li> <li>The quality of work is satisfactory</li> <li>Its dimension: Wall fencing: Length =108m and Height=2.8m. Grill fencing: Length=108m and Height=30cm.</li> </ol>

# CONSTRUCTION OF CC DRAIN FOR PUBLIC DRAINAGE AT LUMMAWBAH UPPER SHILLONG

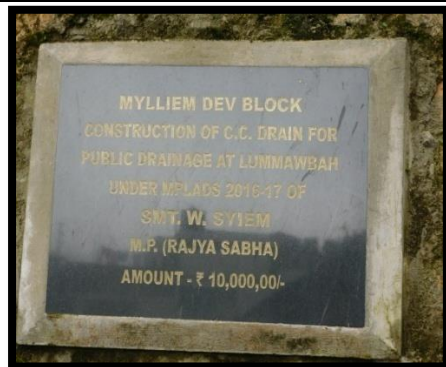


<b>Date of Inspection:</b>	18 <sup>th</sup> August 2017
<b>Team of inspection officers:</b>	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdo, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
<b>Accompanied by:</b>	Shri B. Wanniang, Junior Engineer, Myllem Block
<b>Name of the Scheme:</b>	Construction of CC Drain for Public Drainage at Lummawbah, Upper Shillong
<b>Name of the MP:</b>	Smt. W. Syiem, MP (RS).
<b>Year recommended/sanctioned:</b>	2016-17
<b>Amount &amp; Date of sanction by the DC:</b>	Rs. 10,00,000/-
<b>Reason for delay in sanction, if any:</b>	Nil
<b>Date of release of fund:</b>	
1 <sup>st</sup> instalment :-	6 <sup>th</sup> December 2016.
2 <sup>nd</sup> instalment :-	5 <sup>th</sup> May 2017.
<b>Reason for delay in release of fund, if any:</b>	Nil
<b>Amount utilized:</b>	Rs. 10,00,000/-
<b>Date of commencement/starting of the work:</b>	1 <sup>st</sup> November 2016.
<b>Date of completion/Expected date of completion:</b>	29 <sup>th</sup> April 2017.
<b>Status of the work:</b>	Completed
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.
<b>Name of executing agency:</b>	The work is executed by the Local Dorbar Committee
<b>Whether signboard erected or not:</b>	Yes
<b>Date of submission of UC:</b>	
1 <sup>st</sup> Instalment:	-----
2 <sup>nd</sup> Instalment:	
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	Yes
<b>Impact of the Scheme:</b>	Benefit for locality as drain is covered to be used as a footpath providing accessibility to the main road.
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>On inspection the team found that the construction of CC drainage is completed.</li> <li>Its dimension: CC Drainage: Length=45m, width =1.8m and Height =1.4m. Slab thickness: 100mm.</li> </ol>

# CONSTRUCTION OF AUDITORIUM FOR ST. JOHN BOSCO SECONDARY SCHOOL, LAWSOHTUN



<b>Date of Inspection:</b>	18 <sup>th</sup> August 2017
<b>Team of inspection officers:</b>	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdo, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
<b>Accompanied by:</b>	Shri B. Wanniang, Junior Engineer, Myllem Block
<b>Name of the Scheme:</b>	Construction of Auditorium for St. John Bosco Sec. School, Lawsohtun
<b>Name of the MP:</b>	Shri V.H.Pala, MP(LS)
<b>Year recommended/sanctioned:</b>	2015-16
<b>Amount &amp; Date of sanction by the DC:</b>	Rs. 10,00,000/- sanctioned on 20 <sup>th</sup> January 2017
<b>Reason for delay in sanction, if any:</b>	Nil
<b>Date of release of fund:</b> 1 <sup>st</sup> instalment :- 2 <sup>nd</sup> instalment :-	23 <sup>rd</sup> May 2017. -----
<b>Reason for delay in release of fund, if any:</b>	Nil
<b>Amount utilized:</b>	Rs. 5,00,000/-
<b>Date of commencement/starting of the work:</b>	24 <sup>th</sup> April 2017
<b>Date of completion/Expected date of completion:</b>	-----
<b>Status of the work:</b>	Work in Progress.
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.
<b>Name of executing agency:</b>	The work is executed by the Managing Committee of the School.
<b>Whether signboard erected or not:</b>	Yes
<b>Date of submission of UC:</b> 1 <sup>st</sup> Instalment: 2 <sup>nd</sup> Instalment:	-----
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	Yes
<b>Impact of the Scheme:</b>	Benefit for the school for arranging various programmes, etc.
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>During inspection it has been seen that the construction of auditorium is under progress. The structural work is completed whereas brick walling is under progress.</li> <li>Its dimension: Plinth area: Length=15.7m and Breadth=14.7m Column size: 40cm*60cm (24nos)-----Beam size: 40cm*35cm.</li> <li>The School Managing Committee was advised to erect a plaque with full complete details after completing the scheme.</li> </ol>

# CONSTRUCTION OF MARI GOLD NURSERY SCHOOL BUILDING (BY TREILANG WOMEN SOCIAL WELFARE, MAWLAI NONGKWAR)

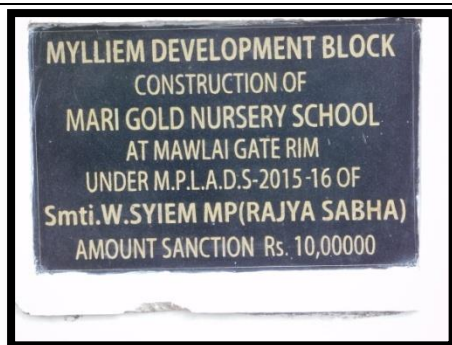

<b>Date of Inspection:</b>	18 <sup>th</sup> August 2017
<b>Team of inspection officers:</b>	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
<b>Accompanied by:</b>	Shri B. Wanniang, Junior Engineer, Myllem Block
<b>Name of the Scheme:</b>	Construction of Mari Gold Nursery School Building (By Treilang, Women Social Welfare, Mawlai Nongkwar)
<b>Name of the MP:</b>	Smt. W. Syiem, MP (RS).
<b>Year recommended/sanctioned:</b>	2016-17
<b>Amount &amp; Date of sanction by the DC:</b>	Rs. 10,00,000/-
<b>Reason for delay in sanction, if any:</b>	Nil
<b>Date of release of fund:</b>	
1 <sup>st</sup> instalment :-	17 <sup>th</sup> August 2016.
2 <sup>nd</sup> instalment :-	10 <sup>th</sup> May 2017.
<b>Reason for delay in release of fund, if any:</b>	Nil
<b>Amount utilized:</b>	Rs. 10,00,000/-
<b>Date of commencement/starting of the work:</b>	8 <sup>th</sup> August 2016.
<b>Date of completion/Expected date of completion:</b>	1 <sup>st</sup> May 2017
<b>Status of the work:</b>	Completed
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.
<b>Name of executing agency:</b>	The work is executed by the Treilang Women Social Welfare, Mawlai Nongkwar
<b>Whether signboard erected or not:</b>	Yes
<b>Date of submission of UC:</b>	
1 <sup>st</sup> Instalment:	-----
2 <sup>nd</sup> Instalment:	
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	Yes
<b>Impact of the Scheme:</b>	It helps in achieving higher academic standards, better education, provision of educational facilities to the local inhabitants, etc.
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>On inspection the team found that the construction of Mari Gold Nursery School is completed. The school building consists of 6 rooms partitioned with plywood and attached with toilet.</li> <li>It was informed that Rs. 1.5 lakhs has been contributed by the School Managing Committee in completion of the scheme.</li> <li>Its dimension: <ul style="list-style-type: none"> <li>Plinth area: Length 0=10m and B=6.3m-----Windows: 200cm*150cm (7nos).</li> <li>Column size: 30cm*30cm (12nos) -----Beam size: 25cm *25cm.</li> <li>Door: 90cm*215cm-----Chowkat: (7*13*510) cm.</li> <li>Toilet room: Length =110cm breadth = 110cm and H=210cm</li> <li>Toilet Door: (90*180) cm. Chowkat: (6*10 *450) cm.</li> </ul> </li> </ol>

# CONSTRUCTION OF COMMUNITY HALL AT MAWLAI NONGKWAR BL-13



<b>Date of Inspection:</b>	18 <sup>th</sup> August 2017
<b>Team of inspection officers:</b>	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
<b>Accompanied by:</b>	Shri B. Wanniang, Junior Engineer, Myllem Block
<b>Name of the Scheme:</b>	Construction of Community Hall at Mawlai Nongkwar BL-13
<b>Name of the MP:</b>	Shri V.H. Pala, MP(LS)
<b>Year recommended/sanctioned:</b>	2013-14
<b>Amount &amp; Date of sanction by the DC:</b>	Rs. 3,00,000/- sanctioned on 9 <sup>th</sup> June 2014
<b>Reason for delay in sanction, if any:</b>	Nil
<b>Date of release of fund:</b> 1 <sup>st</sup> instalment :- 2 <sup>nd</sup> instalment :-	12 <sup>th</sup> August 2014. -----
<b>Reason for delay in release of fund, if any:</b>	Not done as per plan
<b>Amount utilized:</b>	Rs. 1,50,000/-
<b>Date of commencement/starting of the work:</b>	9 <sup>th</sup> June 2014
<b>Date of completion/Expected date of completion:</b>	-----
<b>Status of the work:</b>	Work in progress
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.
<b>Name of executing agency:</b>	The work is executed by the Local Committee
<b>Whether signboard erected or not:</b>	No
<b>Date of submission of UC:</b> 1 <sup>st</sup> Instalment: 2 <sup>nd</sup> Instalment:	-----
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	Yes
<b>Impact of the Scheme:</b>	
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>1. On inspection the team found that the construction of Community Hall is not yet completed.</li> <li>2. It has been observed that the construction of Community Hall is not executed as per plan since the Local Committee wanted a big community Hall and thus the work cannot be completed on time.</li> <li>3. It was informed that Rs. 6.5 lakhs had been contributed by the Local Village Committee.</li> <li>4. The members of the Committee were advised to seek alternative sources of funding for completion of the scheme so that the 2<sup>nd</sup> installment can be drawn.</li> <li>5. The Local Village Committee was advised to erect a plaque with full details mentioning the name of MP, amount sanction, date of starting &amp; completion, etc after completion of the scheme.</li> </ol>

**CONSTRUCTION OF C.C ROAD AT DONG PATA MAWLAI MAWDATBAKI FROM EXISTING ROAD TO FERNANDO TRANSIT SHELTER HOME**



<b>Date of Inspection:</b>	18 <sup>th</sup> August 2017
<b>Team of inspection officers:</b>	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
<b>Accompanied by:</b>	Shri B. Wanniang, Junior Engineer, Myllem Block
<b>Name of the Scheme:</b>	Construction of C.C. Road at Dong Pata Mawlai Mawdatbaki From Existing Road to Fernando Transit Shelter Home
<b>Name of the MP:</b>	Smt. W. Syiem, MP (RS).
<b>Year recommended/sanctioned:</b>	2016-17
<b>Amount &amp; Date of sanction by the DC:</b>	Rs. 5,00,000/-
<b>Reason for delay in sanction, if any:</b>	Nil
<b>Date of release of fund:</b>	
1 <sup>st</sup> instalment :-	23 <sup>rd</sup> August 2016.
2 <sup>nd</sup> instalment :-	24 <sup>th</sup> May 2017
<b>Reason for delay in release of fund, if any:</b>	Nil
<b>Amount utilized:</b>	Rs. 5,00,000/-
<b>Date of commencement/starting of the work:</b>	1 <sup>st</sup> February 2017.
<b>Date of completion/Expected date of completion:</b>	22 <sup>nd</sup> May 2017.
<b>Status of the work:</b>	Completed
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.
<b>Name of executing agency:</b>	The work is executed by the Local Dorbar Committee
<b>Whether signboard erected or not:</b>	Yes
<b>Date of submission of UC:</b>	
1 <sup>st</sup> Instalment:	-----
2 <sup>nd</sup> Instalment:	
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	Yes
<b>Impact of the Scheme:</b>	Providing access to the people of the locality.
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>During inspection it is found that the construction of C.C Road is completed.</li> <li>Its dimension: C.C. Road: Length=76m and Width=3m Hume Pipe: Diameter =1m and Length=9.80m</li> <li>The quality of work is satisfactory.</li> </ol>

# CONSTRUCTION OF FOOTPATH CUM DRAIN AT PYNTHORBAH NEAR COMMUNITY HALL



<b>Date of Inspection:</b>	18 <sup>th</sup> August 2017
<b>Team of inspection officers:</b>	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdo, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
<b>Accompanied by:</b>	Shri B. Wanniang, Junior Engineer, Myllem Block
<b>Name of the Scheme:</b>	Construction of Footpath cum Drain at Pynthorbah near Community Hall
<b>Name of the MP:</b>	Shri V.H. Pala, MP(LS)
<b>Year recommended/sanctioned:</b>	2015-16
<b>Amount &amp; Date of sanction by the DC:</b>	Rs. 5,00,000/- sanctioned on 8 <sup>th</sup> December 2015
<b>Reason for delay in sanction, if any:</b>	Nil
<b>Date of release of fund:</b> 1 <sup>st</sup> instalment :- 2 <sup>nd</sup> instalment :-	8 <sup>th</sup> March 2016. -----
<b>Reason for delay in release of fund, if any:</b>	Nil
<b>Amount utilized:</b>	Rs. 2,50,000/-
<b>Date of commencement/starting of the work:</b>	10 <sup>th</sup> March 2016
<b>Date of completion/Expected date of completion:</b>	-----
<b>Status of the work:</b>	Completed & Final payment will be released soon.Waiting for 2 <sup>nd</sup> instalment
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.
<b>Name of executing agency:</b>	Local Committee.
<b>Whether signboard erected or not:</b>	No
<b>Date of submission of UC:</b> 1 <sup>st</sup> Instalment: 2 <sup>nd</sup> Instalment:	-----
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	Yes
<b>Impact of the Scheme:</b>	Providing access to the people of the locality.
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>On inspection, it has been seen that the construction of footpath cum drain is completed.</li> <li>Its dimension: Drain: L=88m and B=1.8m H=80cm (Both sides) Retaining Wall: Length=5.7m and Height=2.8m. Steel cover grills: 1*1.3m (15nos).</li> <li>The members of the Local Committee were advised to take up with the JE regarding release of 2<sup>nd</sup> installment.</li> <li>The Local Village Committee was advised to erect a plaque with complete details of the scheme.</li> </ol>

# CONSTRUCTION OF SCHOOL BUILDING FOR ST. JOSEPH SECONDARY SCHOOL, PYNTHORUMKHRAH



<b>Date of Inspection:</b>	18 <sup>th</sup> August 2017
<b>Team of inspection officers:</b>	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
<b>Accompanied by:</b>	Shri B. Wanniang, Junior Engineer, Myllem Block
<b>Name of the Scheme:</b>	Construction of School Building for St. Joseph Sec. School, Pynthorumkhras
<b>Name of the MP:</b>	Shri V.H. Pala, MP(LS)
<b>Year recommended/sanctioned:</b>	2016-17
<b>Amount &amp; Date of sanction by the DC:</b>	Rs. 10,00,000/- sanctioned on 5 <sup>th</sup> August 2016
<b>Reason for delay in sanction, if any:</b>	Nil
<b>Date of release of fund:</b>	
1 <sup>st</sup> instalment :-	----- released from Block Office on 8 <sup>th</sup> June 2017
2 <sup>nd</sup> instalment :-	-----
<b>Reason for delay in release of fund, if any:</b>	Nil
<b>Amount utilized:</b>	Rs. 3,00,000/-
<b>Date of commencement/starting of the work:</b>	10 <sup>th</sup> June 2017
<b>Date of completion/Expected date of completion:</b>	-----
<b>Status of the work:</b>	30% Work in progress
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.
<b>Name of executing agency:</b>	The work is executed by the Managing Committee of the School
<b>Whether signboard erected or not:</b>	
<b>Date of submission of UC:</b>	
1 <sup>st</sup> Instalment:	-----
2 <sup>nd</sup> Instalment:	
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	-----
<b>Impact of the Scheme:</b>	Benefit the local people as schooling facilities are available locally. Moreover it will help in providing additional classrooms to the already existing school building.
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>On inspection the team found that the construction of school building is under progress.</li> <li>It has been seen that the work is completed up-to plinth level, whereas laying of soling and compaction of flooring is ongoing.</li> <li>Its dimension: Plinth area Length=9.15m and Breadth=8.75m</li> <li>The School Managing Committee has been advised to erect a plaque with complete details such as name of MP, date of starting and completion, amount sanctioned after completion of the scheme.</li> </ol>

# CONSTRUCTION OF MOTORABLE ROAD AT LANGKYRDING MIHNGI, SHILLONG




<b>Date of Inspection:</b>	18 <sup>th</sup> August 2017
<b>Team of inspection officers:</b>	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
<b>Accompanied by:</b>	Shri B. Wanniang, Junior Engineer, Myllem Block
<b>Name of the Scheme:</b>	Construction of Motorable Road at Langkyrding Mihngi, Shillong
<b>Name of the MP:</b>	Smt W. Syiem, MP(RS)
<b>Year recommended/sanctioned:</b>	2015-16
<b>Amount &amp; Date of sanction by the DC:</b>	Rs. 12,02,500/- sanctioned on 27 <sup>th</sup> November 2015
<b>Reason for delay in sanction, if any:</b>	Nil
<b>Date of release of fund:</b>	
1 <sup>st</sup> instalment :-	-----
2 <sup>nd</sup> instalment :-	3 <sup>rd</sup> May 2016
<b>Reason for delay in release of fund, if any:</b>	Nil
<b>Amount utilized:</b>	Rs. 12,02,500/-
<b>Date of commencement/starting of the work:</b>	3 <sup>rd</sup> March 2016
<b>Date of completion/Expected date of completion:</b>	3 <sup>rd</sup> May 2016
<b>Status of the work:</b>	Completed
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.
<b>Name of executing agency:</b>	The work is executed by the Local Committee
<b>Whether signboard erected or not:</b>	Yes
<b>Date of submission of UC:</b>	
1 <sup>st</sup> Instalment:	-----
2 <sup>nd</sup> Instalment:	
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	Yes
<b>Impact of the Scheme:</b>	Providing access to the people of the locality.
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>On inspection the team found that the construction of motorable road is completed. It was constructed with good quality materials and good workmanship.</li> <li>Its dimension: Motorable Road Total Length=252m and Width=3m. Cross drainage : width= 60cm ,Height = 50cm Length = 3.30m</li> </ol>

# CONSTRUCTION OF COMMUNITY HALL AT POHKSEH



<b>Date of Inspection:</b>	18 <sup>th</sup> August 2017
<b>Team of inspection officers:</b>	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdo, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
<b>Accompanied by:</b>	Shri B. Wanniang, Junior Engineer, Myllem Block
<b>Name of the Scheme:</b>	Construction of Community Hall at Pohkse
<b>Name of the MP:</b>	Smt. W. Syiem, MP (RS).
<b>Year recommended/sanctioned:</b>	2013-14
<b>Amount &amp; Date of sanction by the DC:</b>	Rs. 25,00,000/- sanctioned on 11 <sup>th</sup> June 2014
<b>Reason for delay in sanction, if any:</b>	Nil
<b>Date of release of fund:</b> <b>1<sup>st</sup> instalment :-</b> <b>2<sup>nd</sup> instalment :-</b>	27 <sup>th</sup> August 2014. 1 <sup>st</sup> June 2016.
<b>Reason for delay in release of fund, if any:</b>	Nil
<b>Amount utilized:</b>	Rs. 18,75,000/-
<b>Date of commencement/starting of the work:</b>	28 <sup>th</sup> August 2014.
<b>Date of completion/Expected date of completion:</b>	15 <sup>th</sup> September 2017
<b>Status of the work:</b>	75% Work Completed
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.
<b>Name of executing agency:</b>	The work is executed by the Local Committee.
<b>Whether signboard erected or not:</b>	No
<b>Date of submission of UC:</b> <b>1<sup>st</sup> Instalment:</b> <b>2<sup>nd</sup> Instalment:</b>	-----
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	Yes
<b>Impact of the Scheme:</b>	Benefit to the people of the locality for holding Dorbars, awareness programmes and other social activities.
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>On inspection the team found that the construction of community hall is 75% completed. It was constructed with good quality materials.</li> <li>The community hall consists of 2 Office rooms, a Hall and a Kitchen.</li> <li>Its dimension: Area of a Room: L=5.2m and Breadth =4.4m-----Windows: 1.8m*1.6m (6nos) Area of Kitchen room: L=5.2m and B=3.2m. Area of Hall: L=13.6m and W=5.4m Corridor: Length=5.7m and Breadth =1.7m Veranda (back side): Length =26m and Width =1.6m. Railing Grill: Length =33m and Height =70cm----- Brick walling Railing : Length =33m and Height=50cm. Steel door: 70cm*190cm Chowkat Room1 &amp; Room2: (10*7*520)cm * 4nos. Steel window door: 420cm*230cm. Steel Door:140cm*230cm Gate: 102*90cm -----veranda: L=4.5m and W=1.2m----Tread:25cm Riser: 15cm-----Column Size: 35cm*35cm -----Beam size: 28cm*28cm.</li> <li>The members of the Local Committee were advised to take up with the JE regarding release of final installment.</li> <li>The Local Village Committee was advised to erect a plaque with complete details after completion of the scheme.</li> </ol>

# CONSTRUCTION OF MULTI-PURPOSE HALL FOR ST. PETER'S SECONDARY SCHOOL, MAWPAT

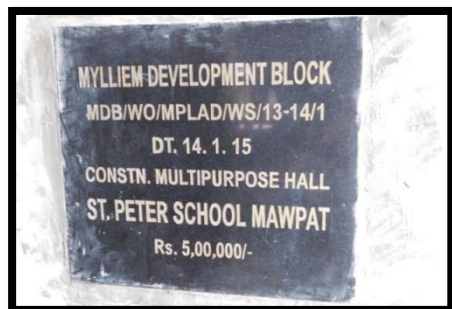

<b>Date of Inspection:</b>	18 <sup>th</sup> August 2017
<b>Team of inspection officers:</b>	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
<b>Accompanied by:</b>	Shri B. Wanniang, Junior Engineer, Myllem Block
<b>Name of the Scheme:</b>	Construction of Multi-purpose Hall for St. Peter's Sec. School, Mawpat
<b>Name of the MP:</b>	Smt. W. Syiem, MP (RS).
<b>Year recommended/sanctioned:</b>	2013-14
<b>Amount &amp; Date of sanction by the DC:</b>	Rs. 5,00,000/- sanctioned on 10 <sup>th</sup> February 2014
<b>Reason for delay in sanction, if any:</b>	Nil
<b>Date of release of fund:</b>	
1 <sup>st</sup> instalment :-	20 <sup>th</sup> January 2015.
2 <sup>nd</sup> instalment :-	9 <sup>th</sup> August 2016.
<b>Reason for delay in release of fund, if any:</b>	Nil
<b>Amount utilized:</b>	Rs. 5,00,000/-
<b>Date of commencement/starting of the work:</b>	20 <sup>th</sup> January 2015
<b>Date of completion/Expected date of completion:</b>	5 <sup>th</sup> August 2016
<b>Status of the work:</b>	Work Completed
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil
<b>Whether inspection carried out from Block/DCs office:</b>	Yes, at regular intervals from Block Office.
<b>Name of executing agency:</b>	The work is executed by the School Managing Committee.
<b>Whether signboard erected or not:</b>	No
<b>Date of submission of UC:</b>	
1 <sup>st</sup> Instalment:	-----
2 <sup>nd</sup> Instalment:	
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	Yes
<b>Impact of the Scheme:</b>	Benefit for the students for conducting various programmes, awareness programmes, parent-teachers meeting, etc.
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>During inspection it has been seen that the construction of multipurpose hall is completed.</li> <li>Its dimension: Plinth area : Room: L=10.8m and B=7m Windows: (1.2*1.2)m (10nos).Door: 90cm*20cm*(2nos) - Chowkat: (15*7*410)cm. Column size: 30cm*30cm (12 nos) Beam size: 25*25cm. Store room: L=5.7m and B=3.8m.</li> <li>The quality of work is satisfactory.</li> </ol>
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G. Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L. Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
