

CONSTRUCTION OF CAPTAIN WILLIAMSON SANGMA MEMORIAL PARK,
WILLIAMNAGAR.EAST GARO HILLS

Date of inspection – 24th April, 2013

Team of inspection officers – Shri. E.B. Lyngdoh, Assistant Director, Shri. D.S. Kharpan, Assistant Director, Shri. N.R. Kharchandy, Assistant Research Officer, Shri. S. Sungoh, Assistant Research Officer and accompanied by Shri. Hitesh Medhi, Assistant Project Officer and Shri Debeswar Narzary, Junior Engineer, Williamnagar Municipality.

Name of the Scheme – Construction of Captain Williamson Sangma Memorial Park, Williamnagar.

Name of the MP – Shri Thomas A. Sangma, Ex-MP (Rajya Sabha)

Year of Sanctioned– 2013

Amount sanctioned – Rs. 25,00,000/- (Twenty five lakhs).

Date of release of fund : 1st installment amounting to Rs. 12,50,000/- released on 11.01.2013

Date of commencement/starting of the work – 30.01.2013

Date of completion/Expected date of completion :- Not yet Completed.

Status of the work – 40% completed.

Whether inspection carried out from Block/DCs Office – Block Office.

Name of executing agency – The work is executed by the Archigenesis, Tura.

Whether signboard erected or not - No

Date of submission of U.C: Utilization Certificate of the 1st installment only has not yet been submitted to the Williamnagar Municipal Board.

Completion Report/Certificate submitted to BDO/DC or not – No

Observations:-

- (i) It was found that the construction is for making fencing/ boundary wall, Amphi-theatre, Toilets, Septic Tank and a Fountain.
- (ii) It was observed that only the boundary wall, septic tank were under construction.
- (iii) It was found that the construction is very satisfactory particularly the Septic Tank which is quite big with all requirements like 3 Chambers, Soak Pit, etc.
- (iv) The Assistant Project Officer, DRDA has also been advised to inform the Archigenesis, Tura to erect a signboard indicating the name of the Scheme, name of MP, date of sanction, amount sanctioned after the construction is completed.







**CONSTRUCTION OF PRINGPRANG CULTURAL YOUTH CLUB AT WARIMAGRE,
WILLIAMNAGAR, EAST GARO HILLS**

Date of inspection – 24th April, 2013

Team of inspection officers – Shri. E.B. Lyngdoh, Assistant Director, Shri. D.S. Kharpan, Assistant Director, Shri. N.R. Kharchandy, Assistant Research Officer, Shri. S. Sungoh, Assistant Research Officer and accompanied by Shri. Hitesh Medhi, Assistant Project Officer and Shri Debeswar Narzary, Junior Engineer, Williamnagar Municipality.

Name of the Scheme – Construction of Pringprang Cultural Youth Club at Warimagre, Williamnagar.

Name of the MP – Kum. Agatha K. Sangma, MP (Lok Sabha)

Year recommended– 2012-13

Amount sanctioned – Rs. 2,00,000/- (Two lakhs).

Date of release of fund : 1st installment amounting to Rs. 1,00,000/- released on 18.05.2012 and the 2nd installment amounting to Rs 1,00,000/- released on 21.12.2012.

Amount utilized – Rs. 2,00,000/-

Date of commencement/starting of the work – 8.09.2012

Date of completion/Expected date of completion :- 29.01.2013.

Status of the work – Completed.

Whether inspection carried out from Block/DCs Office – Block Office.

Name of executing agency – The work is executed by the Pringprang Culture Youth Club, Warimagre.

Whether signboard erected or not - No

Date of submission of U.C: Utilization Certificate of the 1st installment has been submitted to the Williamnagar Municipal Board on 6.11.2013 and the Utilization Certificate of the 2nd installment also has been submitted on 22.04.2013.

Observations:-

- (i) It was found that the building was completed and utilized by the Pringprang Cultural Youth Club, Warimagre.
- (ii) It was found that the construction was an RCC Hall covered with CGI Sheet
- (iii) It was found that construction of the building is satisfactory.
- (iv) The Assistant Project Officer, DRDA has also been advised to inform the Secretary Pringprang Culture Youth Club, Warimagre to erect a signboard indicating the name of the Scheme, name of MP, date of sanction, amount sanctioned etc.



**CONSTRUCTION AND IMPROVEMENT OF UP SCHOOL BUILDING AT NENGKRA
VILLAGE, SAMANDA BLOCK, WILLIAMNAGAR, EAST GARO HILLS**

Date of inspection – 24th April, 2013

Team of inspection officers – Shri. E.B. Lyngdoh, Assistant Director, Shri. D.S. Kharpan, Assistant Director, Shri. N.R. Kharchandy, Assistant Research Officer, Shri. S. Sungoh, Assistant Research Officer and accompanied by Shri. Hitesh Medhi, Assistant Project Officer, Shri. H.N. Sangma, Junior Engineer, Samanda Block and Shri Enok Marak, Junior Engineer, Samanda Block

Name of the Scheme – Construction and Improvement of UP School building at Nengkra village.

Name of the MP – Kum. Agatha Sangma, MP (Lok Sabha)

Year – 2008-09 and 2011-12.

Amount sanctioned – Rs. 5,00,000/- (Five lakhs) and Rs. 2,00,000/- (Two lakhs).

Date of release of fund : 1st installment of Rs 2,50,000/- released on 24-02-2009, 2nd installment of Rs 2,50,000/- released on 07-10-2009/-
1st installment amounting to Rs. 1,00,000/- released on 10.03.2011 and the 2nd installment amounting to Rs 1,00,000/- released on 06.07.2011.

Amount utilized – Rs. 7,00,000/-

Date of commencement/starting of the work – 02-03-2009 and 15.03.2011

Date of completion/Expected date of completion :- 09-11-2009 and 09-.08.2011

Status of the work – Completed.

Whether inspection carried out from Block/DCs Office – Block Office.

Name of executing agency – Shri Harbirth.M.Sangma & Egilin.G.Momin


Whether signboard erected or not - Yes

Date of submission of U.C: Utilization Certificate of the 1st installment only has been submitted to the Block Development Officer, Samanda Block, East Garo Hills on 10.05.2011

Completion Report/Certificate submitted to BDO/DC or not – No

Observations:-

- (i) It was found that the building is already completed and utilized by the Managing Committee.
- (ii) It was noted that the construction was an RCC building covered with CGI Sheet. It was made in the form of a hall which had been partitioned by Plywood into three classes to provide accommodation for children studying in different classes.
- (iii) It was found that construction of the building is very satisfactory.
- (iv) The Assistant Project Officer, DRDA has been advised to inform the Chairman of the Village Construction Committee to submit the Utilisation Certificate of the 2st Installment to the Office of the BDO, Samanda Block at the earliest.

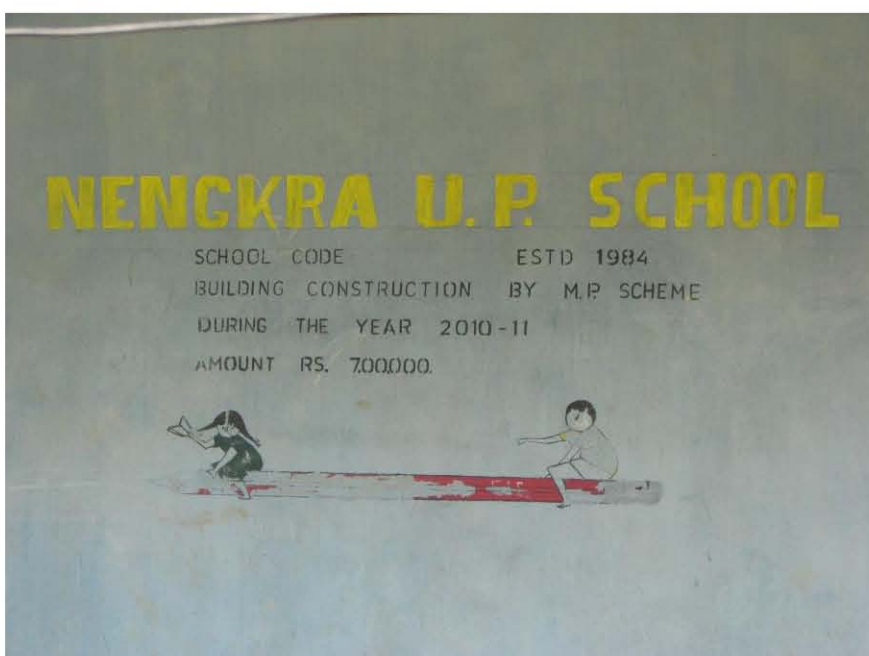

**CONSTRUCTION OF COMMUNITY HALL AT
DARIMGRE, WILLIAMNAGAR, EAST GARO HILLS.**

Date of inspection – 24th April, 2013

Team of inspection officers – Shri. E.B. Lyngdoh, Assistant Director, Shri. D.S. Kharpan, Assistant Director, Shri. N.R. Kharchandy, Assistant Research Officer, Shri. S. Sungoh, Assistant Research Officer and accompanied by Shri. Hitesh Medhi, Assistant Project Officer, Shri. H.N. Sangma, Junior Engineer, Samanda Block and Shri Enok Marak, Junior Engineer, Samanda Block

Name of the Scheme – Construction of Community Hall at Darimgre

Name of the MP – Shri Thomas A. Sangma, Ex-MP (Rajya Sabha)

Year – 2010-11

Amount sanctioned – Rs. 2,00,000/- (Two lakhs).

Date of release of fund : 1st installment amounting to Rs. 1,00,000/- released on 29.11.2011 and the 2nd installment amounting to Rs 1,00,000/- released on 27.02.2012.

Amount utilized – Rs. 2,00,000/-

Date of commencement/starting of the work – 02.12.2011

Date of completion/Expected date of completion :- 14.03.2012

Status of the work – Completed.

Whether inspection carried out from Block/DCs Office – Block Office.

Name of executing agency – The work is executed by the Village Construction Committee.

Whether signboard erected or not - No


Date of submission of U.C: Utilization Certificate of the 1st installment only has been submitted to the Block Development Officer, Samanda Block, East Garo Hills on 10.05.2011

Completion Report/Certificate submitted to BDO/DC or not – No

Observations:-

- (i) It was found that due to high cost of the materials the Village Construction Committee constructed a small Community Hall.
- (ii) It was found that the building was completed and utilized by the Village Construction Committee.
- (iii) It was noted that the construction was an RCC building covered with GI Sheet.
- (iv) It was found that the condition of the Community Hall is good.
- (v) The Assistant Project Officer, DRDA has been advised to inform the Chairman of the Village Construction Committee to submit the Utilisation Certificate of the 2st Installment to the Office of the BDO, Samanda Block at the earliest.

- (vi) The Assistant Project Officer, DRDA has also been advised to inform the Managing Committee to erect a signboard indicating the name of the Scheme, name of MP, date of sanction, amount sanctioned, etc.

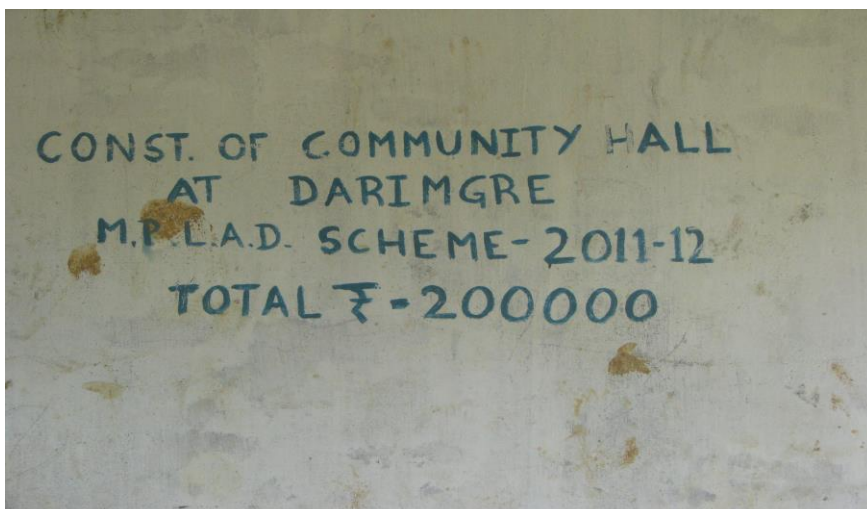

**EXTENSION OF BALSRIGHTIM SECONDARY SCHOOL BUILDING AT
BALSRIGHTIM, WILLIAMNAGAR, EAST GARO HILLS**

Date of inspection – 24th April, 2013

Team of inspection officers – Shri. E.B. Lyngdoh, Assistant Director, Shri. D.S. Kharpan, Assistant Director, Shri. N.R. Kharchandy, Assistant Research Officer, Shri. S. Sungoh, Assistant Research Officer and accompanied by Shri. Hitesh Medhi, Assistant Project Officer and Shri Debeswar Narzary, Junior Engineer, Williamnagar Municipality.

Name of the Scheme – Extension of Balsrightim Secondary School building at Balsrightim, Williamnagar.

Name of the MP – Kum. Agatha K. Sangma, MP (Lok Sabha)

Year recommended– 2010-11

Amount sanctioned – Rs. 2,00,000/- (Two lakhs).

Date of release of fund : 1st installment amounting to Rs. 1,00,000/- released on 24.06.2010 and the 2nd installment amounting to Rs 1,00,000/- released on 9.11.2010.

Amount utilized – Rs. 2,00,000/-

Date of commencement/starting of the work – 20.10.2010

Date of completion/Expected date of completion :- 16.01.2011.

Status of the work – Completed.

Whether inspection carried out from Block/DCs Office – Block Office.

Name of executing agency – The work is executed by the School Managing Committee

Whether signboard erected or not - No

Date of submission of U.C: Utilization Certificate of the 1st installment has been submitted to the Williamnagar Municipal Board on 24.09.2010 and the Utilization Certificate of the 2nd installment also has been submitted on 4.10.2012.

Observations:-

- (i) It was found that the building was completed and utilized by the Managing Committee.
- (ii) It was found that the construction was an RCC building covered with GI Sheet. 1 (one) classroom only was constructed to provide accommodation for the children.
- (iii) It was found that construction of the building is good.
- (iv) The Assistant Project Officer, DRDA has also been advised to inform the Managing Committee to erect a signboard indicating the name of the Scheme, name of MP, date of sanction, amount sanctioned etc.



**CONSTRUCTION OF COMMUNITY HALL AT DAMAGRE, WILLIAMNAGAR, EAST
GARO HILLS**

Date of inspection – 24th April, 2013

Team of inspection officers – Shri. E.B. Lyngdoh, Assistant Director, Shri. D.S. Kharpan, Assistant Director, Shri. N.R. Kharchandy, Assistant Research Officer, Shri. S. Sungoh, Assistant Research Officer and accompanied by Shri. Hitesh Medhi, Assistant Project Officer, Shri. H.N. Sangma, Junior Engineer, Samanda Block and Shri Enok Marak, Junior Engineer, Samanda Block

Name of the Scheme – Construction of Community Hall at Damagre.

Name of the MP – Shri Thomas A. Sangma, Ex-MP (Rajya Sabha)

Year – 2010-11

Amount sanctioned – Rs. 3,00,000/- (Three lakhs).

Date of release of fund : 1st installment amounting to Rs. 1,50,000/- released on 13.07.2012 and the 2nd installment amounting to Rs 1,50,000/- released on 03.02.2013.

Amount utilized – Rs. 3,00,000/-

Date of commencement/starting of the work – 17.07.2012

Date of completion/Expected date of completion :- 20.12.2012

Status of the work – Completed.

Whether inspection carried out from Block/DCs Office – Block Office.

Name of executing agency – The work is executed by the Village Construction Committee.

Whether signboard erected or not - No

Date of submission of U.C: Utilization Certificate of the 1st installment only has been submitted to the Block Development Officer, Samanda Block, East Garo Hills on 21.12.2012

Completion Report/Certificate submitted to BDO/DC or not – No

Observations:-

- (i) It was observed that the Scheme was allotted for construction of community Hall at Damagre but due to mis-understanding among the people of the village, the village was divided into two villages and the scheme was shifted to another side of the village. After the completion of the construction of the community Hall, the Damagre village was divided into two parts viz. Samgong and Damagre. It was found out that the Community Hall was constructed at the location of Upper Samgong.
- (ii) It was observed that many schemes were combined/converged for construction of the Community Hall in the same roof due to less sanction. Some money was given from MLA & MDC Scheme to complete the construction.
- (iii) The Assistant Project Officer, DRDA has been advised to inform the Chairman of the Village Construction Committee to submit the Utilisation Certificate of the 2st Installment to the Office of the BDO, Samanda Block at the earliest.

- (iv) The Assistant Project Officer, DRDA has also been advised to inform the Managing Committee to erect a signboard indicating the name of the Scheme, name of MP, date of sanction, amount sanctioned, etc.



METALLING AND BLACK TOPPING OF ROAD FROM LOYLA SECONDARY SCHOOL CONNECTING DAWA NENGJA VILLAGE, WILLIAMNAGAR, EAST GARO HILLS

Date of inspection – 24th April, 2013

Team of inspection officers – Shri. E.B. Lyngdoh, Assistant Director, Shri. D.S. Kharpan, Assistant Director, Shri. N.R. Kharchandy, Assistant Research Officer, Shri. S. Sungoh, Assistant Research Officer and accompanied by Shri. Hitesh Medhi, Assistant Project Officer, Shri. H.N. Sangma, Junior Engineer, Samanda Block and Shri Enok Marak, Junior Engineer, Samanda Block

Name of the Scheme – Metalling and black topping of road from Loyla Secondary School connecting Dawa Nengja village

Name of the MP – Shri Thomas A. Sangma, Ex-MP (Rajya Sabha)

Year – 2010-11

Amount sanctioned – Rs. 10,00,000/- (Ten lakhs).

Date of release of fund : 1st installment amounting to Rs. 5,00,000/- released on 13.07.2012 and the 2nd installment amounting to Rs 5,00,000/- released on 20.09.2012.

Amount utilized – Rs. 10,00,000/-

Date of commencement/starting of the work – 17.07.2012

Date of completion/Expected date of completion :- 15.10.2012

Status of the work – Completed.

Whether inspection carried out from Block/DCs Office – Block Office.

Name of executing agency – The work is executed by the Village Construction Committee.

Whether signboard erected or not - No

Date of submission of U.C: Utilization Certificate of the 1st installment only has been submitted to the Block Development Officer, Samanda Block, East Garo Hills on 03.09.2012.

Completion Report/Certificate submitted to BDO/DC or not – No

Observations:-

- (i) It was found out that the length of the motorable road is 500 metres (approx)
- (ii) It was informed that the motorable road was constructed entirely of cement due to steep incline of the road and a Road Roller would not be able to roll the road if it was a metalled road.
- (iii) It was found that construction of the road is satisfactory.
- (iv) The Junior Engineer has been advised to inform the Village Construction Committee to submit the Utilisation Certificate of the 2st Installment to the Office of the BDO, Samanda Block at the earliest.
- (v) The Junior Engineer has also been advised to inform the Village Construction Committee to erect a signboard indicating Name of the Scheme, Name of MP, Date of Sanction, Amount sanctioned, etc.



**CONSTRUCTION OF LOYLA COLLEGE BUILDING AT WILLIAMNAGAR,EAST
GARO HILLS**

Date of inspection – 24th April, 2013

Team of inspection officers – Shri. E.B. Lyngdoh, Assistant Director, Shri. D.S. Kharpan, Assistant Director, Shri. N.R. Kharchandy, Assistant Research Officer, Shri. S. Sungoh, Assistant Research Officer and accompanied by Shri. Hitesh Medhi, Assistant Project Officer and Shri Debeswar Narzary, Junior Engineer, Williamnagar Municipality.

Name of the Scheme – Construction of Loyla College building at Williamnagar

Name of the MP – Kum. Agatha K. Sangma, MP (Lok Sabha)

Year recommended– 2010-11

Amount sanctioned – Rs. 10,00,000/- (Ten lakhs).

Date of release of fund : 1st installment amounting to Rs. 5,00,000/- released on 7.02.2012 and the 2nd installment amounting to Rs 5,00,000/- released on 30.05.2012.

Amount utilized – Rs. 10,00,000/-

Date of commencement/starting of the work – 9.02.2012

Date of completion/Expected date of completion :- 20.08.2012.

Status of the work – Completed.

Whether inspection carried out from Block/DCs Office – Block Office.

Name of executing agency – The work is executed by the Loyla College, Williamnagar.

Whether signboard erected or not - No

Date of submission of U.C: Utilization Certificate of the 1st installment only has been submitted to the Williamnagar Municipal Board on 27.04.2012 and the Utilization Certificate of the 2nd installment also has been submitted to the Williamnagar Municipal Board on 24.08.2012.

Completion Report/Certificate submitted to BDO/DC or not – No

Observations:-

- (i) It was found that the Managing Committee of Loyla College had obtained the approval of the MP for changing the name of the scheme from Construction of Loyla College building to Construction of Brick Boundary wall due to insufficient funds sanctioned for Construction of the College Building
- (ii) It was found that the construction of the brick boundary wall is very satisfactory.
- (iii) The Assistant Project Officer, DRDA has also been advised to inform the Managing Committee of Loyla College to erect a signboard indicating the name of the Scheme, name of MP, date of sanction, amount sanctioned etc.

