


## CONSTRUCTION OF A COLLEGE BUILDING FOR RONGJENG COLLEGE



<b>Date of Inspection:</b>	28 <sup>th</sup> November 2017.	
<b>Team of inspection officers:</b>	Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer	
<b>Accompanied by:</b>	Shri Hitesh Medhi, Addl. Programme Officer, DRDA Williamnagar.	
<b>Name of the Scheme:</b>	Construction of a College Building for Rongjeng College	
<b>Name of the MP:</b>	Shri P.A. Sangma, MP(LS)	
<b>Year recommended/sanctioned:</b>	2014-15	
<b>Amount &amp; Date of sanctioned by the DC:</b>	Rs. 10,00,000/- sanctioned on 29 <sup>th</sup> June 2015.	
<b>Reason for delay of sanction, if any:</b>	Nil	
<b>Date of release of fund:</b>		
1 <sup>st</sup> instalment :-	Rs. 6,00,000/-	
2 <sup>nd</sup> instalment :-	Rs. 2,50,000/-	
<b>Reason for delay in release of fund, if</b>	Nil	
<b>Amount utilized:</b>	Rs. 8,50,000/-	
<b>Date of commencement/starting of the work:</b>	20 <sup>th</sup> August 2015	
<b>Date of completion/Expected date of completion:</b>	Work in progress	
<b>Status of the work:</b>	Work in progress	
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil	
<b>Whether inspection carried out from Block/DCs office:</b>	-----	
<b>Name of executing agency:</b>	The work is executed by the Managing Committee, College Building, Rongjeng	
<b>Whether signboard erected or not:</b>	No	
<b>Date of submission of UC:</b>		
1 <sup>st</sup> Instalment:	Submitted to BDO, Rongjeng C&RD Block on 10 <sup>th</sup> February 2016.	
2 <sup>nd</sup> Instalment:	-----	
<b>In case of completed Scheme whether the completion Report/ Certificate submitted to BDO/DC:</b>	-----	
<b>Impact of the scheme:</b>	It will have a positive impact on the students and community, high academic standards, teacher motivation and higher student achievements.	
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>1. During inspection the team found that the construction of a College Building is in progress.</li> <li>2. The work that has been completed are Columns Footing, Columns, Beams, Brick walling, Window fitting, Chowkat fitting. The remaining works are Plastering, Flooring, Door, Roofing and Painting.</li> <li>3. Its dimension:-ff Plinth area: L=14.30m and B=5.10m-----Column size (15 nos): (20*24) cm. Windows: (160*130)cm * 8nos-----chowkat (4 nos): (7*3*480)cm Tie beam: (25*25) cm.</li> <li>4. The Addl. Programme Officer, DRDA Williamnagar has been advised to inform Managing Committee and also to advise to erect a signboard with full complete details of the scheme mentioning the name of the MP, year and date of sanctioned, amount sanctioned,. etc. on completion of the Schemes.</li> <li>5. Necessary action should be taken up from the Block Office regarding the erection of the plague and also the functioning of each and every MPLAD scheme.</li> </ol>	

## CONSTRUCTION OF DARUGRE SECONDARY SCHOOL BUILDING AT DARUGRE

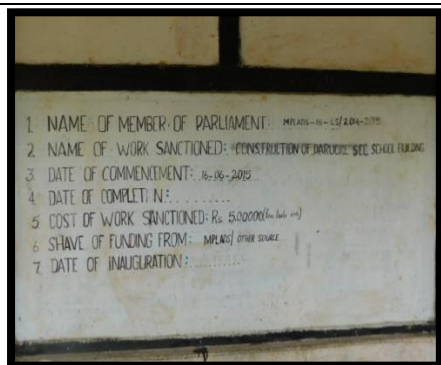

<b>Date of Inspection:</b>	28 <sup>th</sup> November 2017	
<b>Team of inspection officers:</b>	Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer	
<b>Accompanied by:</b>	Shri Hitesh Medhi, Addl. Programme Officer, DRDA Williamnagar.	
<b>Name of the Scheme:</b>	Construction of Darugre Secondary School Building at Darugre	
<b>Name of the MP:</b>	Shri P.A. Sangma, MP(LS)	
<b>Year recommended/sanctioned:</b>	2014-15	
<b>Amount &amp; Date of sanctioned by the DC:</b>	Rs 5,00,000/- sanctioned on 30 <sup>th</sup> April 2015.	
<b>Reason for delay in sanction, if any:</b>	Nil	
<b>Date of release of fund:</b>		
1 <sup>st</sup> instalment :-	Rs. 3,00,000/-	
2 <sup>nd</sup> instalment :-	Rs. 1,50,000/-	
3 <sup>rd</sup> instalment :-	Rs. 75,000/-	
<b>Reason for delay in release of fund, if any:</b>	Nil	
<b>Amount utilized:</b>	Rs. 5,00,000/-	
<b>Date of commencement/starting of the work:</b>	25 <sup>th</sup> June 2015.	
<b>Date of completion/Expected date of completion:</b>	15 <sup>th</sup> April 2017.	
<b>Status of the work:</b>	Completed	
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil	
<b>Whether inspection carried out from Block/DCs office:</b>	----	
<b>Name of executing agency:</b>	The work is executed by the Managing Committee, Sec School building, Darugre	
<b>Whether signboard erected or not:</b>	No	
<b>Date of submission of UC:</b>		
1 <sup>st</sup> Instalment:	Submitted to BDO, Rongjeng C&RD Block on 14 <sup>th</sup> December 2015.	
2 <sup>nd</sup> Instalment:	Submitted to BDO, Rongjeng C&RD Block on 13 <sup>th</sup> December 2016.	
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	----	
<b>Impact of the scheme:</b>	Positive impact on the students and community, setting higher academic standards, teacher motivation and higher student achievements.etc.	
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>During inspection the team found out that the construction of a School Building is completed and utilized by the Managing Committee as Classroom. It consist of 2 (two) classrooms.</li> <li>Its dimension: Plinth Area: L=22.20m and B=8.30m-----Plinth height: 50cm. Door: H=190cm and B=90cm. Windows (5nos): H=90cm and B=90cm.</li> <li>The Addl. Programme Officer, DRDA Williamnagar has been advised to inform the School Managing Committee to make a correction on a signboard with full complete details of the scheme mentioning the name of the MP, year and date of sanctioned, amount sanctioned, etc.</li> </ol>	


**CONSTRUCTION OF BUILDING FOR NONGCHRAM SECONDARY SCHOOL NONGCHRAM**



<b>Date of Inspection:</b>	28 <sup>th</sup> November 2017	
<b>Team of inspection officers:</b>	Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer	
<b>Accompanied by:</b>	Shri Hitesh Medhi, Addl. Programme Officer, DRDA Williamnagar.	
<b>Name of the Scheme:</b>	Construction of Building for Nongchram Secondary School Nongchram	
<b>Name of the MP:</b>	Shri P.A. Sangma, MP(LS)	
<b>Year recommended/sanctioned:</b>	2014-15	
<b>Amount &amp; Date of sanctioned by the DC:</b>	Rs. 5,00,000/- sanctioned on 30 <sup>th</sup> April 2015.	
<b>Reason for delay in sanction, if any:</b>	Nil	
<b>Date of release of fund:</b>		
1 <sup>st</sup> instalment :-	Rs. 3,00,000/-	
2 <sup>nd</sup> instalment :-	Rs. 1,50,000/-	
3 <sup>rd</sup> instalment :-	Rs. 75,000/-	
<b>Reason for delay in release of fund, if any:</b>	Nil	
<b>Amount utilized:</b>	Rs. 5,00,000/-	
<b>Date of commencement/starting of the work:</b>	20 <sup>th</sup> June 2015	
<b>Date of completion/Expected date of completion:</b>	5 <sup>th</sup> April 2017	
<b>Status of the work:</b>	Completed	
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil	
<b>Whether inspection carried out from Block/DCs office:</b>	-----	
<b>Name of executing agency:</b>	The work is executed by the Managing Committee, Sec. School, Nongchram	
<b>Whether signboard erected or not:</b>	Yes	
<b>Date of submission of UC:</b>		
1 <sup>st</sup> Instalment:	Submitted to BDO, Rongjeng C&RD Block on 14 <sup>th</sup> December 2015.	
2 <sup>nd</sup> Instalment:	Submitted to BDO, Rongjeng C&RD Block on 24 <sup>th</sup> October 2016.	
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	-----	
<b>Impact of the Scheme:</b>	Positive impact on the students and community, setting higher academic standards, teacher motivation and higher student achievements.etc	
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>During inspection the team found that the construction of a School Building is completed. It was constructed with good quality materials.</li> <li>It consists of 3 (three) rooms i.e One Teacher rooms and two Classrooms.</li> <li>Its dimension: Plinth Area L=8.20m and B=5.10m -----Veranda: L=8.20m and B=1.90m Plinth Height: 90cm-----Windows (3nos): H=110cm and B=85cm. Door: H=185cm B=90cm-----chowkat: (10*6* 450) cm.</li> <li>The School Managing Committee has been advised to make a correction on a signboard with full complete details of the scheme mentioning the name of the MP, year and date of sanctioned, amount sanctioned, etc.</li> </ol>	



## CONSTRUCTION OF HANGING BRIDGE AT KOKSI GITTIM

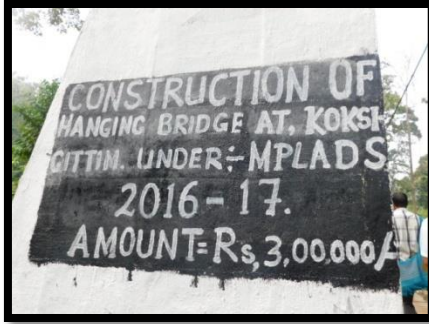

<b>Date of Inspection:</b>	28 <sup>th</sup> November 2017	
<b>Team of inspection officers:</b>	Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer	
<b>Accompanied by:</b>	Shri Hitesh Medhi, Addl. Programme Officer, DRDA Williamnagar.	
<b>Name of the Scheme:</b>	Construction of Hanging Bridge at Koksi Gittim	
<b>Name of the MP:</b>	Shri Conrad K. Sangma, MP(LS)	
<b>Year recommended/sanctioned:</b>	2016-17	
<b>Amount &amp; Date of sanctioned by the DC:</b>	Rs.3,00,000/- sanctioned on 8 <sup>th</sup> August 2017	
<b>Reason for delay in sanction, if any:</b>	Nil	
<b>Date of release of fund:</b> 1 <sup>st</sup> instalment :- 2 <sup>nd</sup> instalment :-	Rs. 1,80,000/- released from Block Office on 22 <sup>nd</sup> August 2017. -----	
<b>Reason for delay in release of fund, if any:</b>	Nil	
<b>Amount utilized:</b>	Rs. 1,80,000/-	
<b>Date of commencement/starting of the work:</b>	1 <sup>st</sup> October 2017	
<b>Date of completion/Expected date of completion:</b>	-----	
<b>Status of the work:</b>	80% Work in progress	
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil	
<b>Whether inspection carried out from Block/DCs office:</b>	-----	
<b>Name of executing agency:</b>	The work is executed by the Managing Committee, Hanging Bridge, Koksigtimm	
<b>Whether signboard erected or not:</b>	Yes	
<b>Date of submission of UC:</b> 1 <sup>st</sup> instalment :- 2 <sup>nd</sup> instalment :-	Submitted to BDO, Rongjeng C&RD Block on 27 <sup>th</sup> November 2017. -----	
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	-----	
<b>Impact of the Scheme:</b>	Benefit for the localities to access across the river.	
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>1. On Inspection it has been seen that construction of a Hanging Bridge is under progress.</li> <li>2. It also has been observed that the bridge deck fitted with teak wood plank, white washing of Bridge Columns are completed.</li> <li>3. The remaining works are Hand Railing fitted with mesh wire and painting.</li> <li>4. Its dimension: Bridge: L=50m and B=1.90m-----Railing: L=50m (both sides) H= 1.20m</li> <li>5. The Managing Committee has been advised to make a correction on a plaque with full complete details of the scheme which include the name of the MP, year and date of sanctioned, amount sanctioned,. etc.</li> </ol>	

**FINANCIAL ASSISTANCE FOR PROCUREMENT OF TENT HOUSE IN FAVOUR OF LOCAL DEVELOPMENT COMMITTEE  
AT RONGJENG**



<b>Date of Inspection:</b>	28 <sup>th</sup> November 2017	
<b>Team of inspection officers:</b>	Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer	
<b>Accompanied by:</b>	Shri Hitesh Medhi, Addl. Programme Officer, DRDA Williamnagar.	
<b>Name of the Scheme:</b>	Financial Assistance for Procurement of Tent House in favour of Local Development Committee at Rongjeng	
<b>Name of the MP:</b>	Shri Conrad K. Sangma, MP(LS)	
<b>Year recommended/sanctioned:</b>	2016-17	
<b>Amount &amp; Date of sanctioned by the DC:</b>	Rs. 4,00,000/- sanctioned on 14 <sup>th</sup> August 2017.	
<b>Reason for delay in sanction, if any:</b>	Nil	
<b>Date of release of fund:</b> 1 <sup>st</sup> instalment :- 2 <sup>nd</sup> instalment :-	Rs. 2,40,000/- released from Block Office on 29 <sup>th</sup> August 2017. -----	
<b>Reason for delay in release of fund, if any:</b>	Nil	
<b>Amount utilized:</b>	Rs. 2,40,000/-	
<b>Date of commencement/starting of the work:</b>	1 <sup>st</sup> October 2017	
<b>Date of completion/Expected date of completion:</b>	-----	
<b>Status of the work:</b>	Completed	
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil	
<b>Whether inspection carried out from Block/DCs office:</b>	-----	
<b>Name of executing agency:</b>	The work is executed by the Managing Committee, Local Dev. Committee, Tent House, Rongjeng	
<b>Whether signboard erected or not:</b>	No	
<b>Date of submission of UC:</b> 1 <sup>st</sup> instalment :- 2 <sup>nd</sup> instalment :-	Submitted to BDO, Rongjeng C&RD Block on 27 <sup>th</sup> November 2017. -----	
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	-----	
<b>Impact of the Scheme:</b>	Benefit for Localities.	
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>1. During inspection the team found that the procurement of Tent House is completed.</li> <li>2. It has been observed that there are 10 (ten) no's of Tent, 4 (four) no's of Sound System with amplifier, 10 (ten) no's of Bamboo support, 10 (ten) no's of support GI Pipes.</li> <li>3. The Managing Committee has been advised to make a signboard with a full complete details of the scheme mentioning the name of the MP, year and date of sanctioned, amount sanctioned, etc. and also submit the UCs and Photographs to release the 2<sup>nd</sup> instalment.</li> </ol>	

**FINANCIAL ASSISTANCE FOR EXTENSION OF HIGHER SECONDARY SCHOOL BUILDING AT RONGJENG**



<b>Date of Inspection:</b>	28 <sup>th</sup> November 2017	
<b>Team of inspection officers:</b>	Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer	
<b>Accompanied by:</b>	Shri Hitesh Medhi, Addl. Programme Officer, DRDA Williamnagar.	
<b>Name of the Scheme:</b>	Financial Assistance for Extension of Higher Secondary School Building at Rongjeng	
<b>Name of the MP:</b>	Shri Conrad K. Sangma, MP(LS).	
<b>Year recommended/sanctioned:</b>	2016-17	
<b>Amount &amp; Date of sanctioned by the DC:</b>	Rs. 5,00,000/- sanctioned on 28 <sup>th</sup> August 2017.	
<b>Reason for delay in sanction, if any:</b>	Nil	
<b>Date of release of fund:</b>		
<b>1<sup>st</sup> instalment :-</b>	Rs. 3,00,000/- released from Block Office on 31 <sup>st</sup> August 2017.	
<b>2<sup>nd</sup> instalment :-</b>	-----	
<b>Reason for delay in release of fund, if any:</b>	Nil	
<b>Amount utilized:</b>	Rs. 3,00,000/-	
<b>Date of commencement/starting of the work:</b>	1 <sup>st</sup> October 2017.	
<b>Date of completion/Expected date of completion:</b>	-----	
<b>Status of the work:</b>	Completed	
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil	
<b>Whether inspection carried out from Block/DCs office:</b>	-----	
<b>Name of executing agency:</b>	The work is executed by the Managing Committee, Higher Sec. School Building, Rongjeng	
<b>Whether signboard erected or not:</b>	No	
<b>Date of submission of UC:</b>		
<b>1<sup>st</sup> Instalment:</b>	Submitted to BDO, Rongjeng C&RD Block on 27 <sup>th</sup> November 2017.	
<b>2<sup>nd</sup> Instalment:</b>	-----	
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	-----	
<b>Impact of the Scheme:</b>	Accommodation for students for better education.	
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>On inspection it has been seen that the Extension of the school building is completed. It is covered with CGI sheet roof with usage of good quality materials.</li> <li>It also has been observed that some extra works that has been executed are repairing of roofing and replacing of Doors (2nos) window and s (4nos).</li> <li>Its dimension:                      Room: L=5.60m and B=3.50m -----Veranda: L=3.50m and B=1.80m                      Windows (6 nos): (90*120) cm. -----Door (3nos): (90*190) cm                      chowkat: (60*10*480)cm</li> <li>The School Managing Committee has been advised to erect a signboard with a full complete details of the scheme which include the name of the MP, year and date of sanctioned, amount sanctioned,. etc. and also to submit the UCs and Photographs for releasing of the 2<sup>nd</sup> instalment.</li> </ol>	



**CONSTRUCTION OF LOCALITY ADMINISTRATIVE BUILDING AT RONGJENG**



<b>Date of Inspection:</b>	28 <sup>th</sup> November 2017.	
<b>Team of inspection officers:</b>	Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer	
<b>Accompanied by:</b>	Shri Hitesh Medhi, Addl. Programme Officer, DRDA Williamnagar.	
<b>Name of the Scheme:</b>	Construction of Locality Administrative Building at Rongjeng	
<b>Name of the MP:</b>	Shri Conrad K. Sangma, MP(LS)	
<b>Year recommended/sanctioned:</b>	2016-17	
<b>Amount &amp; Date of sanctioned by the DC:</b>	Rs. 4,00,000/- sanctioned on 14 <sup>th</sup> August 2017.	
<b>Reason for delay in sanction, if any:</b>	Nil	
<b>Date of release of fund:</b>		
<b>1<sup>st</sup> instalment :-</b>	Rs. 2,40,000/- released from Block Office on 29 <sup>th</sup> August 2017.	
<b>2<sup>nd</sup> instalment :-</b>	-----	
<b>Reason for delay in release of fund, if any:</b>	Nil	
<b>Amount utilized:</b>	Rs. 2,40,000/-	
<b>Date of commencement/starting of the work:</b>	25 <sup>th</sup> August 2017.	
<b>Date of completion/Expected date of completion:</b>	-----	
<b>Status of the work:</b>	60% Work in Progress.	
<b>Cause/Reason for delay in sanction/completion of works:</b>	Nil	
<b>Whether inspection carried out from Block/DCs office:</b>	-----	
<b>Name of executing agency:</b>	The work is executed by the Managing Committee, Locality Adm. Building, Rongjeng	
<b>Whether signboard erected or not:</b>	No	
<b>Date of submission of UC:</b>		
<b>1<sup>st</sup> Instalment:</b>	U/C not yet received.	
<b>2<sup>nd</sup> Instalment:</b>		
<b>In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:</b>	-----	
<b>Impact of the Scheme:</b>	Benefits for the locality.	
<b>Findings/Observations:</b>	<ol style="list-style-type: none"> <li>During inspection the team found that the Construction of the Administrative Building is under progress. Structural works are completed.</li> <li>The remaining works are walling, plastering, flooring, painting, and fitting doors, windows and glass pane.</li> <li>Its dimension: Plinth area: L=15m and B=7.40m-----Column size (10 nos): (45cm*30cm). Tie beam: 30cm*30cm-----Plinth Height: 55cm-----Slab thickness: 100mm.</li> <li>The Local Development Committee has been advised to submit U/Cs, Photographs and also to erect a plaque with a full complete details of the scheme, mentioning the name of the MP, year and date of sanctioned, amount sanctioned,. etc. when the scheme is completed.</li> </ol>	
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-	
Shri R.M.G. Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-	
Shri L.L.L. Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-	
