

CONSTRUCTION OF AUDITORIUM AT KHLIEHRIAT WEST



Date of Inspection: 31/05/2019

Team of Inspection Officers: Shri E.B. Lyngdoh, Deputy Director, Shri S. Sungoh, Research Officer, Shri R.G.M Nongtdu, Executive Engineer and Shri L.R.D. Jyrwa, Junior Engineer accompanied by Shri R. Daw, Assistant Engineer and Shri E. Rymbai, Gram Sevak.

Name of the Scheme: Construction of Auditorium at Khliehriat West.

Name of the MP: Shri Vincent H. Pala, MP (Lok Sabha).

Year recommended/sanctioned: 2016-17.

Amount & Date of sanction by the DC: Rs. 25,00,000/- sanctioned on 02/05/2016.

Reason for delay of sanction, if any: NIL.

Amount & Date of release of fund:

1st installment - Rs. 12,50,000/- released from Block Office on 21/04/2017.
2nd installment - NIL.

Reason for delay in release of fund, if any: Due to delay in finalisation of site by the Executing Agency.

Amount utilized: Rs. 12,50,000/-

Date of commencement/starting of the work: 15/02/2018.

Date of completion/Expected date of completion:-

Status of the work: Work in progress.

Cause/Reason for delay in sanction/completion of works:- Nil

Whether inspection carried out from Block/DCs office: Yes, at regular intervals from Block Office.

Name of executing agency: The work is executed by the Local Committee, Khliehriat West Village.

Whether signboard erected or not: No.

Date of submission of UC:

1st installment -Submitted to the BDO Khliehriat C&RD Block on 24/04/2019.

2nd installment -

Impact of the scheme: The construction of Auditorium will enable the Local Dorbar Shnong to conduct various Social & Cultural activities and since it is located in the District Headquarter it can also be used for conducting various functions and awareness programmes, etc.

Findings/Observations:

1. The inspection team found that the construction of the Auditorium at Khliehriat West is under progress.
2. It is seen that the Construction is completed upto plinth level only and there are 18 numbers of columns out of which 6 numbers are being casted.
3. It was found that the quality of construction of the building was very good and the structure is very strong and it appears that the fund was rightly used for the purpose.
4. Its dimension:
 - a. Plinth area, Length= 21.5m & Breadth= 11.8m
 - b. Plinth Height = 60cm.
 - c. Columns = 18 nos with size (30*45) cm.
 - d. Nos of bar used in columns:
 - i. 4 nos of 20 mm dia.
 - ii. 6 nos of 16 mm dia.
 - iii. 10mm dia ties.
 - e. Beam size = 30cm*40cm.
5. The Village Secretary who represented the Local Committee has been advised to speed up the work and also to erect a plaque with full complete details of the scheme as per Guidelines after completion of the scheme.
6. It was observed that since the scheme will not be completed as per the Guidelines, it is necessary from the Block office to conduct regular inspection for completion of the scheme. The Assistant Engineer of the Block was advised to take up the matter with the Local Committee for completion of the scheme.

**CONSTRUCTION OF AUDITORIUM AT DON BOSCO COLLEGE (ST ANTHONYS COLLEGE
EXTN.) BYNDIHATI WITH TRUSSLESS ROFTING SYSTEM**



Date of Inspection: 31/05/2019

Team of Inspection Officers: Shri E.B. Lyngdoh, Deputy Director, Shri S. Sungoh, Research Officer, Shri R.G.M Nongtdu, Executive Engineer and Shri L.R.D. Jyrwa, Junior Engineer accompanied by Shri R. Daw, Assistant Engineer and Shri E. Rymbai, Gram Sevak.

Name of the Scheme: Construction of Auditorium at Don Bosco College (St Anthony's College Extn.) Byndihati with trussless roofing system.

Name of the MP: Shri Vincent H. Pala, MP (Lok Sabha).

Year recommended/sanctioned: 2017-18.

Amount & Date of sanctioned by the DC: Rs. 32,00,000/- sanctioned on 21/08/2017.

Reason for delay of sanction, if any: NIL.

Amount & Date of release of fund:

1st installment - Rs. 16,00,000/- released from Block Office on 07/08/2018.
2nd installment - Rs. 16,00,000/- released from Block Office on 30/11/2018.

Reason for delay in release of fund, if any: NIL.

Amount utilized: Rs. 32,00,000/-

Date of commencement/starting of the work: 18/04/2018.

Date of completion/Expected date of completion: 20/11/2018.

Status of the work: Completed.

Cause/Reason for delay in sanction/completion of works: NIL.

Whether inspection carried out from Block/DCs office: Yes, at regular intervals from Block Office.

Name of executing agency: The work is executed by the Principal & Secretary, Governing Body ,
St Anthony's College, Shillong.

Whether signboard erected or not: Yes.

Date of submission of UC:

1st installment - Submitted to the BDO Khliehriat C&RD Block on 12/10/2018.

2nd installment - Submitted to the BDO, Khliehriat C&RD Block on 10/12/2018.

In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC: Yes

Impact of the scheme: The construction of Auditorium will benefit the students for their various needs like awareness programmes, award ceremonies, dramatic plays, concert performance, dancing competition etc. which helps in updating the knowledge of the students and to showcase their talents.

Findings/Observations:

1. The inspection team found that the construction of the Auditorium at Don Bosco College is completed. It has also been observed that the Auditorium is constructed on the top floor (3rd floor) of the college building.
2. The Principal & Secretary, Governing Body Don Bosco College informed that to expedite early completion of the Auditorium, the Committee had already spent from their own funds while awaiting for the 2nd instalment from the Block Office.
3. It was also informed by the Principal that for installation of Trussless Roofing a Crane was hired that charged Rs 4.00 lakhs @ Rs 1.00 lakh per day and the installation was completed in 4 (Four) days.
4. It was observed that the quality of construction is very good. The workmanship is of the best quality with usage of quality and durable materials.
5. The roof is constructed with a trussless roofing system which is water proof, tamper proof, rust resistant and does not require any trusses for its support besides space saving. It was informed by the Principal that it is the first of its kind ever to be constructed in North East India.
6. Its dimension:
 - a. Auditorium Plinth area L= 34m & B= 15.7m
 - b. Stage step of a Podium, L = 11.8m & Riser = 15cm (5 nos of steps)
 - c. Stage, L = 15.7m & B = 7.4m.
 - d. Sliding Aluminium windows (24 nos) with Height = 1.2m and Length=1.8m.
 - e. Transom windows (24 nos) with Height = 50cm and B=180cm.

**CONSTRUCTION AND IMPROVEMENT OF FOOTBALL PLAYGROUND AT DONG
UMSNAGAT SPORT CLUB, BYNDIHATI, EAST JAINTIA HILLS**



Date of Inspection: 31/05/2019

Team of Inspection Officers: Shri E.B. Lyngdoh, Deputy Director, Shri S. Sungoh, Research Officer, Shri R.G.M Nongtdu, Executive Engineer and Shri L.R.D. Jyrwa, Junior Engineer accompanied by Shri R. Daw, Assistant Engineer and Shri E. Rymbai, Gram Sevak.

Name of the Scheme: Construction and Improvement of Football Playground at Dong Umsngat Sport Club, Byndihati, East Jaintia Hills.

Name of the MP: Smt. Wansuk Syiem, MP (Rajya Sabha).

Year recommended/sanctioned: 2017-18.

Amount & Date of sanctioned by the DC: Rs. 50,00,000/- sanctioned on 13/06/2017.

Reason for delay of sanction, if any: NIL.

Amount & Date of release of fund:

1st installment - Rs. 25,00,000/- released from Block Office on 22/12/2017.

2nd installment - Not yet released.

Reason for delay in release of fund, if any: NIL.

Amount utilized: Rs. 25,00,000/-

Date of commencement/starting of the work: 22/12/2017.

Date of completion/Expected date of completion:-

Status of the work: Work in progress.

Cause/Reason for delay in sanction/completion of works: NIL.

Whether inspection carried out from Block/DCs office: Yes, at regular intervals from Block Office.

Name of executing agency: The work is executed by the Local Committee, Dong Umsngat Sports Club, Byndihati.

Whether signboard erected or not: No.

Date of submission of UC:

1st installment - Submitted to the BDO Khliehriat C&RD Block on 25/03/2019.

2nd installment - Not yet submitted.

Impact of the scheme: The availability of Playground will benefit the local people and the school students of nearby schools who can use it for their needs like holding football tournaments, fetes, etc.,

Findings/Observations:

1. The inspection team found that the construction and improvement of the football playground is under progress.
2. It is seen that earth filling, compaction for the playground is completed which was done by JCB Machine as informed by the Chairman, Local Committee. The construction of side drain is completed and construction of sitting gallery is under progress.
3. Its dimension:
 - a. Playground, Length = 150m & Breadth= 112m.
 - b. PCC Side drain, L= 333m, H = 50cm&B = 40cm.
 - c. Slab drain cover, L = 335m B = 75cm, & Depth = 100mm.
 - d. Sitting Gallery, L = 240m, Thread = 55cm & Riser = 50cm.
 - e. Earth work excavation blasting (very hard rock), L = 52m & H = 3m.
4. The Chairman, Local Committee has been advised to submit the Utilization Certificate and Photographs of 1st instalment to the Block office at the earliest to demand the 2nd Instalment.
5. The Local Committee has been advised to speed up the work and also to erect a plaque with full complete details of the scheme as per Guidelines after completion of the scheme.

**CONSTRUCTION AND EXTENSION OF THE AMBROSE MEMORIAL SECONDARY SCHOOL
BUILDING AT KHLIEHRIAT, EAST JAINTIA HILLS**



Date of Inspection: 31/05/2019

Team of Inspection Officers: Shri E.B. Lyngdoh, Deputy Director, Shri S. Sungoh, Research Officer, Shri R.G.M Nongtdu, Executive Engineer and Shri L.R.D. Jyrwa, Junior Engineer accompanied by Shri R. Daw, Assistant Engineer and Shri E. Rymbai, Gram Sevak.

Name of the Scheme: Construction and Extension of the Ambrose Memorial Secondary School Building at Khliehriat, East Jaintia Hills.

Name of the MP: Smt. Wansuk Syiem, MP (Rajya Sabha).

Year recommended/sanctioned: 2018-19.

Amount & Date of sanctioned by the DC: Rs. 50,00,000/- sanctioned on 01/05/2018.

Reason for delay of sanction, if any: NIL.

Amount & Date of release of fund:

1st installment - Rs. 25,00,000/- released from Block Office on 11/12/2018.

2nd installment - Not yet released.

Reason for delay in release of fund, if any: NIL.

Amount utilized: Rs. 25,00,000/-

Date of commencement/starting of the work: 15/01/2019.

Date of completion/Expected date of completion:-

Status of the work: Work in progress.

Cause/Reason for delay in sanction/completion of works: NIL.

Whether inspection carried out from Block/DCs office: Yes, at regular intervals from Block Office.

Name of executing agency: The work is executed by the School Managing Committee, Ambrose Memorial Secondary School, Khliehriat.

Whether signboard erected or not: No.

Date of submission of UC:

1st installment - Not yet submitted.

2nd installment -

Impact of the scheme: Extension of the School Building will help in creation of additional classrooms having a positive impact both on the students and community and in providing quality education. The School can accommodate more students from areas in and around Khliehriat.

Findings/Observations:

1. The inspection team found that the construction and extension of the Ambrose Memorial Secondary School Building is under progress.
2. It was found that the construction of school building is completed upto plinth level and erection of column whereas steel reinforcement for floor beams, earth filling and soling for flooring are under progress.
3. It was informed by the Principal that additional work has been executed i.e. CC drain, due to the site condition.
4. Its dimension:
 - a. Plinth area, L= 24m & B= 9.3m.
 - b. Plinth Height = 1.2m.
 - c. Column = 18 nos.
 - d. Beam size = 46cm * 30cm.
 - e. Nos of bars used for column:
 - i. 4 nos of 20mm dia.
 - ii. 4 nos of 16mm dia.
 - iii. 10mm diaties.
 - f. Nos of bars used in beams:
 - i. 4 nos of 20mm dia.
 - ii. 4 nos of 16mm dia.
 - iii. 10mm dia of stirrup.
 - g. CC drain, L = 44m, B = 1.4m & H = 1.5m.
 - h. Drain slab, L = 10.3m & B = 2.4m with Thickness = 150mm.
5. The Principal of the school has been advised to erect a plaque with full complete details as per Guidelines after completion of the scheme.

**CONSTRUCTION OF COMMUNITY HALL OF RANG WAHLAKHMAR WELFARE CLUB
DKHIAH EAST, EAST JAINTIA HILLS**



Date of Inspection: 31/05/2019

Team of Inspection Officers: Shri E.B. Lyngdoh, Deputy Director, Shri S. Sungoh, Research Officer, Shri R.G.M Nongtdu, Executive Engineer and Shri L.R.D. Jyrwa, Junior Engineer accompanied by Shri R. Daw, Assistant Engineer and Shri E. Rymbai, Gram Sevak.

Name of the Scheme: Construction of Community Hall of Rang Wah lakhmar Welfare Club Dkhiah East, East Jaintia Hills.

Name of the MP: Smt. Wansuk Syiem, MP (Rajya Sabha).

Year recommended/sanctioned: 2018-19.

Amount & Date of sanctioned by the DC: Rs. 25,00,000/- sanctioned on 01/05/2018.

Reason for delay of sanction, if any: NIL.

Amount & Date of release of fund:

1st installment - Rs. 12,50,000/- released from Block Office on 03/01/2019.

2nd installment - NIL.

Reason for delay in release of fund, if any: NIL.

Amount utilized: Rs. 12,50,000/-

Date of commencement/starting of the work: 10/01/2019.

Date of completion/Expected date of completion:- Work in progress

Status of the work: Work in progress.

Cause/Reason for delay in sanction/completion of works: NIL.

Whether inspection carried out from Block/DCs office: Yes, at regular intervals from Block Office.

Name of executing agency: The work is executed by the Local Committee, Rang Wahlakhmar Welfare Club, Dkhiah East.

Whether signboard erected or not: No.

Date of submission of UC:

1st installment - Not yet submitted.

2nd installment-


Impact of the scheme: Construction of Community Hall will benefit the local people for their various needs like public awareness programmes, Dorbar, award ceremonies, dramatic plays, concert performance, dancing competition etc.,.

Findings/Observations:

1. The inspection was carried out in presence of Secretary & Members of the Local Committee of Rang Wahlakhmar Welfare Club Dkhiah East.
2. The inspection team found that the construction of Community Hall of Rang Wahlakhmar Welfare Club Dkhiah East is under progress.
3. It was found that the quality of construction of the building was very good and the structure is very strong.
4. De-shuttering of beams and slabs is observed during the inspection.
5. It is seen that the structural works of the building is completed whereas the remaining works such as walling, flooring, plastering, fittings and fixing of doors and windows, painting and electrification are yet to be started.
6. Its dimension:
 - a. Plinth area, L= 26.4m & B= 14.2m.
 - b. Plinth Height = 60cm.
 - c. RCC wall, L = 26.4m & H = 3.2m with wall thickness = 20cm.
 - d. Column = 21 nos with size of 35cm * 28cm.
 - e. Floor Beams = 28 nos with size of 30cm * 40cm.
 - f. Nos of bars used for column:
 - i. 4 nos of 22mm dia.
 - ii. 2 nos of 16mm dia.
 - iii. 10mm dia of lateral ties.
 - g. Nos of bars used in beams:
 - i. 6 nos of 22mm dia.
 - ii. 2 nos of 16mm dia.
 - iii. 10mm dia of stirrup

- h. Slab, L = 14.6cm & B = 14.2cm with thickness = 150mm (12mm dia as main bars and 10mm dia as distribution bars).
7. The Secretary, Village Committee was advised to submit the Utilization Certificate along with Photograph to the Block office so as to avail the 2nd instalment.
 8. The Secretary, Village Committee has been advised to erect a plaque with full complete details as per Guidelines after the construction work is completed.

CONSTRUCTION OF HALL OF HOLY CROSS HIGHER SECONDARY SCHOOL, UMKIANG

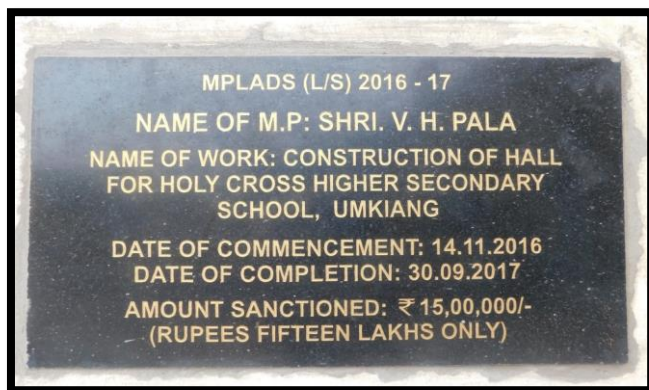

Date of Inspection: 31/05/2019

Team of Inspection Officers: Shri E.B. Lyngdoh, Deputy Director, Shri S. Sungoh, Research Officer, Shri R.G.M Nongtdu, Executive Engineer and Shri L.R.D. Jyrwa, Junior Engineer accompanied by Shri R. Daw, Assistant Engineer and Shri H. Lyngdoh, Gram Sevak.

Name of the Scheme: Construction of Hall of Holy Cross Higher Secondary School, Umkiang.

Name of the MP: Shri Vincent H. Pala, MP (Lok Sabha).

Year recommended/sanctioned: 2016-17.

Amount & Date of sanctioned by the DC: Rs. 15,00,000/- sanctioned on 02/05/2016.

Reason for delay of sanction, if any: NIL.

Amount & Date of release of fund:

1st installment - Rs. 7,50,000/- released from Block Office on 08/05/2017.

2nd installment - Rs. 7,50,000/- released from Block Office on 24/05/2019.

Reason for delay in release of fund, if any: Due to delay in submission of Photographs, Cash memos, Vouchers etc to the Block Office for demanding the 2nd instalment..

Amount utilized: Rs. 15,00,000/-

Date of commencement/starting of the work:14/11/2016.

Date of completion/Expected date of completion:30/09/2017.

Status of the work: Completed.

Cause/Reason for delay in sanction/completion of works: NIL.

Whether inspection carried out from Block/DCs office: Yes, at regular intervals from Block Office.

Name of executing agency: The work is executed by the School Managing Committee, Holy Cross Higher Secondary School, Umkiang.

Whether signboard erected or not: Yes.

Date of submission of UC:

1st installment - Submitted to the BDO, Khliehriat C&RD Block on the 08/11/2017.

2nd installment - Submitted to the BDO, Khliehriat C&RD Block on the 29/05/2019.

In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC: Yes.

Impact of the scheme: The construction of the Hall will enable the School to conduct various extra curricular activities and thereby encourage the students to take part and improve their knowledge and talent & also facilitate the holding of activities associated with the school like school functions, parent – teacher meetings, etc

Findings/Observations:

1. The inspection was carried out in presence of the Secretary, School Managing Committee, Umkiang.
2. The inspection team found that the Hall is already completed and being used by the School Managing Committee.
3. It was observed that the quality of construction is very good. The workmanship is of the best quality with usage of quality and durable materials.
4. Its dimension:
 - a. Plinth area of the hall, L= 33m & B= 13.2m.
 - b. Stage Podium, L = 13.2m & B = 6m.
 - c. Sliding Aluminium windows with 11 nos, H = 1.5m & L = 1.8m..
 - d. Doors with 4 nos, H = 2.4m & B = 1.2m.
 - e. Transom windows with 16 nos, L = 1.8m &H = 0.6m.
 - f. Chowkat with 4 nos = (6 x0.06x0.12) m.
