


Queries	Response
Click on the button to record the GPS location	25.33171727322042 92.33363734558225 1107.0 16.5
Profile & Demography	
State	Meghalaya
Select the District	East Jaintia Hills
Select the Block	Khliehriat
Select the Village	Rymbai
Details	
Name of the Scheme	Construction of Community Hall for Pampyrthat Rymbai Village
Name of the MP	Shri.V.H Pala
Year recommended	01-Jan-2017
Amount of sanction by the DC	500000
Date of sanction by the DC	04-May-2017
Delay in Sanction	No
Reason for delay in sanction	
Please mention the other reason:	
Released Funds	
Amount 1st Installment	250000
Date 1st Installment	20-Nov-2017
Amount 2nd Installment	200000
Date 2nd Installment	20-Aug-2018
Amount 3rd Installment	50000
Date 3rd Installment	31-Oct-2019
Delay in Fund Release	No

Reason for delay in release of fund	
Please mention the other reasons for Delay:	
Amounts	
Amount utilized	500000
Date of commencement/starting of the work	25-Jul-2017
Date of completion/Expected date of completion	30-Sep-2019
Status of the work	Completed
Delay in completion of work	No
Reason for delay in completion of works	
Please mention the other reasons for the delay in work	
Work	
Whether inspection carried out from Block/DCs office	Yes
Name of executing agency:	Local Committee of Pampyrthat
Whether signboard erected or not:	Yes
Date of submission of UC: 1st installment :-	04-Jun-2018
Date of submission of UC: 2nd installment :-	15-Nov-2019
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the scheme:	Availability of Community Hall benefitted the local people for arrangements for various activities and programmes.etc.

<p>Findings/Observation:</p>	<ol style="list-style-type: none"> 1. During inspection it was found that the construction of Community Hall is completed. 2. It is functioning and utilize by the people of Village 3. Dimensions: Plinth area(8x8)m 2 nos. W1 (36x53)inches 1 nos W2 (72x53)inches Steel Door (36x73)inches
<p>Quality of work:</p>	<p>Satisfactory</p>
<p>Please take a picture</p>	

Queries	Response
Click on the button to record the GPS location	25.35611820872873 92.37417072057724 1110.0 2.0
Profile & Demography	
State	Meghalaya
Select the District	East Jaintia Hills
Select the Block	Khliehriat
Select the Village	Khliehriat East
Details	
Name of the Scheme	Construction of Retaining wall at Khliehriat East near Old Govt. LP School
Name of the MP	Smt.W.Syiem
Year recommended	01-Jan-2019
Amount of sanction by the DC	800000
Date of sanction by the DC	23-Aug-2019
Delay in Sanction	No
Reason for delay in sanction	
Please mention the other reason:	
Released Funds	
Amount 1st Installment	400000
Date 1st Installment	30-Jan-2020
Amount 2nd Installment	
Date 2nd Installment	
Amount 3rd Installment	
Date 3rd Installment	
Delay in Fund Release	No

Reason for delay in release of fund	
Please mention the other reasons for Delay:	
Amounts	
Amount utilized	400000
Date of commencement/starting of the work	30-Jan-2020
Date of completion/Expected date of completion	31-Dec-2021
Status of the work	On-Going
Delay in completion of work	No
Reason for delay in completion of works	
Please mention the other reasons for the delay in work	
Work	
Whether inspection carried out from Block/DCs office	Yes
Name of executing agency:	Local Committee Khliehriat East
Whether signboard erected or not:	No
Date of submission of UC: 1st installment :-	26-Mar-2021
Date of submission of UC: 2nd installment :-	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	
Impact of the scheme:	To retain the soil erosion and also Demarcation of Boundary.


<p>Findings/Observation:</p>	<ol style="list-style-type: none"> 1. During inspection the Team found that construction of Retaining wall is under progress. 2. The Member of Local committee informed that they demand for release of the 2nd installment to complete the Scheme . 3 The Assistant Engineer has been advised to look into the matter with the Committee for release of the 2nd installment after the Committee has submitted the required documents such as UC, Photographs. etc. 4. The member also advised to erect a plaque with complete details of the scheme such as Name of MP, Name of Scheme, Date of Starting and Completion, Amount sanction. etc 5. Dimensions : Length: 70 meters Avg.Height: 3.00 meters Width:0.60meter
<p>Quality of work:</p>	<p>Good</p>

Please take a picture




Queries	Response
Click on the button to record the GPS location	25.32613144721836 92.37313337624073 1019.0 3.0
Profile & Demography	
State	Meghalaya
Select the District	East Jaintia Hills
Select the Block	Khliehriat
Select the Village	Byndihati
Details	
Name of the Scheme	Construction of Building for Shylla Development Society Byndihati
Name of the MP	Smt.W.Syiem
Year recommended	01-Jan-2019
Amount of sanction by the DC	4000000
Date of sanction by the DC	29-Nov-2019
Delay in Sanction	No
Reason for delay in sanction	
Please mention the other reason:	
Released Funds	
Amount 1st Installment	2000000
Date 1st Installment	17-Jun-2020
Amount 2nd Installment	
Date 2nd Installment	
Amount 3rd Installment	
Date 3rd Installment	
Delay in Fund Release	No

Reason for delay in release of fund	
Please mention the other reasons for Delay:	
Amounts	
Amount utilized	2000000
Date of commencement/starting of the work	17-Jun-2020
Date of completion/Expected date of completion	31-Dec-2021
Status of the work	On-Going
Delay in completion of work	No
Reason for delay in completion of works	
Please mention the other reasons for the delay in work	
Work	
Whether inspection carried out from Block/DCs office	Yes
Name of executing agency:	Local Committee of Byndihati
Whether signboard erected or not:	No
Date of submission of UC: 1st installment :-	21-Jun-2021
Date of submission of UC: 2nd installment :-	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	
Impact of the scheme:	Benefitted the Locality for arrangements of various programmes and activities.

<p>Findings/Observation:</p>	<ol style="list-style-type: none"> 1. During inspection it is found that the construction of building is under progress. 2. It is seen that Earthwork in foundation, Columns in Foundation upto Plinth Level, Erection of Columns are completed whereas steel reinforcements and Shuttering for Floor beams is under progress. 3. The member of the Local committee has been advised to speed up the work to complete the Scheme within stipulated timeline. and also to erect a signboard on completion of the Scheme as per MPLADS Guidelines. 4. Dimensions: Plinth area (20x14.3)m Columns size (14x18)inches Plinth beam (12x13)inches
<p>Quality of work:</p>	<p>Good</p>
<p>Please take a picture</p>	


Queries	Response
Click on the button to record the GPS location	25.36393031012267 92.36180439591408 1130.0 39.0
Profile & Demography	
State	Meghalaya
Select the District	East Jaintia Hills
Select the Block	Khliehriat
Select the Village	Dkhiah East
Details	
Name of the Scheme	Construction of Community Hall at Dong Lad Sutnga
Name of the MP	Shri.V.H Pala
Year recommended	01-Jan-2018
Amount of sanction by the DC	500000
Date of sanction by the DC	22-Oct-2018
Delay in Sanction	No
Reason for delay in sanction	
Please mention the other reason:	
Released Funds	
Amount 1st Installment	250000
Date 1st Installment	03-Jul-2019
Amount 2nd Installment	
Date 2nd Installment	
Amount 3rd Installment	
Date 3rd Installment	
Delay in Fund Release	No

Reason for delay in release of fund	
Please mention the other reasons for Delay:	
Amounts	
Amount utilized	250000
Date of commencement/starting of the work	06-Jun-2019
Date of completion/Expected date of completion	21-Dec-2020
Status of the work	Completed
Delay in completion of work	No
Reason for delay in completion of works	
Please mention the other reasons for the delay in work	
Work	
Whether inspection carried out from Block/DCs office	Yes
Name of executing agency:	Local Committee Dong Lad Sutnga
Whether signboard erected or not:	No
Date of submission of UC: 1st installment :-	01-May-2020
Date of submission of UC: 2nd installment :-	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the scheme:	Benefitted the Local people for their various needs like Public awareness, meeting, Award ceremonies, etc.

<p>Findings/Observation:</p>	<ol style="list-style-type: none"> 1. It is found that the construction of Community Hall is Completed. It is functional and Utilized by the Village. 2. It is constructed with good quality materials and workmanship. 3. It is seen that its constructed on first floor of a building. It comprises of 1 Hall, 1 store room,2 nos of Toilet. 4. The member of the Local committee has been advised to erect a plaque as per MPLADS Guidelines. 5. Dimensions:Plinth area (9.3x8)meters , Toilet area (63x71) inches 5 nos. of Aluminum casement windows (47x72)inches 1nos Door1 (47x76) inches 2 nos Door 2 (36x76)inches 2 nos Door3 (25x69) inches
<p>Quality of work:</p>	<p>Satisfactory</p>
<p>Please take a picture</p>	


Queries	Response
Click on the button to record the GPS location	25.43815084733069 92.29412404820323 1301.0 17.5
Profile & Demography	
State	Meghalaya
Select the District	East Jaintia Hills
Select the Block	Khliehriat
Select the Village	Tuber Kmaishnong
Details	
Name of the Scheme	Construction of School at Robinson Memorial UP School Tuber Kmaishnong
Name of the MP	Smt.W.Syiem
Year recommended	01-Jan-2019
Amount of sanction by the DC	2000000
Date of sanction by the DC	23-Aug-2019
Delay in Sanction	No
Reason for delay in sanction	
Please mention the other reason:	
Released Funds	
Amount 1st Installment	1000000
Date 1st Installment	17-Jun-2020
Amount 2nd Installment	
Date 2nd Installment	
Amount 3rd Installment	
Date 3rd Installment	
Delay in Fund Release	No

Reason for delay in release of fund	
Please mention the other reasons for Delay:	
Amounts	
Amount utilized	1000000
Date of commencement/starting of the work	17-Jun-2020
Date of completion/Expected date of completion	31-Dec-2021
Status of the work	On-Going
Delay in completion of work	No
Reason for delay in completion of works	
Please mention the other reasons for the delay in work	
Work	
Whether inspection carried out from Block/DCs office	Yes
Name of executing agency:	School Managing Committee
Whether signboard erected or not:	No
Date of submission of UC: 1st installment :-	30-Jul-2021
Date of submission of UC: 2nd installment :-	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	
Impact of the scheme:	To accommodate the students

<p>Findings/Observation:</p>	<ol style="list-style-type: none"> 1. On inspection it was found that the construction of School building is under progress. 2. The Construction of School Building was constructed on First floor of an existing building. 3. It is also seen that casting of slab concrete during of slab concrete is under progress. 4. The School managing committee has been advised to erect a signboard with its complete details mentioning the Name of MP, Name of Scheme, Date of Starting & Completion, Amount Sanction, etc. after the building is completed. 5. Dimensions: Plinth area (21.2x8)meters Column size (10x15)inches Beam size (8x12) inches
<p>Quality of work:</p>	<p>Good</p>
<p>Please take a picture</p>	


Queries	Response
Click on the button to record the GPS location	25.436008390970528 92.29360143654048 1322.0 16.0
Profile & Demography	
State	Meghalaya
Select the District	East Jaintia Hills
Select the Block	Khliehriat
Select the Village	Tuber Kmaishnong
Details	
Name of the Scheme	Construction/Extension of Community Hall at Sein Rajj Tuber EJHD
Name of the MP	Smt. W .Syiem
Year recommended	01-Jan-2018
Amount of sanction by the DC	500000
Date of sanction by the DC	01-May-2018
Delay in Sanction	No
Reason for delay in sanction	
Please mention the other reason:	
Released Funds	
Amount 1st Installment	250000
Date 1st Installment	31-Jan-2019
Amount 2nd Installment	200000
Date 2nd Installment	08-Jan-2020
Amount 3rd Installment	
Date 3rd Installment	
Delay in Fund Release	No

Reason for delay in release of fund	
Please mention the other reasons for Delay:	
Amounts	
Amount utilized	450000
Date of commencement/starting of the work	01-Feb-2019
Date of completion/Expected date of completion	31-May-2021
Status of the work	On-Going
Delay in completion of work	No
Reason for delay in completion of works	
Please mention the other reasons for the delay in work	
Work	
Whether inspection carried out from Block/DCs office	Yes
Name of executing agency:	Local Committee Sein Tuber Rajj
Whether signboard erected or not:	No
Date of submission of UC: 1st installment :-	10-Oct-2019
Date of submission of UC: 2nd installment :-	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	
Impact of the scheme:	Benefitted the people of Sein Rajj of Tuber for their various activities

<p>Findings/Observation:</p>	<ol style="list-style-type: none"> 1. During inspection it was found that the Construction/Extension of Hall is under 95% completed. 2. It is seen that Painting works is under progress. 3. It is constructed with usage of good quality materials. 4. It is also seen that it is constructed at Ground Floor comprises of 4 (four) rooms. 5. The Member of Committee has been advised to erect a Plaque on completion of the Scheme with complete details as per MPLADS Guidelines. 6. Dimensions: Plinth Area (20.35x4.5)meters 8 nos of windows (58x58) inches 4 nos of doors (36x76) inches
<p>Quality of work:</p>	<p>Good</p>
<p>Please take a picture</p>	

Queries	Response
Click on the button to record the GPS location	25.361126270145178 92.36338916234672 1170.0 47.0
Profile & Demography	
State	Meghalaya
Select the District	East Jaintia Hills
Select the Block	Khliehriat
Select the Village	Khliehriat West
Details	
Name of the Scheme	Construction of School Hall at Khliehriat Hr. Secondary School
Name of the MP	Shri.V.H Pala
Year recommended	01-Jan-2018
Amount of sanction by the DC	700000
Date of sanction by the DC	21-Jan-2019
Delay in Sanction	No
Reason for delay in sanction	
Please mention the other reason:	
Released Funds	
Amount 1st Installment	350000
Date 1st Installment	24-Sep-2019
Amount 2nd Installment	
Date 2nd Installment	
Amount 3rd Installment	
Date 3rd Installment	
Delay in Fund Release	No

Reason for delay in release of fund	
Please mention the other reasons for Delay:	
Amounts	
Amount utilized	350000
Date of commencement/starting of the work	24-Sep-2019
Date of completion/Expected date of completion	31-Dec-2021
Status of the work	On-Going
Delay in completion of work	No
Reason for delay in completion of works	
Please mention the other reasons for the delay in work	
Work	
Whether inspection carried out from Block/DCs office	Yes
Name of executing agency:	School Managing Committee
Whether signboard erected or not:	No
Date of submission of UC: 1st installment :-	01-May-2020
Date of submission of UC: 2nd installment :-	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	
Impact of the scheme:	Benefitted the School Students for arrangements of various programme, such as quiz ,dancing competition, meeting. etc.

<p>Findings/Observation:</p>	<ol style="list-style-type: none"> 1. It is found that construction of Hall is under progress. 2. It is seen that remaining works are electrification works, Painting works, fitting & fixing doors, glass panes, flooring topping, etc. 3. The School Principal has been advised to erect a plaque with complete details as per MPLADS Guidelines. 4. Dimensions: Plinth area (16.6x7.3)meters 8 nos. of steel windows (47x83)inches, 8 nos. ventilation (83x18)inches.
<p>Quality of work:</p>	<p>Good</p>
<p>Please take a picture</p>	

Queries	Response
Click on the button to record the GPS location	25.35796109586954 92.36208938062191 1126.0 7.0
Profile & Demography	
State	Meghalaya
Select the District	East Jaintia Hills
Select the Block	Khliehriat
Select the Village	Khliehriat West
Details	
Name of the Scheme	Construction of Approach Motorable Road at Catholic Cemetery Khliehriat West
Name of the MP	Smt.W.Syiem
Year recommended	01-Jan-2019
Amount of sanction by the DC	800000
Date of sanction by the DC	23-Aug-2019
Delay in Sanction	No
Reason for delay in sanction	
Please mention the other reason:	
Released Funds	
Amount 1st Installment	400000
Date 1st Installment	30-Jan-2020
Amount 2nd Installment	
Date 2nd Installment	
Amount 3rd Installment	
Date 3rd Installment	
Delay in Fund Release	No

Reason for delay in release of fund	
Please mention the other reasons for Delay:	
Amounts	
Amount utilized	400000
Date of commencement/starting of the work	30-Jan-2020
Date of completion/Expected date of completion	30-Jul-2021
Status of the work	On-Going
Delay in completion of work	No
Reason for delay in completion of works	
Please mention the other reasons for the delay in work	
Work	
Whether inspection carried out from Block/DCs office	Yes
Name of executing agency:	Local Committee , Khliehriat west
Whether signboard erected or not:	No
Date of submission of UC: 1st installment :-	17-Dec-2020
Date of submission of UC: 2nd installment :-	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	
Impact of the scheme:	Benefitted the Locality for connectivity to cemetery and connect to others neighboring localities.


<p>Findings/Observation:</p>	<p>1. During inspection the team found that the construction of Approach road is completed. It is seen that due to site condition additional work is executed i.e Slab culverts, Retaining wall.</p> <p>2. The member of committee has been advised to erect a plaque mentioning the Name of MP Name of Scheme, Amount sanction, Date of Starting and completion, etc.</p> <p>3. The member informed that UC and Photographs has been submitted to the Block Office for releasing of the 2nd installment.</p> <p>4. The Assistant Engineer has been advised to take matter with the member committee for release of the 2nd installment.</p> <p>5. Dimensions: Road Length : 90meters width: 3.90meters Slab Culvert: (3.90x1.4)meters</p>
<p>Quality of work:</p>	<p>Good</p>

Please take a picture




Queries	Response
Click on the button to record the GPS location	25.35827696789056 92.36716219224036 1123.0 9.0
Profile & Demography	
State	Meghalaya
Select the District	East Jaintia Hills
Select the Block	Khliehriat
Select the Village	Khliehriat West
Details	
Name of the Scheme	Construction of Auditorium at Khliehriat west
Name of the MP	Smt.W.Syiem
Year recommended	01-Jan-2019
Amount of sanction by the DC	2000000
Date of sanction by the DC	23-Aug-2019
Delay in Sanction	No
Reason for delay in sanction	
Please mention the other reason:	
Released Funds	
Amount 1st Installment	1000000
Date 1st Installment	17-Jun-2020
Amount 2nd Installment	
Date 2nd Installment	
Amount 3rd Installment	
Date 3rd Installment	
Delay in Fund Release	No

Reason for delay in release of fund	
Please mention the other reasons for Delay:	
Amounts	
Amount utilized	1000000
Date of commencement/starting of the work	17-Jun-2020
Date of completion/Expected date of completion	31-Dec-2021
Status of the work	On-Going
Delay in completion of work	No
Reason for delay in completion of works	
Please mention the other reasons for the delay in work	
Work	
Whether inspection carried out from Block/DCs office	Yes
Name of executing agency:	Local Committee Khliehriat west
Whether signboard erected or not:	No
Date of submission of UC: 1st installment :-	30-Jun-2021
Date of submission of UC: 2nd installment :-	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	
Impact of the scheme:	Benefitted the Locality for arrangements of various activities such as competition, awareness programme, meetings,etc.

<p>Findings/Observation:</p>	<ol style="list-style-type: none"> 1. It is found that the construction of Auditorium is under progress. 2. It is also found that casting of slab concrete, curing of slab is under progress. 3. The member of committee has been advised to speed up the work to complete the Scheme within stipulated timeline. 4. And also advised the Member to erect a plaque as per MPLADS Guidelines. 5. Dimensions: Plinth area(23.5x18.2)m Columns size (12x18)inches Beam size (12x14)inches
<p>Quality of work:</p>	<p>Good</p>
<p>Please take a picture</p>	

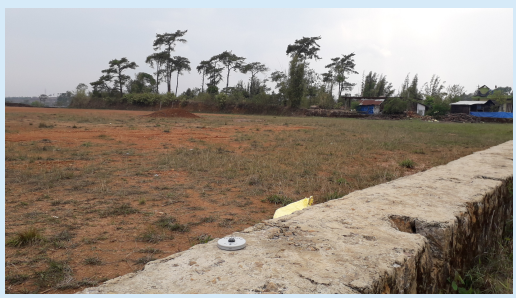
Queries	Response
Click on the button to record the GPS location	25.33828055486083 92.32559306547046 1075.0 8.0
Profile & Demography	
State	Meghalaya
Select the District	East Jaintia Hills
Select the Block	Khliehriat
Select the Village	Rymbai
Details	
Name of the Scheme	Construction of Playground for Shken Shynriah,Rymbai
Name of the MP	Shri.V.H Pala
Year recommended	01-Jan-2017
Amount of sanction by the DC	500000
Date of sanction by the DC	04-May-2017
Delay in Sanction	No
Reason for delay in sanction	
Please mention the other reason:	
Released Funds	
Amount 1st Installment	250000
Date 1st Installment	20-Nov-2017
Amount 2nd Installment	250000
Date 2nd Installment	24-Aug-2020
Amount 3rd Installment	
Date 3rd Installment	
Delay in Fund Release	No

Reason for delay in release of fund	
Please mention the other reasons for Delay:	
Amounts	
Amount utilized	500000
Date of commencement/starting of the work	20-Nov-2017
Date of completion/Expected date of completion	20-Jun-2019
Status of the work	Completed
Delay in completion of work	No
Reason for delay in completion of works	
Please mention the other reasons for the delay in work	
Work	
Whether inspection carried out from Block/DCs office	Yes
Name of executing agency:	Local Committee of Shken Shynriah
Whether signboard erected or not:	Yes
Date of submission of UC: 1st installment :-	15-Jul-2019
Date of submission of UC: 2nd installment :-	03-Nov-2020
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the scheme:	Availability of Playground will benefitted the locality for arrangements of various activities and programmes.

<p>Findings/Observation:</p>	<ol style="list-style-type: none"> 1. During inspection the Team found that the construction of Playground is completed. 2. It was informed by the Member committee that additional work i .e Seating Gallery is executed for seating arrangements. 3. Dimensions: Ground (22.60x20)m Gallery (20x0.45)m
<p>Quality of work:</p>	<p>Good</p>
<p>Please take a picture</p>	

Queries	Response
Click on the button to record the GPS location	25.32992283347994 92.32338049449027 1099.0 10.0
Profile & Demography	
State	Meghalaya
Select the District	East Jaintia Hills
Select the Block	Khliehriat
Select the Village	Rymbai
Details	
Name of the Scheme	Construction of Playground for Wahshnong Rymbai,Rymbai Village
Name of the MP	Shri.V.H Pala
Year recommended	01-Jan-2017
Amount of sanction by the DC	500000
Date of sanction by the DC	04-May-2017
Delay in Sanction	No
Reason for delay in sanction	
Please mention the other reason:	
Released Funds	
Amount 1st Installment	250000
Date 1st Installment	07-May-2018
Amount 2nd Installment	200000
Date 2nd Installment	04-Oct-2018
Amount 3rd Installment	50000
Date 3rd Installment	19-Aug-2019
Delay in Fund Release	No

Reason for delay in release of fund	
Please mention the other reasons for Delay:	
Amounts	
Amount utilized	500000
Date of commencement/starting of the work	07-May-2018
Date of completion/Expected date of completion	14-Nov-2018
Status of the work	Completed
Delay in completion of work	No
Reason for delay in completion of works	
Please mention the other reasons for the delay in work	
Work	
Whether inspection carried out from Block/DCs office	Yes
Name of executing agency:	Local Committee of Wahshnong Rymbai
Whether signboard erected or not:	Yes
Date of submission of UC: 1st installment :-	31-Aug-2018
Date of submission of UC: 2nd installment :-	28-Oct-2019
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the scheme:	Availability of the Playground benefitted for Local People and School Students for various activities and programmes.etc

<p>Findings/Observation:</p>	<ol style="list-style-type: none"> 1. It is seen that the construction of Playground is completed. 2. It is also seen that the works executed are Earthwork cutting, filling, soil compaction etc. 3. The member of Committee informed that additional work is executed i.e Retaining wall to retain the soil. 4. Dimensions: Earthwork:length 75m , Breadth 71m Retaining wall :Length: 75m Height:1.5m width:0.90m
<p>Quality of work:</p>	<p>Good</p>
<p>Please take a picture</p>	

Queries	Response
Click on the button to record the GPS location	25.195363448001444 92.25647061131895 552.0 16.5
Profile & Demography	
State	Meghalaya
Select the District	East Jaintia Hills
Select the Block	Khliehriat
Select the Village	Lad Lakadong
Details	
Name of the Scheme	Construction of Additional Classroom at St.Eugene Lad Lakadong RCLP School Lakadong
Name of the MP	Shri.V.H Pala
Year recommended	01-Jan-2018
Amount of sanction by the DC	1000000
Date of sanction by the DC	04-Oct-2018
Delay in Sanction	No
Reason for delay in sanction	
Please mention the other reason:	
Released Funds	
Amount 1st Installment	500000
Date 1st Installment	03-Jul-2019
Amount 2nd Installment	
Date 2nd Installment	
Amount 3rd Installment	
Date 3rd Installment	
Delay in Fund Release	No

Reason for delay in release of fund	
Please mention the other reasons for Delay:	
Amounts	
Amount utilized	500000
Date of commencement/starting of the work	11-Jan-2019
Date of completion/Expected date of completion	02-Feb-2020
Status of the work	Completed
Delay in completion of work	No
Reason for delay in completion of works	
Please mention the other reasons for the delay in work	
Work	
Whether inspection carried out from Block/DCs office	Yes
Name of executing agency:	School Managing Committee
Whether signboard erected or not:	Yes
Date of submission of UC: 1st installment :-	05-Feb-2020
Date of submission of UC: 2nd installment :-	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the scheme:	Helps in accommodation of additional classrooms and also benefitted the students of the Villages and near by Villages

<p>Findings/Observation:</p>	<ol style="list-style-type: none"> 1. It is seen that the construction of Additional classrooms is completed. 2. It is functioning and Utilized and also constructed with usage of good quality materials and workmanship. 3. It comprises of 1 Hall and divide into 4 Classrooms. 4. Dimensions. Plinth area (22x5.5)m 10nos. windows (35x47)inches 4nos. Steel Doors (35x72)inches
<p>Quality of work:</p>	<p>Good</p>
<p>Please take a picture</p>	
