

## CONSTRUCTION OF LATYRKE FACILITATION CENTRE AT LATYRKE VILLAGE



**Date of Inspection:** 21/06/2019

**Team of Inspection Officers:** Shri E.B. Lyngdoh, Deputy Director, Shri S. Sungoh, Research Officer, Shri R.G.M. Nongtdu, Executive Engineer and Shri L.R.D. Jyrwa, Junior Engineer accompanied by Shri P. Dhar, Assistant Engineer & Shri C.H. Sutnga, Gram Sevak.

**Name of the Scheme:** Construction of Latyrke Facilitation Centre at Latyrke Village.

**Name of the MP:** Smt. Wansuk Syiem, MP (Rajya Sabha).

**Year recommended/sanctioned:** 2017-18.

**Amount & Date of sanction by the DC:** Rs. 50,00,000/- sanctioned on 13/06/2017

**Reason for delay of sanction, if any:** Beneficiary did not turn up in time.

**Amount & Date of release of fund:**

1 <sup>st</sup> installment -	Rs. 15,00,000/-	released from Block Office on 22/12/2017.
2 <sup>nd</sup> installment	-	Rs. 10,00,000/- released from Block Office on 25/05/2018.
3 <sup>rd</sup> installment -	Rs. 25,00,000/-	released from Block Office on 25/01/2019.

**Reason for delay in release of fund, if any:** NIL.

**Amount utilized:** Rs. 50,00,000/-

**Date of commencement/starting of the work:** 28/06/2017.

**Date of completion/Expected date of completion:** 31<sup>st</sup> March, 2019

**Status of the work:** Work in progress.

**Cause/Reason for delay in sanction/completion of works:** Due to less labourers.

**Whether inspection carried out from Block/DCs office:** Yes, at regular intervals from Block Office.

**Name of executing agency:** The work is executed by the Village Committee.

**Whether signboard erected or not:** Yes.

**Date of submission of UC:**


1 <sup>st</sup> installment -	Submitted to the BDO Saipung C&RD Block on 22/12/2017.
2 <sup>nd</sup> installment-	Submitted to the BDO Saipung C&RD Block on 25/01/2019.
3 <sup>rd</sup> installment-	Not yet submitted.

**Impact of the scheme:** The construction of Auditorium will enable the Local Committee of the village to conduct various Social & Cultural activities and it can also be used for conducting various functions and programmes such as awareness programmes, etc.

**Findings/Observations:**

1. The inspection team found that the construction of Latyrke Facilitation Centre is under progress. It comprises of 2(two) storeys and it was constructed with usage of good quality materials. The quality of construction of the building was very good and the structure is very strong.
2. It was observed that the structural work is completed. It was observed that the ongoing works on the First Floor are brick walling, wall plastering, ceiling plastering, fitting and fixing of windows, chowkhat and glass panes whereas for the Ground Floor work is yet to be done. It was also observed that the staircase is being casted.
3. Its dimensions:
  - a. Plinth area = (16.20\*10) m.
  - b. Plinth Height = 60cm.
  - c. Staircase, Riser = 15cm & Thread = 30cm.
  - d. 8 numbers window1 = (1.80\*1.70) m.
  - e. 2 numbers window2 = (2.20\*2.00) m.
  - f. 29 numbers of columns = (30\*35) cm.
    - i. Number of Bars = 4 numbers f 20mm dia and 4 numbers of 16mm dia.
    - ii. Lateral Ties = 8mm dia.
  - g. Slab reinforcement – 12 mm dia for main bars & 10mm dia for Distribution bars.
4. The Assistant Engineer has been advised to inform the Village Committee to complete the scheme at the earliest and also to erect a permanent plaque with full complete details of the scheme indicating the Name of MP, Year, Name of Scheme, Amount sanctioned, Date of Completion, etc.,as per guidelines after completion of the scheme.

**CONSTRUCTION OF GALLERY AT FOOTBALL PLAYGROUND MOOSHUT PYRDUNG(PHET NIW) JALAPHET, BRI SUTNGA**

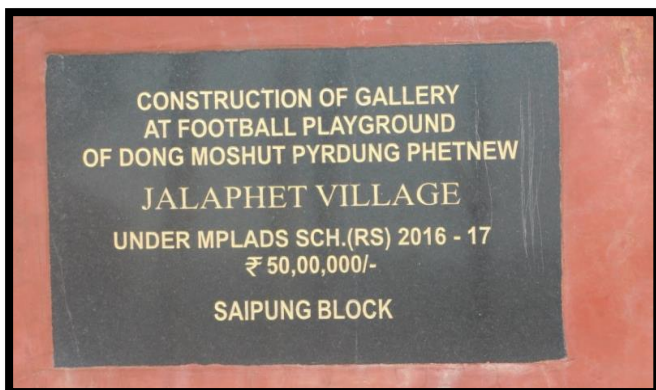

**Date of Inspection:**21/06/2019

**Team of Inspection Officers:** Shri E.B. Lyngdoh, Deputy Director, Shri S. Sungoh, Research Officer, Shri R.G.M. Nongtdu, Executive Engineer and Shri L.R.D. Jyrwa, Junior Engineer accompanied by Shri P. Dhar, Assistant Engineer and Shri G. Dkhar, Gram Sevak.

**Name of the Scheme:** Construction of Gallery at Football Playground Mooshut Pyrdung (Phet niw) Jalaphet, Bri Sutnga.

**Name of the MP:** Smt. Wansuk Syiem, MP (Rajya Sabha).

**Year recommended/sanctioned:** 2018-19.

**Amount & Date of sanction by the DC:** Rs. 50,00,000/- sanctioned on 01/05/2018

**Reason for delay of sanction, if any:** NIL.

**Amount & Date of release of fund:**

1<sup>st</sup> installment - Rs. 25,00,000/- released from Block Office on 07/01/2019.

2<sup>nd</sup> installment - NIL.

**Reason for delay in release of fund, if any:** NIL.**Amount utilized:** Rs. 25,00,000/-**Date of commencement/starting of the work:** 12/01/2019.**Date of completion/Expected date of completion:** 31<sup>st</sup> March, 2020**Status of the work:** Work is under progress (60%)**Cause/Reason for delay in sanction/completion of works:** NIL.**Whether inspection carried out from Block/DCs office:** Yes, at regular intervals from Block Office.**Name of executing agency:** The work is executed by the Local Committee of the Village.**Whether signboard erected or not:** Yes.**Date of submission of UC:**

1<sup>st</sup> installment - Submitted to the BDO Saipung C&RD Block on 07-01-2019

2<sup>nd</sup> installment -

**Impact of the scheme:** The construction of the Gallery will provide sitting space for 200-300 spectators of this Village. Moreover the completion of the additional works i.e. referee rooms, slab for VIP Gallery, office rooms, breast wall, etc, will be an added infrastructure which completes the set up required for a football playground.

**Findings/Observations:**

1. The inspection was carried out in the presence of Secretary & Members of the Local Committee of Mooshut Pyrdung (Phet niw) Jalaphet.
2. The inspection team found that the construction of two Galleries at football playground is under progress.
3. It was informed by the Secretary & Members of the Local Committee that besides construction of the Gallery, there were other works i.e., approach steps, repairing and renovation of player changing rooms, referee rooms, slab for VIP Gallery, office rooms, breast wall, etc, which were utilised from the same funds.
4. The Members of the Village Committee have been advised to make a correction on the plaque with full details of the scheme indicating the Name of MP, Year, Name of Scheme, Amount sanctioned, Date of completion, etc., as per guidelines after completion of the scheme.
5. Its dimensions:
  - a. Spectator Gallery:
    - i. Gallery I – Length = 38m, Riser = 45cm & Thread = 110cm.

- ii. Gallery II – Length = 43.80m, Riser = 45cm & Thread = 110cm.
- b. Approach Steps (both sides):
  - i. Breadth = 3.60m
  - ii. Riser = 15cm
  - iii. Thread = 30cm
- c. Breast wall (both sides):
  - i. Length = 9.00m
  - ii. Height = 90cm
  - iii. Thickness = 30cm

**CONSTRUCTION OF FENCING FOR MADAN LUMSHRAM MADAN KROHMUIT JALAPHET,  
BRI SUTNGA**



**Date of Inspection:** 21/06/2019

**Team of Inspection Officers:** Shri E.B. Lyngdoh, Deputy Director, Shri S. Sungoh, Research Officer, Shri R.G.M. Nongtdu, Executive Engineer and Shri L.R.D. Jyrwa, Junior Engineer accompanied by Shri P. Dhar, Assistant Engineer and Shri G. Dkhar, Gram Sevak.

**Name of the Scheme:** Construction of Fencing for Madan Lumshram Madan Krohmuit Jalaphet, Bri Sutnga.

**Name of the MP:** Shri V.H. Pala, MP (Lok Sabha).

**Year recommended/sanctioned:** 2018-19.

**Amount & Date of sanction by the DC:** Rs. 10,00,000/- sanctioned on 22/10/2018.

**Reason for delay of sanction, if any:** NIL.

**Amount & Date of release of fund:**

1<sup>st</sup> installment - Rs. 5,00,000/- released from Block Office on 28/01/2019.

2<sup>nd</sup> installment - NIL.

**Reason for delay in release of fund, if any:** NIL.

**Amount utilized:** Rs. 5,00,000/-

**Date of commencement/starting of the work:** 31/01/2019

**Date of completion/Expected date of completion:** By 31<sup>st</sup> March, 2020.

**Status of the work:** Work is under progress (55%)

**Cause/Reason for delay in sanction/completion of works:** NIL.

**Whether inspection carried out from Block/DCs office:** Yes, at regular intervals from Block Office.

**Name of executing agency:** The work is executed by the Local Committee of Jalaphet, Bri Sutnga.

**Whether signboard erected or not:-** Will be done, on completion.

**Date of submission of UC:**

1<sup>st</sup> installment - Submitted to the BDO Saipung C&RD Block on 28/01/2019.

2<sup>nd</sup> installment - -

**Impact of the scheme:** To prevent encroachment and to demarcate the boundary of the Playground.

**Findings/Observations:**

1. It was found that the construction of fencing is under progress and it was completed upto a length of 111.40 meters and the remaining length of 276.20 meters is yet to be done.
2. It was observed that the quality of construction is very good.
3. The Assistant Engineer was advised to inform the Secretary, Local Committee to submit the Utilization Certificate and Photographs to the Block office at the earliest so that demand for the 2<sup>nd</sup> Installment can be made.
4. The Assistant Engineer was also advised to inform the Secretary, Local Committee to speed up the work and to erect a plaque with complete details as per Guidelines after completion of the scheme.
5. Its dimensions:
  - a. Column: (20\*20) cm.
  - b. Number of bars: 4 numbers of 12mm dia.
  - c. Lateral ties: 5mm dia.
  - d. Beam: (15\*15) cm.
  - e. Number of bars used: 3 number of 10mm dia.
  - f. Stirrup: 5mm dia.

**CONSTRUCTION OF VOCATIONAL TRAINING CENTRE AT PALA PRESBYTERIAN, PALA VILLAGE**



**Date of Inspection:**21/06/2019

**Team of Inspection Officers:** Shri E.B. Lyngdoh, Deputy Director, Shri S. Sungoh, Research Officer, Shri R.G.M. Nongtdu, Executive Engineer and Shri L.R.D. Jyrwa, Junior Engineer accompanied by Shri P. Dhar, Assistant Engineer and Shri J. Paslein, Gram Sevak.

**Name of the Scheme:** Construction of Vocational Training Centre at Pala Presbyterian, Pala Village.

**Name of the MP:** Shri V.H. Pala, MP (Lok Sabha).

**Year recommended/sanctioned:** 2017-18.

**Amount & Date of sanction by the DC:** Rs. 10,00,000/-.

**Reason for delay of sanction, if any:** NIL.

**Amount & Date of release of fund:**

1<sup>st</sup> installment - Rs. 5,00,000/- released from Block Office on 26/06/2019.

2<sup>nd</sup> installment - NIL.

**Reason for delay in release of fund, if any:** Due to return of cheque twice since no funds are available in the account of the Block.

**Amount utilized:** Nil

**Date of commencement/starting of the work:-** 29-06-2019

**Date of completion/Expected date of completion:** 31<sup>st</sup> March, 2020

**Status of the work:** Work in progress.

**Cause/Reason for delay in sanction/completion of works:** NIL.

**Whether inspection carried out from Block/DCs office:** - Yes, at regular intervals from Block Office.

**Name of executing agency:** The work is to be executed by the Village Committee.



**Whether signboard erected or not:** No.

**Date of submission of UC:**

1<sup>st</sup> installment - Submitted to the BDO Saipung C&RD Block on 26/06/2019.  
2<sup>nd</sup> installment - -

**Impact of the scheme:** The availability of this Vocational Training Centre will benefit the village people for taking up vocational works like basket weaving, tailoring, knitting, etc to supplement their incomes.

**Findings/Observations:**

1. It was observed that a plot of land is available at site for construction of the scheme. It was informed by the Secretary, Village Committee that earth work cutting has been done for levelling from their own funds.
2. The Secretary informed that earlier two cheques were issued from the BDOs office which was returned by the Bank stating that there are no funds available on the account of the Block Office. It was only recently that the 1<sup>st</sup> installment was issued to the beneficiary.
3. It was observed that since the 1<sup>st</sup> installment was only recently released, the Assistant Engineer was advised to take up the matter of early completion of the scheme with the Secretary of the Village Committee so that there will be no further delays in the implementation of the scheme.

**CONSTRUCTION OF WAHLUBER OUTDOOR GAMES & RECREATION CLUB AT LATYRKE,  
EAST JAINTIA**



**Date of Inspection:**21/06/2019

**Team of Inspection Officers:** Shri E.B. Lyngdoh, Deputy Director, Shri S. Sungoh, Research Officer, Shri R.G.M. Nongtdu, Executive Engineer and Shri L.R.D. Jyrwa, Junior Engineer accompanied by Shri P. Dhar, Assistant Engineer and Shri G. Sutnga, Gram Sevak

**Name of the Scheme:** Construction of Wahlubur Outdoor Games & Recreation Club at Latyrke, East Jaintia.

**Name of the MP:** Smt. Wansuk Syiem, MP (Rajya Sabha).

**Year recommended/sanctioned:** 2015-16.

**Amount & Date of sanction by the DC:** Rs. 20,00,000/-.

**Reason for delay of sanction, if any:** NIL.

**Amount & Date of release of fund:**

1<sup>st</sup> installment - Rs. 10,00,000/- released from Block Office on 03/08/2016.

2<sup>nd</sup> installment - Rs. 10,00,000/- released from Block Office on 30/11/2016.

**Reason for delay in release of fund, if any:** NIL.

**Amount utilized:** Rs. 20,00,000/-.

**Date of commencement/starting of the work:** 04/12/2016.

**Date of completion/Expected date of completion:** 31/03/2019.

**Status of the work:** Completed

**Cause/Reason for delay in sanction/completion of works:** NIL.

**Whether inspection carried out from Block/DCs office:** Yes, at regular intervals from Block Office.

**Name of executing agency:** The work is executed by the Village Committee.

**Whether signboard erected or not:** No

**Date of submission of UC:**

1<sup>st</sup> installment - Submitted to the BDO, Saipung C&RD Block on the 30/11/2016.

2<sup>nd</sup> installment - Not yet submitted

**Impact of the scheme:** Construction of the outdoor games and recreation club will benefit the Local people for their various needs like public awareness programmes, Sports and any other activities, for which, as of now the playground has been used for Inter Block Tournament organized by the District Sports Officers and other tournaments.

**Findings/Observations:**

1. During inspection the team found that the construction of Wahluber Outdoor Games & Recreation Club is completed.
2. It was informed by the Secretary, Village Committee that earth cutting and levelling for the playground was executed by JCB machine. It is also seen that the structural work and roofing with Dyna roof for the Recreational Club are completed, whereas, works on the Ground Floor which consist of the players changing rooms, referee changing rooms and the First Floor i.e., the VIP sitting gallery are yet to be done.
3. It was found that the quality of structural work of the building was very good with usage of quality materials.
4. It was informed by the Secretary that since all the funds have been spent for preparation of the playground and on the infrastructure they could not complete the remaining works on the Recreation Club. The Secretary also informed that they will spend from their own village funds in order to complete the remaining works.
5. The Secretary, Local Committee has been advised that since the work is already completed out of funds sanctioned under MPLADS, so signboard/plaque should be in place.
6. Its dimensions:
  - a. Playground: Length = 120m & Breadth = 80m.
  - b. Recreation club: Plinth area (15.2\*5.5) m.
    - i. 10 numbers columns: (30\*35) cm.
    - ii. 13 numbers Floor Beams: (40\*25) cm.
  - c. Staircase (both sides)
    - i. Stair Width = 1.50 m.
    - ii. Risers = 15cm.
    - iii. Thread = 30cm.
  - d. Slab thickness = 120mm.
