

## Construction of Ieng Swer Memorial School Dkhiah (MPLADS)

**Date of inspection** - 20th May, 2009

**Team of inspection officers** – Shri P.L. Nongbri, Assistant Director, Shri. E.B. Lyngdoh, Research Officer and Shri. S . Sungoh, Research Assistant.

**Name of the Scheme** – Construction of Ieng Swer Memorial School Dkhiah, Jaintia Hills.

**Name of the MP** –Shri P.R. Kyndiah, Ex. MP (LS)

**Year recommended/sanctioned** – 2006-07

**Amount sanctioned** - Rs. 10,00,000/-

**Date of sanctioned** - 10<sup>th</sup> March 2008.

**Date of released of fund** -

- (i) 1<sup>st</sup> installment of Rs 5,00,000/-was drawn on April, 2008
- (ii) 2<sup>nd</sup> installment of Rs.5,00,000/-was drawn on April, 2009



Front side of the building

**Date of commencement** – The work had already started before getting the sanction with the available fund of the school


**Amount utilized/Expenditure-** Rs10,00,000/-

**Submission of Utilization Certificate-** Utilization Certificate of the 1<sup>st</sup> installment only has been submitted to the Block Development Officer, Khliehriat, Jaintia Hills.

**Expected date of completion-** July 2009.

**Quality of work** – Excellent

**Whether inspection from BDO** – Yes, at regular intervals.

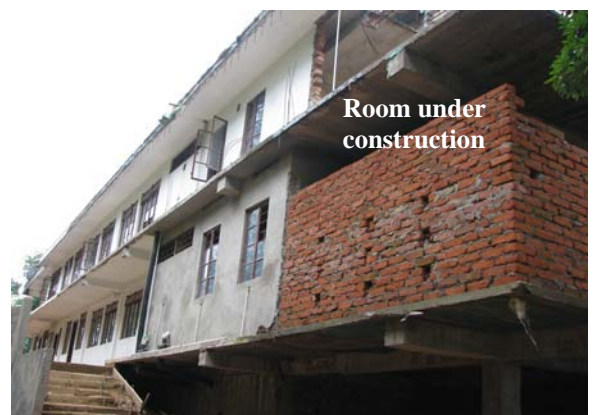

Room under construction

Back side of the building

**Name of implementing/executing agency** – The work is executed/implemented by the Managing Committee of the school.

## Observations:-

- (i) It was observed that the estimate of the school building submitted was Rs. 11,80,700/-and hence the Managing Committee will have to bear the excess amount.
- (ii) The Secretary of Managing Committee had informed that the construction of the school building was constructed in memory of his grandfather 'Jeng Swer' who was also the Dolloi of the area in the past.
- (iii) It was found that the building is well maintained and all classrooms including benches and desks are in good condition.
- (iv) It was found that a portion of the construction work viz a room in the 1<sup>st</sup> Floor, toilet, washroom, corridor etc is yet to be completed.
- (v) The Secretary of the Managing Committee has assured that a signboard depicting the name of the schemes, name of MP Etc. will be erected after the construction is completed.
- (vi) It was found that the quality of construction of the school Building was very good and it appears that the fund was rightly used for the purpose.

